51133

de maximis, inc.

450 Montbrook Lane
Knoxville, TN 37919
865-691-5052 phone
865-691-6485 fax

CD Scanned
PM Copy

May 27, 2022

Mr. Tim Hornosky
SC Department of Health and Environmental Control
Bureau of Land and Waste Management
2600 Bull Street
Columbia, South Carolina 29201

Subject: 2021 2nd Semi-Annual Monitoring and Annual Report Summary
Former Federal Pacific Electric Company Facility **(Site ID 00346)**
Edgefield, South Carolina

Dear Mr. Hornosky:

On behalf of Federal Pacific Electric Company (FPE), we are submitting the 2021 2nd Semi-Annual Monitoring and Annual Report Summary, one hardcopy and an electronic copy. The submitted document generally follows the outline discussed and provided with our 8OCT21 submittal and provides a summary and interpretation of the groundwater monitoring, surface water monitoring and recovery/treatment system data collected at the facility during 2021. In addition, this report provides an evaluation of the effectiveness of ongoing groundwater recovery/treatment, the results of ongoing remedial investigations, system and facility maintenance activities, and recommendations.

If you have questions or comments, please feel welcome to contact me at 865-691-5052 or Jeff Beckner at 706-828-4421.

Best regards,

de maximis, inc.

Bennie L. Underwood

cc: J. Beckner, Arcadis

51133

CD Scanned
PM Copy

ARCADIS

FORMER FEDERAL PACIFIC ELECTRIC CO. SITE

2021 2nd SEMIANNUAL MONITORING AND ANNUAL SUMMARY REPORT

Site ID – 00346, Edgefield, SC

May 2022

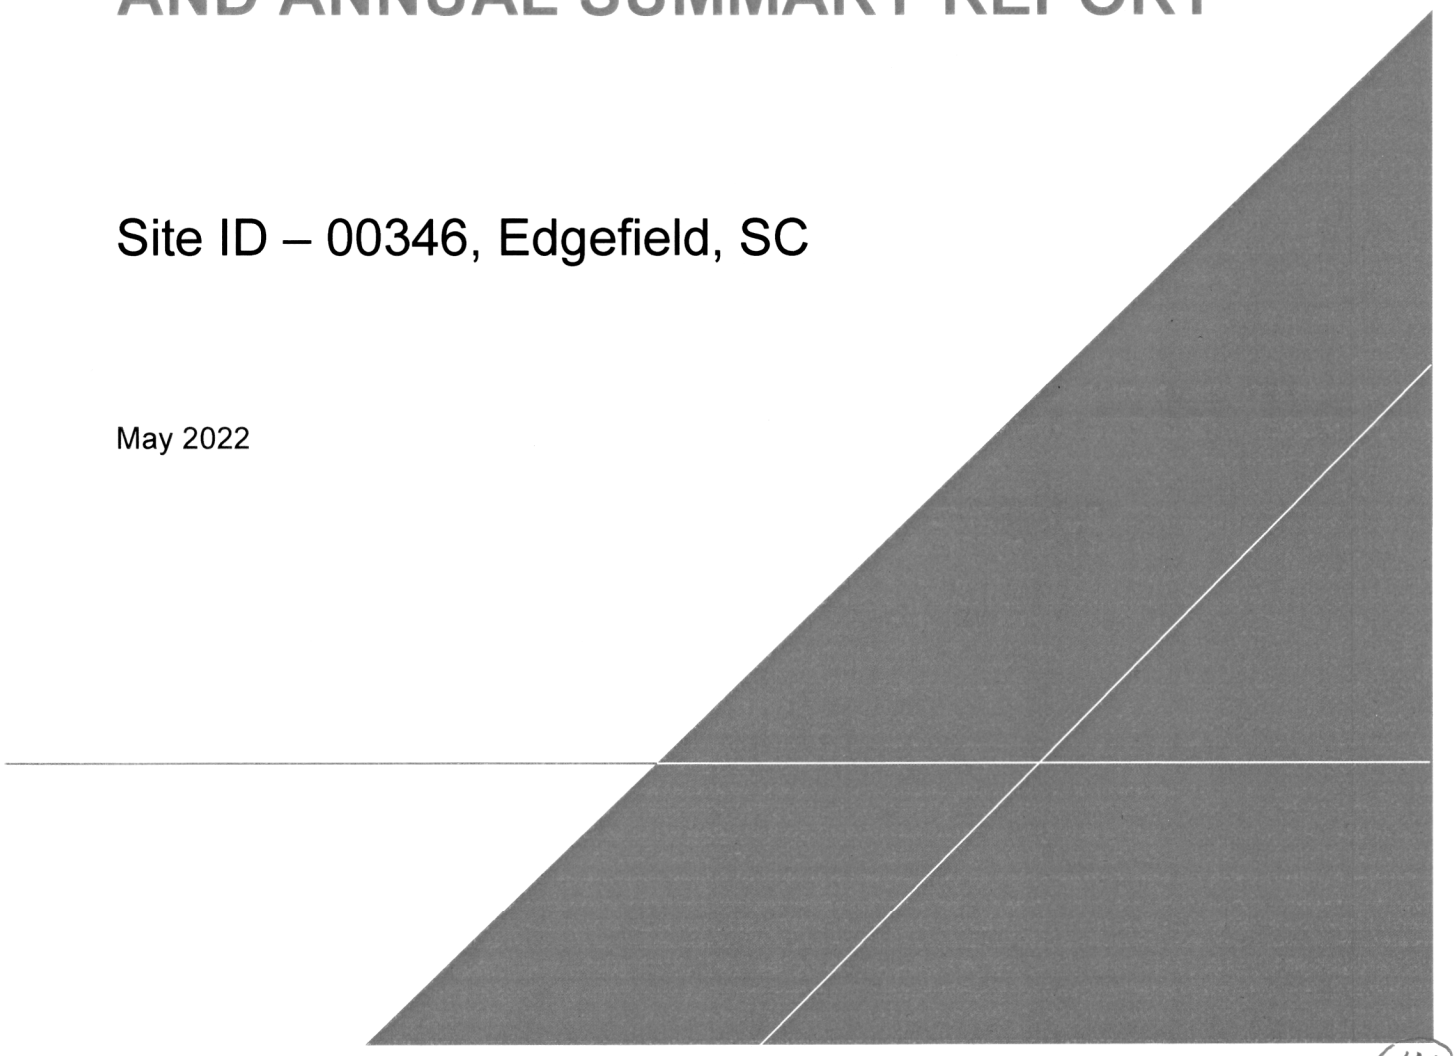

106

2021 2nd SEMIANNUAL MONITORING AND ANNUAL SUMMARY REPORT

Former Federal Pacific Electric Co. Site
Edgefield, South Carolina

Bennie L. Underwood, P.E.
Trustee, FPE Liquidation Trust



Jeff S. Beckner, P.G. #865
Project Manager
ARCADIS U.S.

Prepared for:
Federal Pacific Electric

Prepared by:
Arcadis U.S., Inc.
1450 Greene Street
Suite 220
Augusta
Georgia 30901-5201
Tel 706 828 4421
Fax 706 828 4722

Our Ref.:
30067293

Date:
May 2022

CONTENTS

FIGURES

TABLES

APPENDICES

EXECUTIVE SUMMARY

This report provides a summary of the status of FPE's ongoing groundwater recovery and compliance monitoring during the period from July to December 2021, a summary of 2021 remedial action effectiveness, and anticipated 2022 activities. The groundwater, surface water, and treatment/recovery system data collected during 2021 indicate the following:

- The saprolite and partially weathered rock (PWR) remain dewatered in most of the on-site area in response to continued groundwater extraction. The off-site recovery system has produced depressed groundwater levels in the vicinity of Rabbit Trail Road.
- The operating groundwater extraction systems continue to influence chlorinated hydrocarbon (CHC) concentration trends. In general, fluctuating, but overall decreasing dissolved CHC concentration trends are occurring both on-site and downgradient of the former FPE facility. The fluctuations in the concentration trends are seasonal and reflect variability in groundwater level and changes in transport pathways as a function of increasing capture zones and changes in pumping operations.
- Reported CHC concentrations in all sampled Odell Reservoir surface water stations were below the laboratory detection limits during both 2021 monitoring events. CHC concentrations at all reservoir stations have been below South Carolina Surface Water Quality Standards (SCSWQS) since March 2010 and are attributed to the startup and operation of the active off-site groundwater recovery system.
- In 2021, approximately 8.1 million gallons (Mgal) of groundwater and 184 lbs of CHC mass were extracted by the on-site recovery system (EW-1R, EW-2, EW-3, EW-4, and EW-5). This represents an approximate 7 percent increase in recovered groundwater and an approximate 24 percent decrease in mass recovery compared to 2020 and is attributed to the decreasing CHC concentrations in recovered groundwater during 2021.
- In 2021, the off-site active recovery system (EW-10, EW-11, EW-12, and FASW) extracted approximately 6.7 Mgal of groundwater and 85 lbs of total dissolved CHC mass. This represents an approximate 11 percent decrease in recovered groundwater and an approximate 25 percent decrease in mass recovery compared to 2020 and is attributed the decreasing CHC concentrations and lower volume of recovered groundwater during 2021.
- In 2021, the passive Toe Drain system recovered approximately 0.61 Mgal of groundwater and approximately 1.1 lbs of dissolved CHC mass. This represents an approximate 28 percent decrease in recovered groundwater and near equal mass recovery compared to 2020 and is attributed to seasonal variations and slightly higher CHC concentrations in recovered groundwater during 2021.
- Monthly National Pollutant Discharge Elimination System (NPDES) and POTW monitoring during 2021 reported three permit exceedances in April, May, and December 2021, respectively.

The following activities are planned for 2022:

- Continue operation and optimization of ongoing groundwater recovery and treatment systems.
- Planning/permitting of CHC mass removal at three on-site source areas.

1 INTRODUCTION

Arcadis U.S., Inc. (Arcadis) has prepared this 2021 2nd Semiannual Remedial Action and Annual Summary Report for the former Federal Pacific Electric Company (FPE) facility in Edgefield, South Carolina, on behalf of FPE. This report documents FPE's ongoing groundwater recovery and treatment operations, monthly and quarterly discharge monitoring, quarterly, semiannual groundwater and surface-water monitoring, and additional system modifications and investigations conducted during 2021.

This report provides a description of work performed, information regarding the distribution of dissolved chlorinated hydrocarbons (CHCs) in groundwater, trends in water quality, system modifications, recovery and treatment system operations, maintenance, performance, and a summary of CHC mass recovery during 2021. The report also includes tabulated data and laboratory analytical reports for the samples collected during the reporting period.

The following activities were conducted during the reporting period:

- Continuous oversight of recovery and treatment system operations, maintenance, and monitoring
- Monthly recovery system and discharge sampling
- Quarterly groundwater gauging and sewer-discharge sampling (March 2021, June 2021, September 2021, and December 7, 2021)
- Semiannual surface water and groundwater sampling (April 2021 and September 2021)
- Multi-media and main control panel PLC upgrade

2 SUMMARY OF 2021 ACTIVITIES

FPE operates on-site and off-site groundwater capture systems comprised currently of nine extraction wells and a Toe Drain capture system. Influent groundwater is conveyed to FPE's on-site treatment plant (see **Figure 1**). Recovered groundwater from the on-site and off-site capture systems is pumped to an equalization tank; it then passes through multi-media filters and is transferred to a low-profile air stripper for treatment. Once treated, the groundwater flows to an effluent holding tank, where the water is discharged to three different locations following carbon polishing, including on-site infiltration trenches, Beaverdam Creek (NPDES permitted outfall 001), and the on-site storm water pond (NPDES permitted outfall 002). Operation and maintenance of the current groundwater capture and treatment system consists of weekly inspections of the groundwater extraction and treatment components, as well as routine and response maintenance of the remediation systems. Additionally, the following activities are performed to assess CHC mass recovery and meet discharge compliance requirements:

- Monthly sampling of recovered groundwater from extraction wells and the Odell Reservoir Toe Drain capture system
- Monthly sampling of treated effluent (under National Pollution Discharge Elimination System [NPDES] permit number SC0047813)
- Quarterly sewer discharge sampling (ACPSA permit number FPE 2019-1)

The methodology and findings of the system operation, maintenance, and monitoring activities completed during the reporting period are summarized in the following sections of this report.

2.1 Weekly Groundwater Recovery and Treatment System Operation, Maintenance, Monitoring, and Monthly Discharge Sampling

Weekly system management events currently consist of groundwater recovery and treatment system inspections, routine system maintenance and repairs, and recording of system operating data. Response to system malfunctions/alarms and associated repairs and resets are performed on an as-needed basis. Inspection and maintenance logs are maintained at the facility, as required by the operating permit. **Table 1** of **Appendix A** provides a cumulative summary of system downtime and associated maintenance/repairs.

Water samples were collected monthly from the on-site and off-site extraction wells, Toe Drain influent, combined system influent, and effluent discharged to Beaverdam Creek (Outfall 001) and on-site storm water pond (Outfall 002). Results of the water sampling are used to evaluate CHC mass recovery/treatment system performance and to prepare the monthly Discharge Monitoring Report (DMR), as required under NPDES discharge permit (# SC0047813). All samples were analyzed for Target Compound List (TCL) volatile organic compounds (VOCs) by SGS North America, Orlando, Florida, using United States Environmental Protection Agency (USEPA) Method 8260B. In addition, Toe Drain effluent samples were analyzed for biological oxygen demand (BOD), total suspended solids (TSS), and pH (Pace Analytical). Monthly influent and effluent analytical data collected since September 2009 are provided in **Table 2** of **Appendix A**.

Quarterly ACPSA Discharge Monitoring composite samples of the system effluent were collected over a 24-hour period during March, June, September, and December 2021, in accordance with the permit requirements. Quarterly sewer effluent samples were analyzed for pH, BOD, TSS, Chemical Oxygen Demand (COD), Total Petroleum Hydrocarbons (TPH), barium, chromium, trichloroethene (TCE), and cis-1,2-dichloroethene (cis-1,2-DCE). All samples were analyzed by SGS using USEPA Methods. Analytical results for all parameters complied with permit conditions.

Effluent flow rates, recorded by the supervisory control and data acquisition (SCADA) system, are retrieved daily to document total treated effluent discharge volumes. These data, coupled with the effluent analytical data, comprise the NPDES and the ACPSA DMR data sets that are submitted monthly to the South Carolina Department of Health and Environmental Control (SCDHEC) and ACPSA.

2.2 Quarterly Groundwater Gauging

Water-levels were gauged quarterly during 2021 in approximately 120 wells located at the former FPE facility, the Star Fibers/Martin property, and other properties located in the vicinity of Rabbit Trail Road (**Figure 1**). Water-level measurements, which were obtained to the nearest 0.01 foot using an electronic water-level indicator, were used in conjunction with existing top-of-casing elevation data to determine groundwater elevations in the saprolite, partially weathered rock (PWR), and bedrock zones.

2.3 Semiannual Surface-Water and Groundwater Quality Monitoring

Surface-water quality monitoring was performed during April and September 2021 at established locations of the Odell Reservoir, the Odell Dam discharge pipes, and Beaverdam Creek . Surface water samples from the Odell Reservoir were collected from a depth approximately 1.5 feet above the reservoir bottom with a stainless-steel-bomb sampler and samples from the Odell Dam discharge pipes and Beaverdam Creek were collected directly from the surface. All surface water samples were placed in pre-preserved 40-ml VOA vials, placed on ice in a cooler and shipped to SGS under chain-of-custody protocol, for analysis of TCL VOCs via SW-846 Method 8260B. In situ field parameter measurements (pH, dissolved oxygen [DO], conductivity, temperature, total dissolved solids [TDS], oxidation-reduction potential [ORP], and turbidity) were measured at all sampling locations using a calibrated water quality meter.

Groundwater samples were collected from 23 and 59 established well locations during April 2021 and September 2021, respectively. Upon completion of water-level gauging, the monitoring wells containing groundwater were each purged of a minimum of three well volumes of water, or until the well was dry, using a submersible pump. Purge water from the sampled wells was discharged to the on-site treatment system. After purging, a representative groundwater sample was obtained from each well using disposable polyethylene bailers, transferred into laboratory-prepared containers, placed on ice in a cooler, and shipped to SGS under chain-of-custody protocol for analysis of TCL VOCs by SW-846 Method 8260B. Field parameters (pH, temperature, conductivity, DO, ORP, TDS, and turbidity) were measured and recorded upon sample collection.

2.4 Recovery and Treatment System Modifications

Main Treatment System PLC Panel Upgrade

As part of a multi-phase effort to upgrade the on-site and off-site system PLC panels initiated in 2020, Phase II activities were completed during 2021 with the fabrication and replacement of the multi-media filter (MMF) and main treatment system control panels/PLCs. Installation and startup of the replacement main PLC panel was completed July 18, 2021, with 9 days interruption to treatment system operation. All recovery wells and the treatment plant were shut down during the 9-day period, and the Toe Drain effluent was discharged directly to the ACPSA sewer outfall.

3 GROUNDWATER FLOW AND RECOVERY SYSTEM INFLUENCE

3.1 Groundwater Occurrence and Flow

Regional groundwater flows in a general north-northeast direction across the site. Measured groundwater elevations from the quarterly 2021 gauging events are provided in **Table 1**. **Figures 2, 3,** and **4** illustrate the potentiometric surfaces for the saprolite, PWR, and bedrock zones, respectively, during the 3Q21 monitoring event.

Localized gradient perturbations have developed in response to recovery and infiltration system operations. The potentiometric surfaces for each of the hydro-stratigraphic zones (saprolite, PWR, and bedrock) are influenced by the preferential anisotropy of the permeability resulting from fractures and foliations related to folding of the metamorphic and igneous bedrock along southwest-northeast axial planes. In response to groundwater extraction, the saprolite and PWR hydro-stratigraphic zones have been dewatered along these axial planes where resistant bedrock ridges occur and the saprolite unit is thin. The estimated capture zone of the current groundwater recovery system, based on September 2021 gauging data, is illustrated in **Figure 5**, and encompasses a majority of the groundwater in the three hydro-stratigraphic zones that contain detectable concentrations of dissolved CHCs exceeding SC Drinking Water Standards (SCDWS).

3.2 Groundwater Recovery and Treatment System

The on-site groundwater recovery system, which currently consists of extraction wells EW-1R, EW-2, EW-3, EW-4, and EW-5, has been in operation since June 2004. Replacement extraction well EW-1R was installed on December 19, 2016, piped to the existing treatment system, and brought on-line in April 2017. New extraction well EW-5 was constructed in existing open borehole monitoring well MW-55 in September 2019 and was brought online March 3, 2020. The off-site groundwater recovery system, which currently consists of extraction wells EW-10, EW-11, EW-12, and FASW, and the passive Toe Drain system, has been in operation in September 2009. EW-12, which was installed September 2014, has been on-line since February 2015. The Toe Drain capture system and its associated treatment system operated from January 1999 to 2009 when it was redirected to the onsite treatment plant. The Toe Drain Seep Collection system, which directs shallow groundwater to the Toe Drain Sump, was constructed and brought on line in July 2019.

The groundwater treatment system was put into operation in 2004 and currently consists of multi-media filtration, air stripping, and carbon polishing, with treated discharge going to two NPDES permitted outfalls, an on-site infiltration gallery, and an available POTW outfall. Except for effluent samples collected in April, May, and December 2021, analyzed constituents in treated effluent discharged to NPDES permitted outfalls 001 and 002 were all below method detection limits and/or permit discharge limits during 2021. Granular activated carbon filtration media was replaced following the April/May 2021 discharge limit exceedance and discharge to the NPDES outfalls resumed on June 10, 2021. Upon receipt of effluent analytical results (10 µg/L TCE) on December 28, 2021, a confirmation sample was immediately collected, all groundwater recovery well and treatment systems were immediately shutdown, the Toe Drain influent was redirected to the ACPSA permitted outfall, and SCDHEC was notified in accordance with NPDES Permit SC47813. An evaluation of treatment system equipment and operations ensued following system shutdown to determine the root cause and implement necessary corrective actions.

4 SURFACE WATER AND GROUNDWATER QUALITY

4.1 Surface Water Quality

The surface-water quality monitoring data from each location for 2021 are summarized in **Table 3** and the analytical laboratory report for the September 2021 monitoring event is included in **Appendix B**. Reported

CHC concentrations in surface-water samples collected during September 2021 are illustrated in **Figure 6**. Reported CHC concentrations in all surface-water samples from the dam discharge structure, the Odell Reservoir, and Beaverdam Creek were below detection during 2021. The analytical results for all reservoir samples collected since March 2010 have met the South Carolina Surface Water Quality Standards (SCSWQS).

4.2 Groundwater Quality

The groundwater quality monitoring data from each location for 2021 are summarized in **Table 4** and the analytical laboratory report for the September 2021 monitoring event is included in **Appendix B**. **Figures 7**, **8**, and **9** illustrate interpolated iso-concentration contours for dissolved TCE in the saprolite, PWR, and bedrock hydrogeologic zones, respectively. Following are overall observations of groundwater quality in the three hydro-stratigraphic zones.

Saprolite Zone Groundwater

Reported TCE concentrations in saprolite zone groundwater during 2021 indicate an order or magnitude decrease in downgradient well SMMW-3 as compared to those observed in September 2020. Conversely, reported TCE concentrations in saprolite well SMMW-2 were an order of magnitude greater in 2021 than those reported in September 2020. The reported 2021 TCE concentrations are within historic ranges and the fluctuations are attributed to seasonal variation.

PWR Zone Groundwater

Reported TCE concentrations in the PWR zone groundwater during 2021 are consistent with those reported in September 2020. The highest reported TCE concentration continues to be reported in Star Fiber Property well SMMW-4 (3.94 mg/L).

Bedrock Zone Groundwater

Reported TCE concentrations in the bedrock zone groundwater during 2021 are generally consistent with those reported in September 2020. Notable decreases of TCE concentrations in onsite recovery wells EW-2 and EW-5, and downgradient monitoring wells B-4SF, B-1SF, SMMW-7, and SMMW-9 are observed in September 2021 versus September 2020; however, 2020 and 2021 concentrations are of the same order of magnitude and the highest TCE concentration continues to be reported in Star Fiber Property well SMMW-9 (13.8 mg/L).

5 GROUNDWATER RECOVERY SYSTEM EFFECTIVENESS

Ongoing operation of the on-site and off-site groundwater extraction systems continues to remove CHC mass from the ground water. The 2021 monthly groundwater recovery volumes for each extraction well are presented in **Table 5** and the total CHC mass recovery for each extraction well during 2021 is illustrated in **Figure 10**. The total volume of groundwater recovered from the on-site, off-site, and Toe Drain groundwater recovery systems during 2021 was approximately 15.4 million gallons (mGAL) (**Table 5**), which represents an average continuous withdrawal rate of approximately 29 gallons per minute (gpm).

The cumulative total volume of groundwater recovered and treated by the system from 2004-2021 is approximately 222 mGal. Overall trends and 2021 groundwater extraction and CHC mass recovery for each of the recovery systems and summarized in the following.

2021 Onsite System Groundwater Volume and CHC Mass Recovery

Operation of the on-site extraction system has slowed downgradient migration of impacted groundwater by effectively lowering the hydraulic gradient from the facility to the downgradient Star Fiber property (see **Figure 5**). In addition, large portions of the saprolite have been dewatered onsite due to the operation of the extraction system. During 2021, the on-site system recovered a total of approximately 8 million gallons (Mgal) of groundwater, for a cumulative on-site total of approximately 119 Mgal since installation in 2004. Most of the groundwater has been extracted by recovery well EW-4, which produced approximately 59 percent of the total recovered on-site water volume during 2021. During 2021 the on-site extraction system recovered approximately 184 pounds (lbs) of CHC mass, with a majority (approximately 88 percent) of the CHC mass extracted by recovery wells EW-2, EW-4, and EW-5.

The following CHC concentration trends and 2021 mass recovery have been observed, based on groundwater extraction and samples collected from the extraction wells during 2021:

- EW-1R: TCE concentrations in EW-1R ranged from 2.0 mg/L (February) to 5.4 (May) mg/L during 2021 and are consistent with those reported in 2020; EW-1R recovered approximately 14 lbs of total CHCs in 2021.
- EW-2: In general, declining TCE concentration trends have been observed at this extraction well since September 2009. TCE ranged from 7.22 mg/L (March 2021) to 3.21 mg/L (October 2021) during 2021; EW-2 recovered approximately 36 lbs of total CHCs in 2021.
- EW-3: TCE concentrations have steadily declined since January 2015 and ranged from 1.1 mg/L (May 2021) to 0.62 mg/L (August 2021) during 2021; EW-3 recovered approximately 7 lbs of total CHCs in 2021.
- EW-4: TCE concentrations in well EW-4 have exhibited a steady decline since November 2014. Concentrations ranged from 1.08 mg/L (February 2021) to 1.54 mg/L (September 2021) during 2021; EW-4 recovered approximately 67 lbs of dissolved CHC mass during 2021.
- EW-5: TCE concentrations have continued to decline in new extraction well EW-5 since its initial startup in March 2020 with concentrations ranging from 6.76 mg/L (March 2021) to 3.62 mg/L (October 2021); EW-5 recovered approximately 59 lbs of dissolved CHC mass during 2021.

Overall mass recovery of the onsite recovery system during 2021 was approximately 58 lbs less than 2020. The reduced mass recovery is primarily attributed to decreasing concentrations as approximately 0.14 Mgal more groundwater was recovered compared to 2020. All recovery systems (except the Toe Drain) were shut down during planned treatment equipment upgrades during July 2021.

2021 Offsite System Groundwater Volume and CHC Mass Recovery

Sustained pumping of the offsite groundwater extraction wells has resulted in non-detectable concentrations of CHCs in the surface water of the Odell Reservoir since 2010. During 2021, the active

offsite system recovered approximately 6.7 Mgal of groundwater, for a cumulative total of approximately 88 Mgal since installation in 2009. Approximately 77 percent of the off-site groundwater recovered during 2021 was extracted by recovery wells EW-11 and EW-12, which recovered approximately 5.6 Mgal. The total CHC mass recovered by the active off-site system in 2021 was 85 lbs, representing a decrease of approximately 29 lbs when compared to 2020. The majority of the off-site CHC mass was recovered by extraction wells EW-10 and EW-12 (approximately 56 percent) of the off-site total. EW-12 recovered approximately 49 lbs in 2021, which is 34% lower than the mass recovered in 2020 (75 lbs).

During 2021, the passive Toe Drain system recovered approximately 0.61 Mgal of water and approximately 1.1 lbs of dissolved CHC mass. This represents an approximate 28 percent decrease in recovered groundwater and near equal mass recovery compared to 2020.

The following CHC concentration trends and 2021 mass recovery have been observed, based on groundwater extraction and samples collected from the extraction wells and Toe Drain during 2021:

- EW-10: TCE concentrations have steadily decreased since the mid-2013 but remained steady during 2021 with concentrations ranging from 2.13 mg/L (May 2021) to 1.51 mg/L (November 2021); EW-10 recovered approximately 18 lbs of total CHCs in 2021.
- EW-11: TCE concentrations have steadily declined overall since startup in September 2009. Concentrations ranged from 0.494 mg/L (May 2021) to 0.331 mg/L (October 2021) with approximately 13 lbs of total CHCs recovered in 2021.
- EW-12: Overall decreasing TCE concentrations have been observed in EW-12 since fourth quarter 2018. Reported TCE concentrations ranged from to 2.4 mg/L (February 2021) to 1.62 mg/L (May 2021) during 2021; EW-12 recovered approximately 49 lbs of total CHCs in 2021.
- FASW: TCE concentrations have continued to exhibit a gradual decrease since 2009, with reported concentrations ranging from 0.486 (March 2021) to 1.67 mg/L (September 2021). FASW recovered approximately 5 lbs of total CHCs in 2021.
- Toe Drain: TCE concentrations have decreased overall since 2017 following the startup of upgradient extraction well EW-12 in 2014. The highest TCE concentrations are detected in the left Toe Drain and ranged from 0.083 mg/L (October) to 0.188 mg/L (May 2021) during 2021. The right Toe Drain continues to exhibit low TCE concentrations ranging from ND (January 2021) to 0.007 mg/L (September 2021) during 2021.

Overall mass recovery of the offsite recovery system during 2021 was approximately 29 lbs less than 2020. The reduced mass recovery is attributed to both decreasing concentrations and approximately 1.15 Mgal less recovered groundwater compared to 2020. All recovery systems (except the Toe Drain) were shut down during planned treatment equipment upgrades during July 2021.

CHC Distribution and Mass Recovery Over Time

To date, approximately 222 Mgals of groundwater and 11,000 lbs total CHC mass have been extracted by the on-site and off-site recovery systems. The on-site groundwater recovery system has been effective in reducing downgradient migration of impacted groundwater, reducing residual CHC mass, and lowering concentrations throughout the plume. The off-site groundwater recovery system has been effective in

reducing dissolved CHC concentrations in the Odell Reservoir to non-detect levels since 2010, thus mitigating human and ecological exposure.

Since startup of the on-site groundwater recovery system in 2004, the overall distribution and concentration of dissolved CHCs (primarily TCE) in the PWR/bedrock zones have been reduced as illustrated in **Figure 11**. In 2004, the lateral and vertical extent of groundwater containing dissolved CHCs in PWR/bedrock zone groundwater exceeding SCDWS' consisted of one large on-site area, emanating from several source areas, that extended across the Starr Fibers property and onto the Rabbit Trail Rd property. Specifically, dissolved TCE concentrations in excess of 50 mg/L were detected in the vicinity of the former Drum Burial Area (DBA) with comparable concentrations being detected in downgradient monitor wells SMMW-7 and -9, suggesting hydraulic connection in the PWR and fractured bedrock between the two areas. Reported dissolved concentrations at the former Alfred house also exceeded 10 mg/L during 2004. Reported TCE concentrations in 2012 exhibited notable reductions, particularly at the former Alfred house, following 8 years of groundwater recovery. Reported TCE concentrations in 2021 exhibited further reductions with concentrations exceeding 5 mg/L being limited to the area at and just downgradient of the former Paint Bed Drying Area (PBDA) and on Starr Fiber property at well B-1SF and downgradient well cluster SMMW-7 and -9.

Although notable volumes of CHC mass have and continue to be removed from the PWR/bedrock zones by the on-site and off-site areas recovery systems, a majority of the recovery wells have exhibited declining CHC concentrations for at least 8 years As illustrated in **Figure 12**, CHC recovery from PWR/bedrock recovery wells is generally characterized by a rapid decline in concentrations upon and shortly after initiating recovery, followed by gradual declines and relatively stable concentrations. It is expected that CHC concentrations in recovery system influent will continue to gradually decline to asymptotic conditions.

6 PLANNED 2022 ACTIVITIES

Future on-site remedial efforts will focus on optimizing the current groundwater CHC mass recovery efficiency and removal of mass within the current unsaturated zone at three primary source areas. Specifically, planned 2022 activities include planning/permitting of CHC mass removal from three identified source areas, the former DBA, former PBDA, and former Degreasing Operational Area (DOA). Ongoing off-site groundwater recovery will continue in 2022, with adjustments in drawdown depth and pumping rates to optimize recovery efficiency within the system as influent concentrations continue to decline.

FIGURES

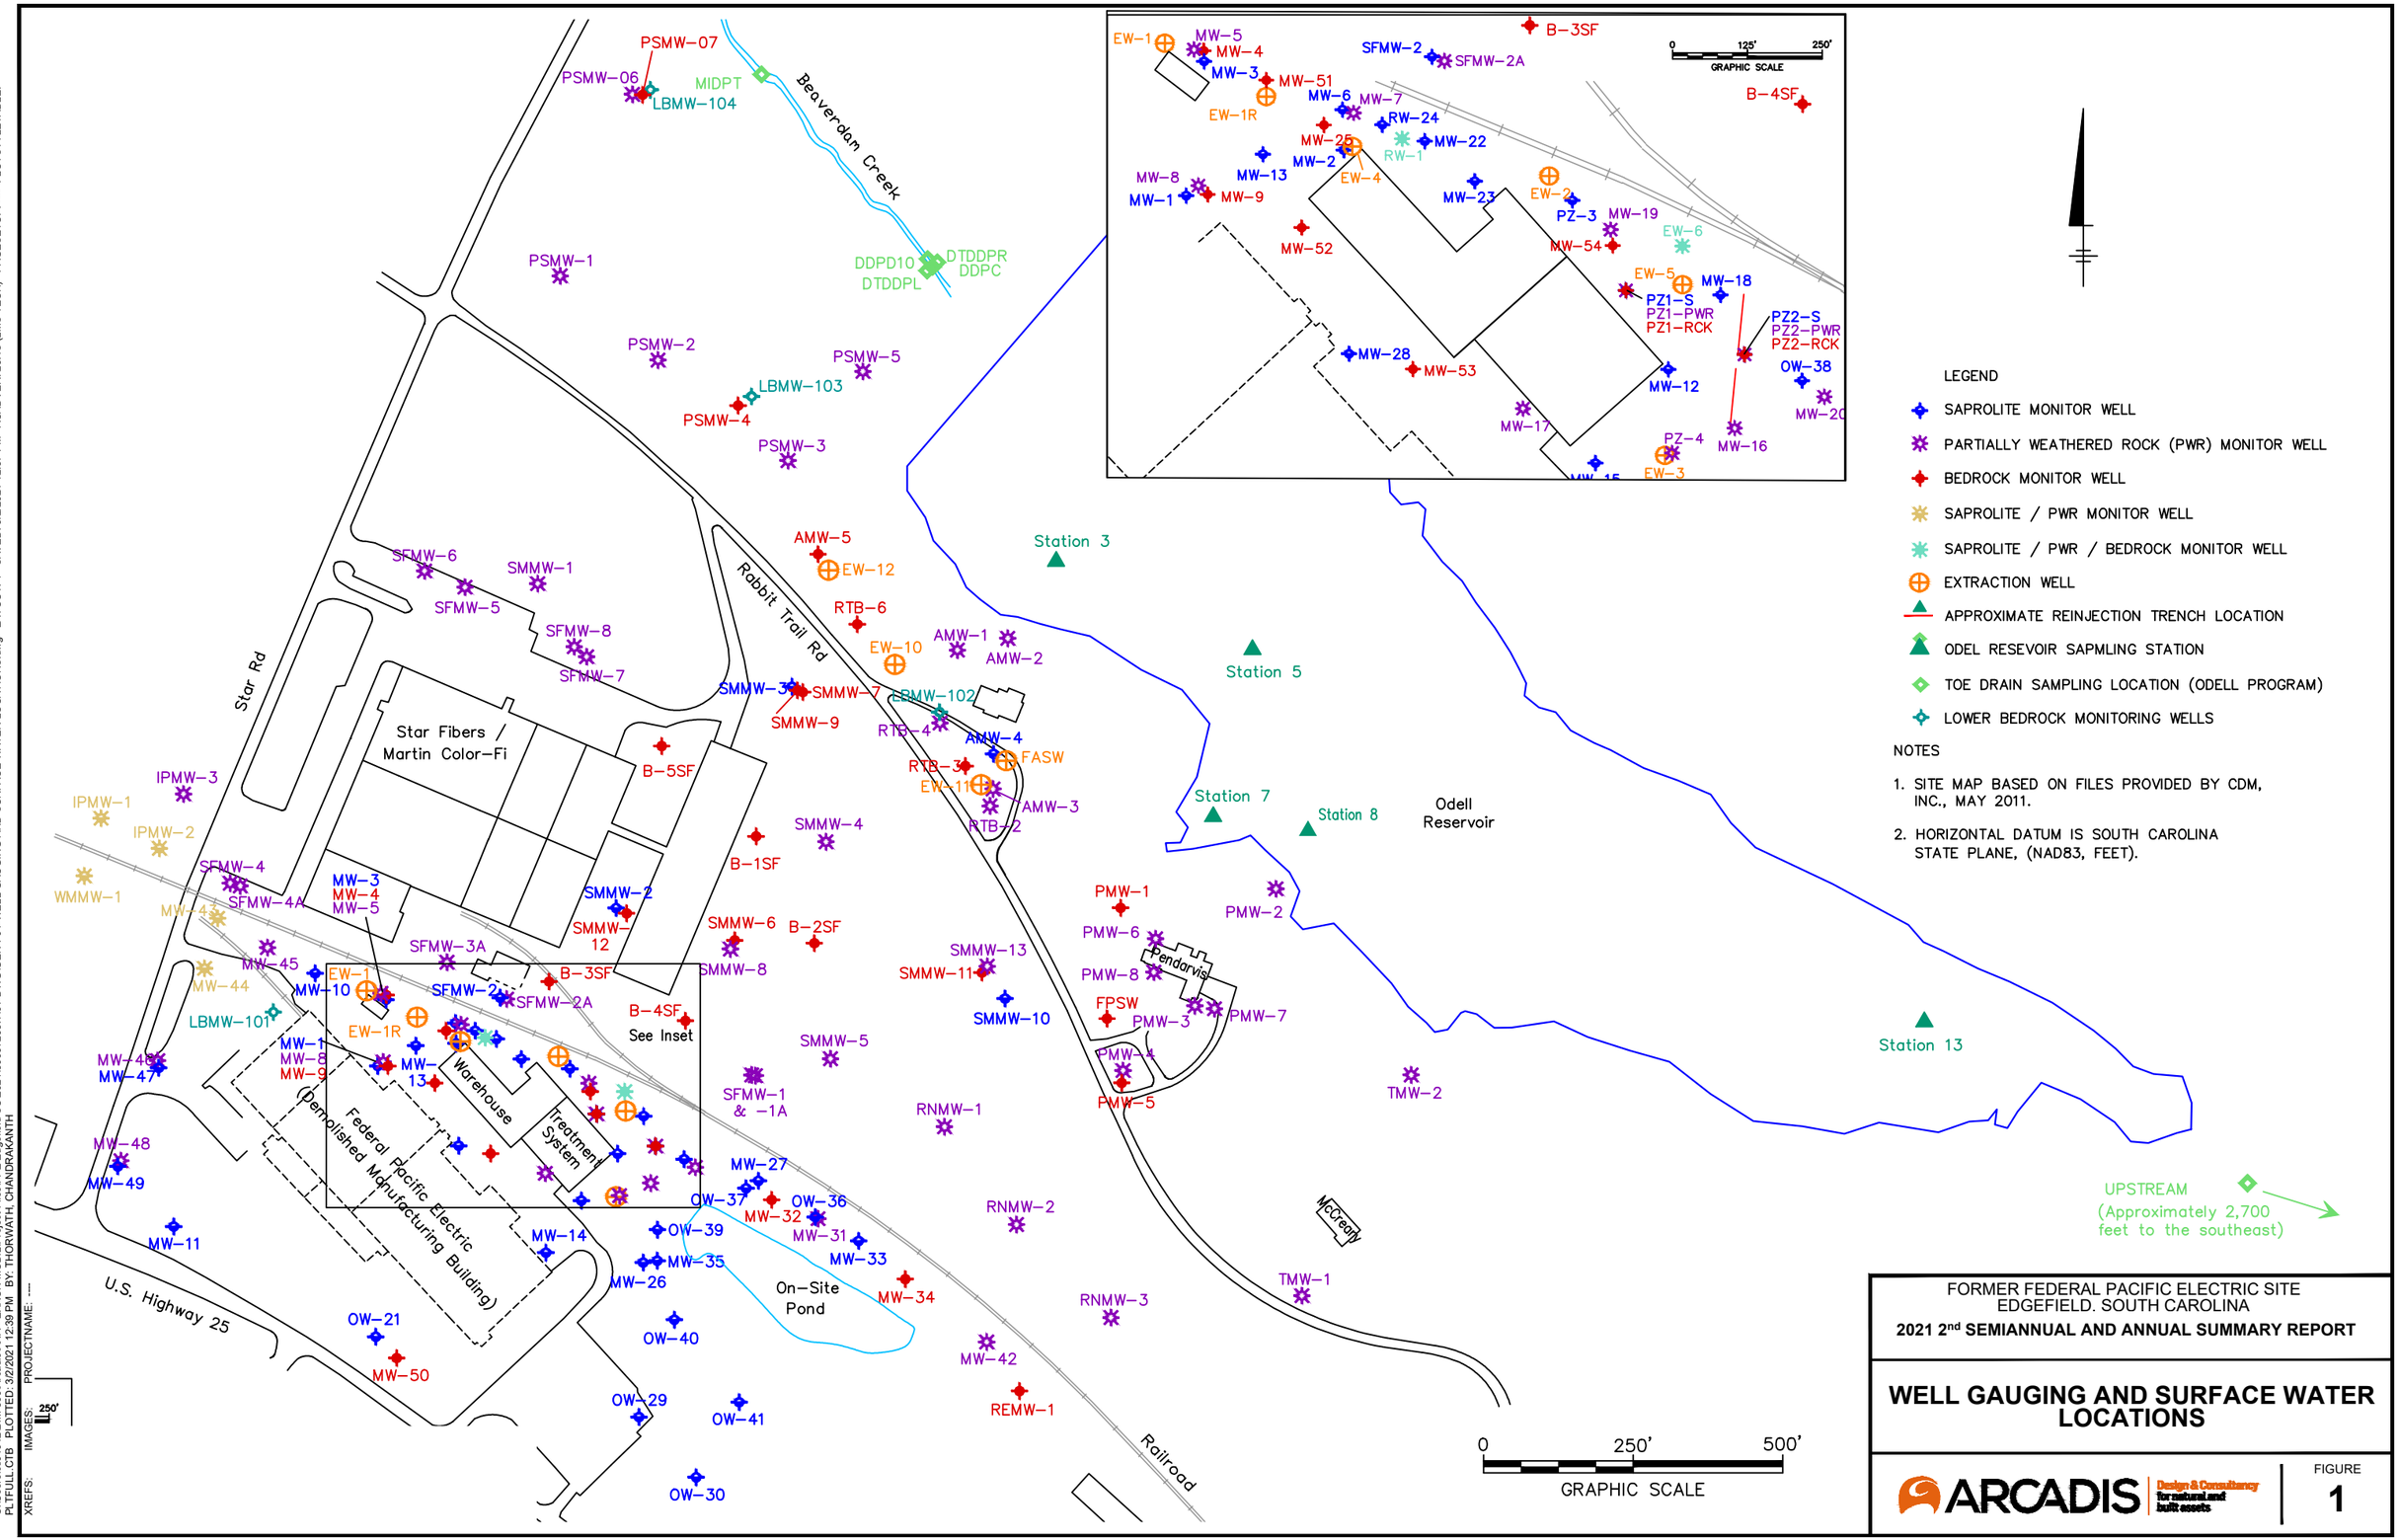

FORMER FEDERAL PACIFIC ELECTRIC SITE
EDGEFIELD. SOUTH CAROLINA
2021 2nd SEMIANNUAL AND ANNUAL SUMMARY REPORT

WELL GAUGING AND SURFACE WATER LOCATIONS

ARCADIS Design & Consultancy for natural and built assets

FIGURE
1

CITY:(Reqd) DIV/GROUP:(Reqd) DB:(Reqd) LD:(Opt) PIC:(Opt) PM:(Reqd) TM:(Opt) LYR:(Opt)ON=*;OFF=*REF*
C:\Users\ct01012\BIM 360\Arcadis\ANA - EXXON MOBIL\Project Files\FPE Edgefield SC\2021\30067293.1101-DWG\GEN-F01-WELL GAUGING AND SURFACE WATER LOCATIONS.dwg LAYOUT: 1 SAVED: 3/2/2021 12:37 PM ACADVER: 23.1S (LMS TECH) PAGESETUP: ---- PLOTSTYLETABLE:
PLTFULL.CTB PLOTTED: 3/2/2021 12:39 PM BY: THORWATH, CHANDRAKANTH
XREFS: IMAGES: PROJECTNAME: ---

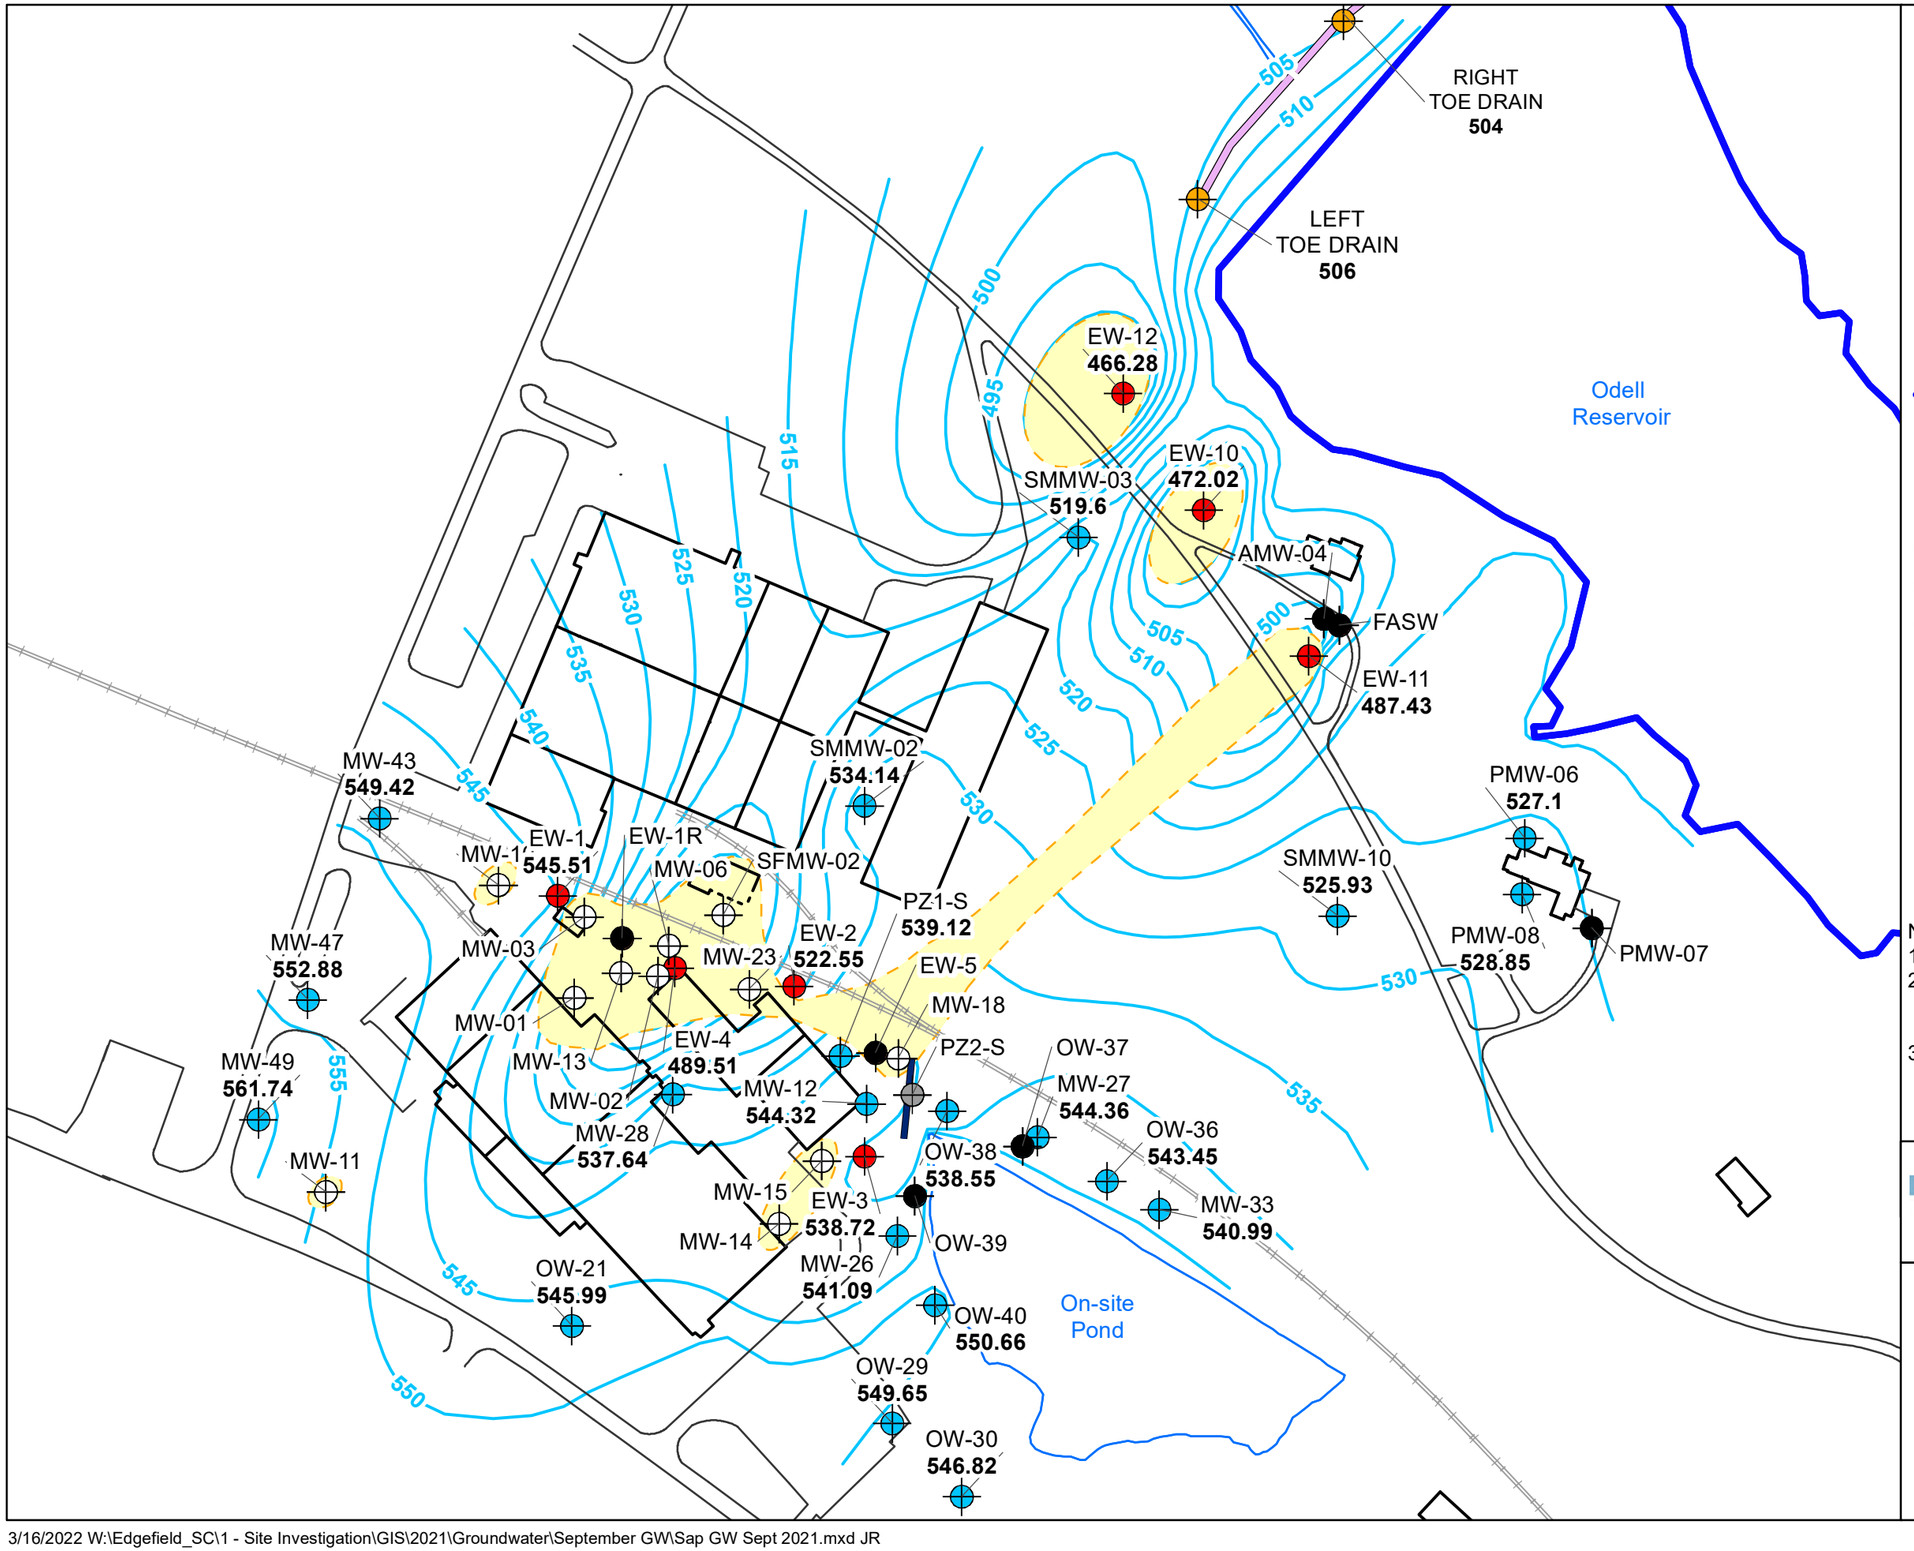

Legend

- NOT MEASURED
- WELL COLLAPSED
- DRY WELL
- TOE DRAIN WELL
- EXTRACTION WELL
- SAPROLITE WELL
- ODELL RESERVOIR
- WATER FEATURE
- ROADS
- RAILROADS
- BUILDINGS
- TOE DRAIN
- TRENCH
- GROUNDWATER ELEVATIONS, FEET ABOVE MEAN SEA LEVEL
- SAPROLITE DRY ZONE

N, W, E, S

0 100 200 400 Feet

Notes:
1. All locations and dimensions are approximate.
2. Kriging variogram components:
   Linear with anisotropy of ratio = 2, angle = 55, and slope = 1. Contour level is at 5 feet.
3. Partially weathered rock and bedrock well elevations from AMW-01, AMW-03, SMMW-04, SMMW-07, SMMW-13, and RTB-06 were used in the saprolite contouring.

NewFields
Perspective. Vision. Solutions.
1980 Post Oak Blvd., Suite 227
Houston, Texas 77056
(713) 357-5244

FIGURE 2

GROUNDWATER CONTOURS OF SAPROLITE SEPTEMBER 13, 2021

Former Federal Pacific Site, Edgefield, South Carolina

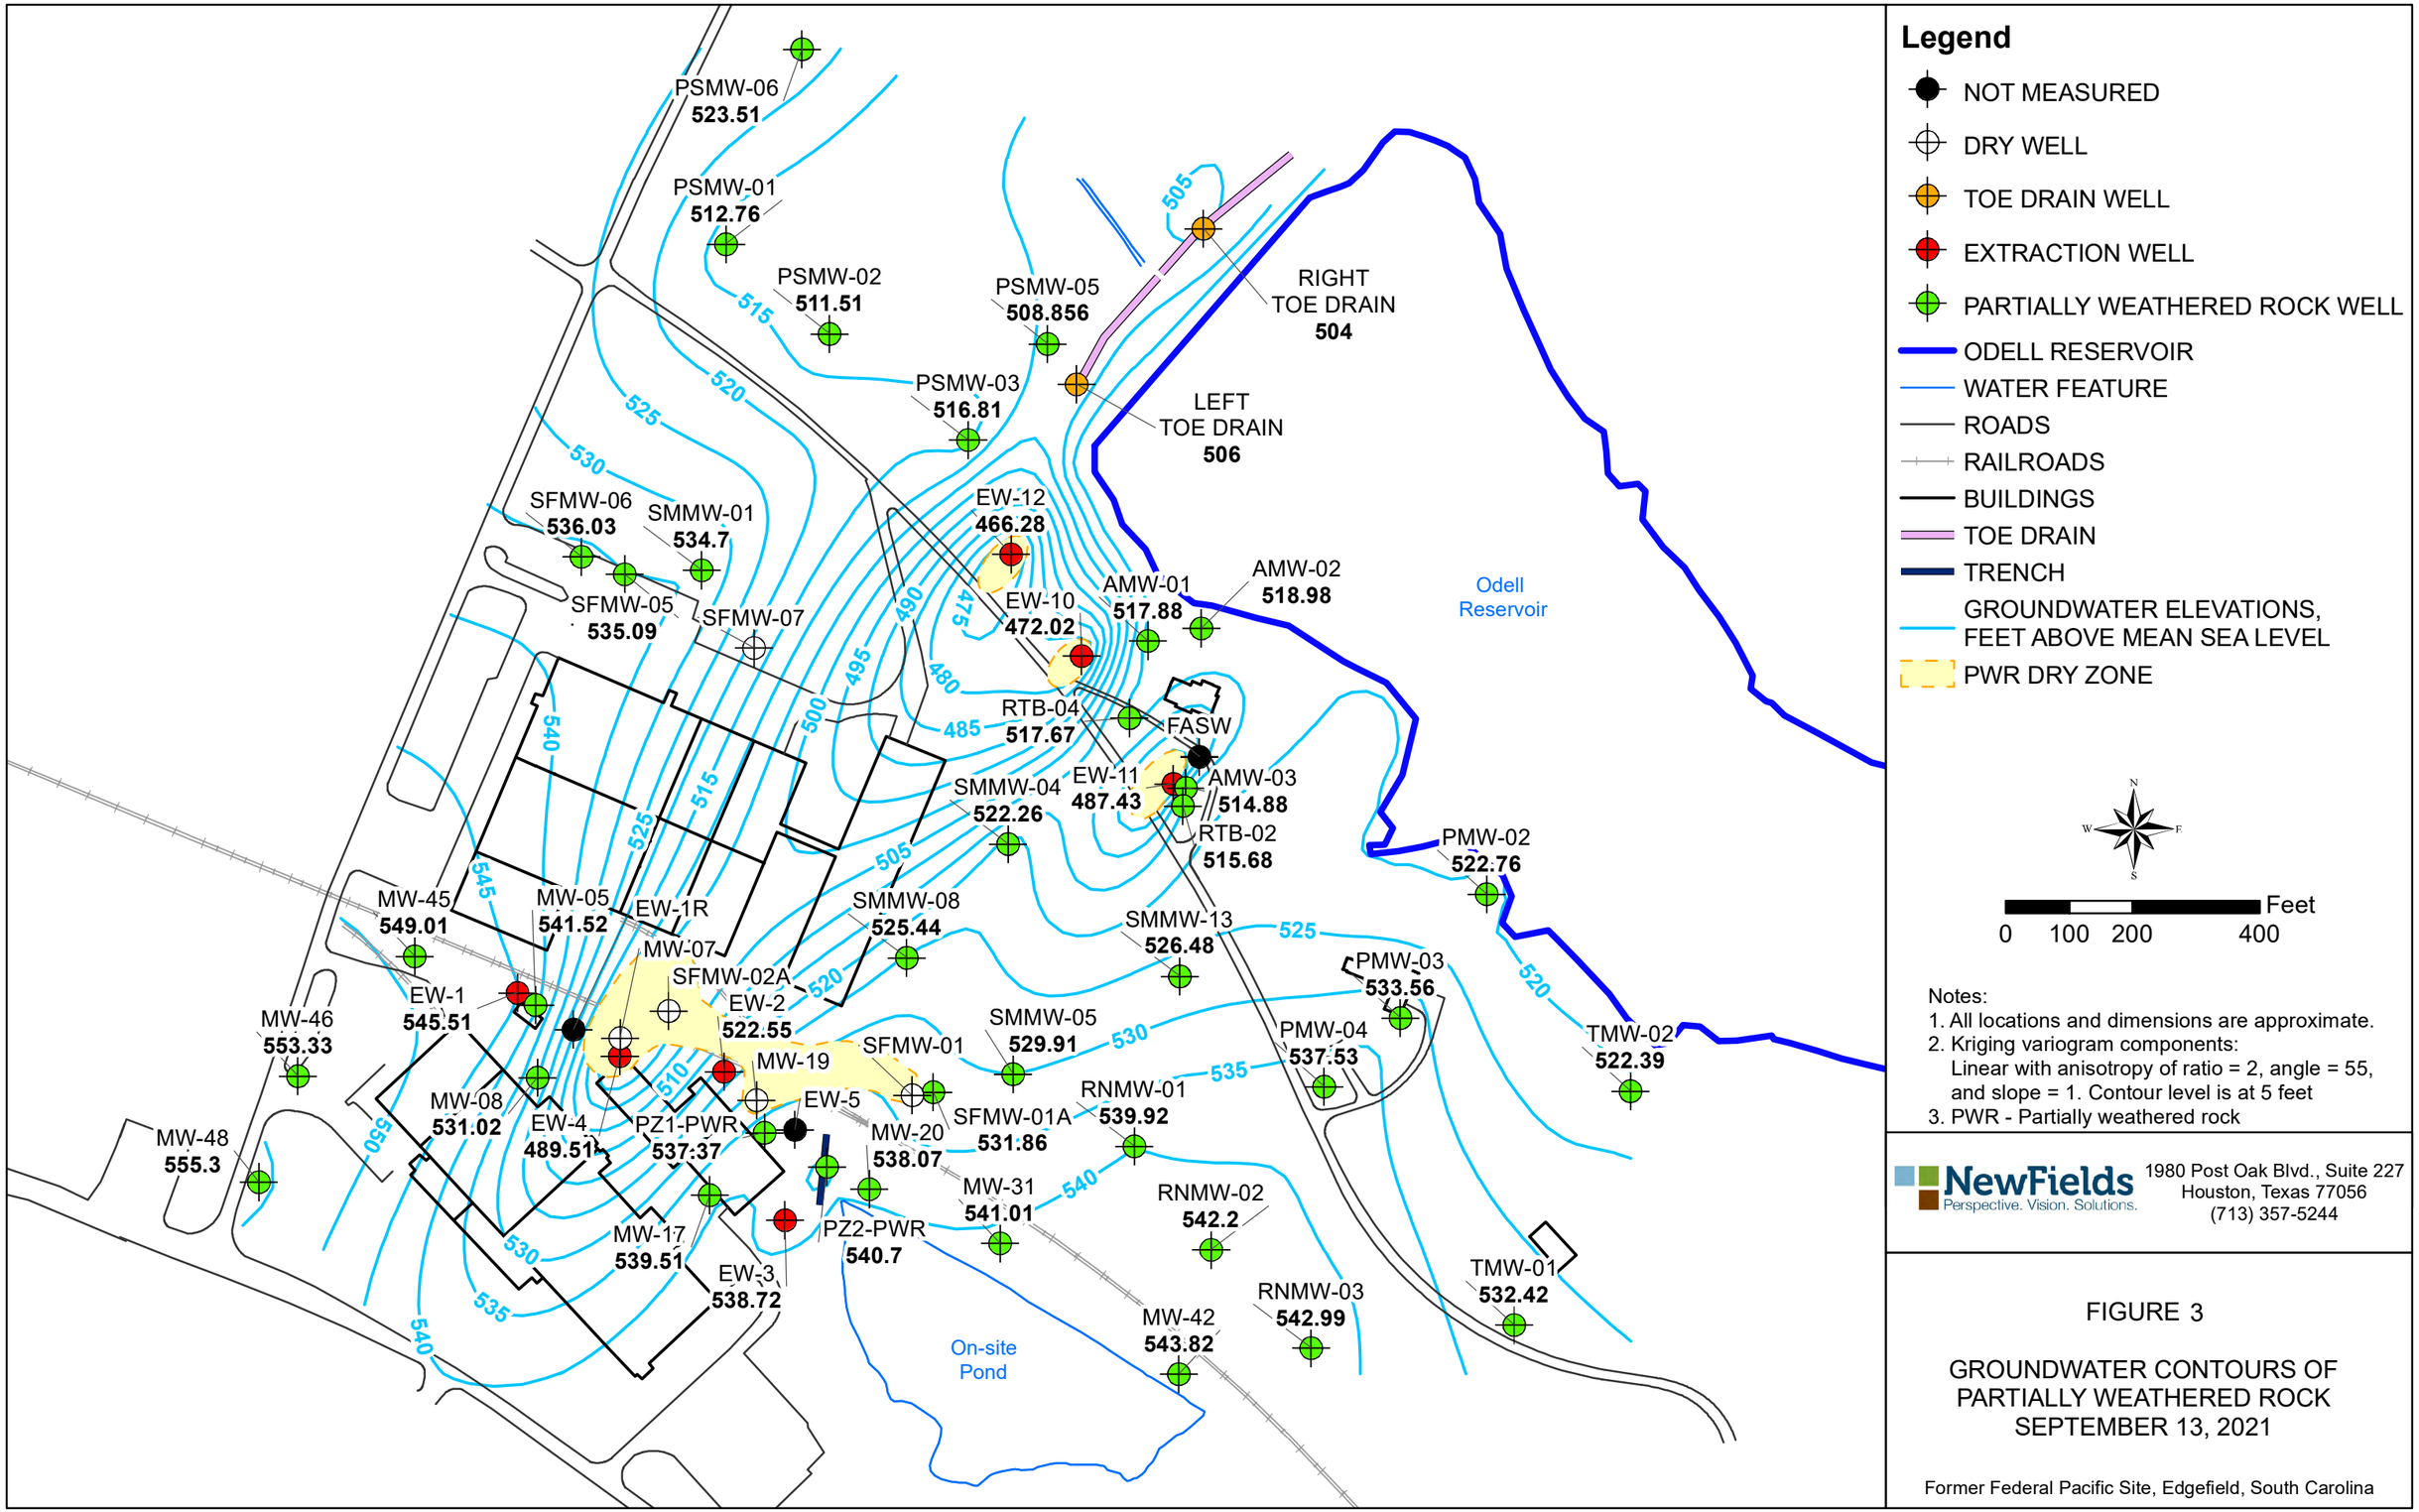

Legend

- NOT MEASURED
- DRY WELL
- TOE DRAIN WELL
- EXTRACTION WELL
- PARTIALLY WEATHERED ROCK WELL
- ODELL RESERVOIR
- WATER FEATURE
- ROADS
- RAILROADS
- BUILDINGS
- TOE DRAIN
- TRENCH
- GROUNDWATER ELEVATIONS, FEET ABOVE MEAN SEA LEVEL
- PWR DRY ZONE

N, W, E, S

0 100 200 400 Feet

Notes:
1. All locations and dimensions are approximate.
2. Kriging variogram components:
   Linear with anisotropy of ratio = 2, angle = 55, and slope = 1. Contour level is at 5 feet
3. PWR - Partially weathered rock

NewFields
Perspective. Vision. Solutions.
1980 Post Oak Blvd., Suite 227
Houston, Texas 77056
(713) 357-5244

FIGURE 3

GROUNDWATER CONTOURS OF PARTIALLY WEATHERED ROCK SEPTEMBER 13, 2021

Former Federal Pacific Site, Edgefield, South Carolina

PSMW-07
531.87

LBMW-104
503.28

LBMW-103
516.49

PSMW-04
517.48

RIGHT
TOE DRAIN
504

LEFT
TOE DRAIN
506

AMW-05
507.65

EW-12
466.28

RTB-06
516.67

EW-10
472.02

SMMW-09
520.97

LBMW-102
511.36

SMMW-07
519.59

FASW

RTB-03
514.86

EW-11
487.43

B-5SF

B-1SF

EW-1R

SMMW-12
529.99

SMMW-06
523.78

B-2SF

PMW-01
522.47

SMMW-11
526.3

FPSW
539.39

PMW-05
537.7

MW-04
541.68

MW-25
498.77

B-3SF

EW-1
545.51

LBMW-101
525.63

EW-2
522.55

B-4SF

EW-4
489.51

MW-54
493.69

MW-09
527.5

EW-5

MW-52
494.45

PZ2-RCK
540.78

MW-32
537.21

PZ1-RCK
508.18

MW-53
535.58

MW-34
542.22

EW-3
538.72

MW-50
546.19

REMW-01
544.06

505
510
515
520
525
530
535
540
545

Odell
Reservoir

On-site
Pond

Legend

- NOT MEASURED
- TOE DRAIN WELL
- EXTRACTION WELL
- BEDROCK WELL
- LOWER BEDROCK WELL
- ODELL RESERVOIR
- WATER FEATURE
- ROADS
- RAILROADS
- BUILDINGS
- TOE DRAIN
- TRENCH
- WATER LEVEL BELOW TOP OF BEDROCK ELEVATIONS, FEET ABOVE MEAN SEA LEVEL
- TOP OF BEDROCK DRY ZONE

N
W
E
S

0 100 200 400 Feet

Notes:
1. All locations and dimensions are approximate.
2. Kriging variogram components:
   Linear with anisotropy of ratio = 2, angle = 55,
   and slope = 1. Contour level is at 5 feet
3. PSMW-07 and the lower bedrock water level are not honored in shallow bedrock potentiometric surface.

NewFields
Perspective. Vision. Solutions.
1980 Post Oak Blvd., Suite 227
Houston, Texas 77056
(713) 357-5244

FIGURE 4

GROUNDWATER CONTOURS
OF BEDROCK
SEPTEMBER 13, 2021

Former Federal Pacific Site, Edgefield, South Carolina

2021 2nd SEMIANNUAL AND ANNUAL SUMMARY REPORT

2021 2nd SEMIANNUAL AND ANNUAL SUMMARY REPORT

PSMW-07 531.87
LBMW-104 503.28
LBMW-103 516.49
PSMW-04 517.48
RIGHT TOE DRAIN 504
LEFT TOE DRAIN 506
AMW-05 507.65
EW-12 466.28
RTB-06 516.67
EW-10 472.02
LBMW-102 511.36
SMMW-09 520.97
SMMW-07 519.59
FASW
B-5SF
RTB-03 514.86
B-1SF
EW-11 487.43
PMW-01 522.47
SMMW-12 529.99
SMMW-06 523.78
B-2SF
SMMW-11 526.3
FPSW 539.39
PMW-05 537.7
EW-1R
MW-04 541.68
MW-25 498.77
B-3SF
EW-1 545.51
EW-2 522.55
LBMW-101 525.63
EW-4 489.51
B-4SF
MW-54 493.69
MW-09 527.5
EW-5
MW-52 494.45
PZ2-RCK 540.78
MW-32 537.21
PZ1-RCK 508.18
MW-53 535.58
MW-34 542.22
EW-3 538.72
MW-50 546.19
REMW-01 544.06
Odell Reservoir
On-site Pond

505 510 515 520 525 530 535 540 545

Legend

- NOT MEASURED
- TOE DRAIN WELL
- EXTRACTION WELL
- BEDROCK WELL
- LOWER BEDROCK WELL
- ODELL RESERVOIR
- WATER FEATURE
- ROADS
- RAILROADS
- BUILDINGS
- TOE DRAIN
- TRENCH
- WATER LEVEL BELOW TOP OF BEDROCK ELEVATIONS, FEET ABOVE MEAN SEA LEVEL
- ESTIMATED GROUNDWATER RECOVERY SYSTEM CAPTURE ZONE

N W E S

0 100 200 400 Feet

Notes:
1. All locations and dimensions are approximate.
2. Kriging variogram components:
   Linear with anisotropy of ratio = 2, angle = 55,
   and slope = 1. Contour level is at 5 feet
3. PSMW-07 and the lower bedrock water level are not honored in shallow bedrock potentiometric surface.

NewFields
Perspective. Vision. Solutions.
1980 Post Oak Blvd., Suite 227
Houston, Texas 77056
(713) 357-5244

FIGURE 5

GROUNDWATER RECOVERY SYSTEM
CAPTURE ZONE
SEPTEMBER 2021

Former Federal Pacific Site, Edgefield, South Carolina

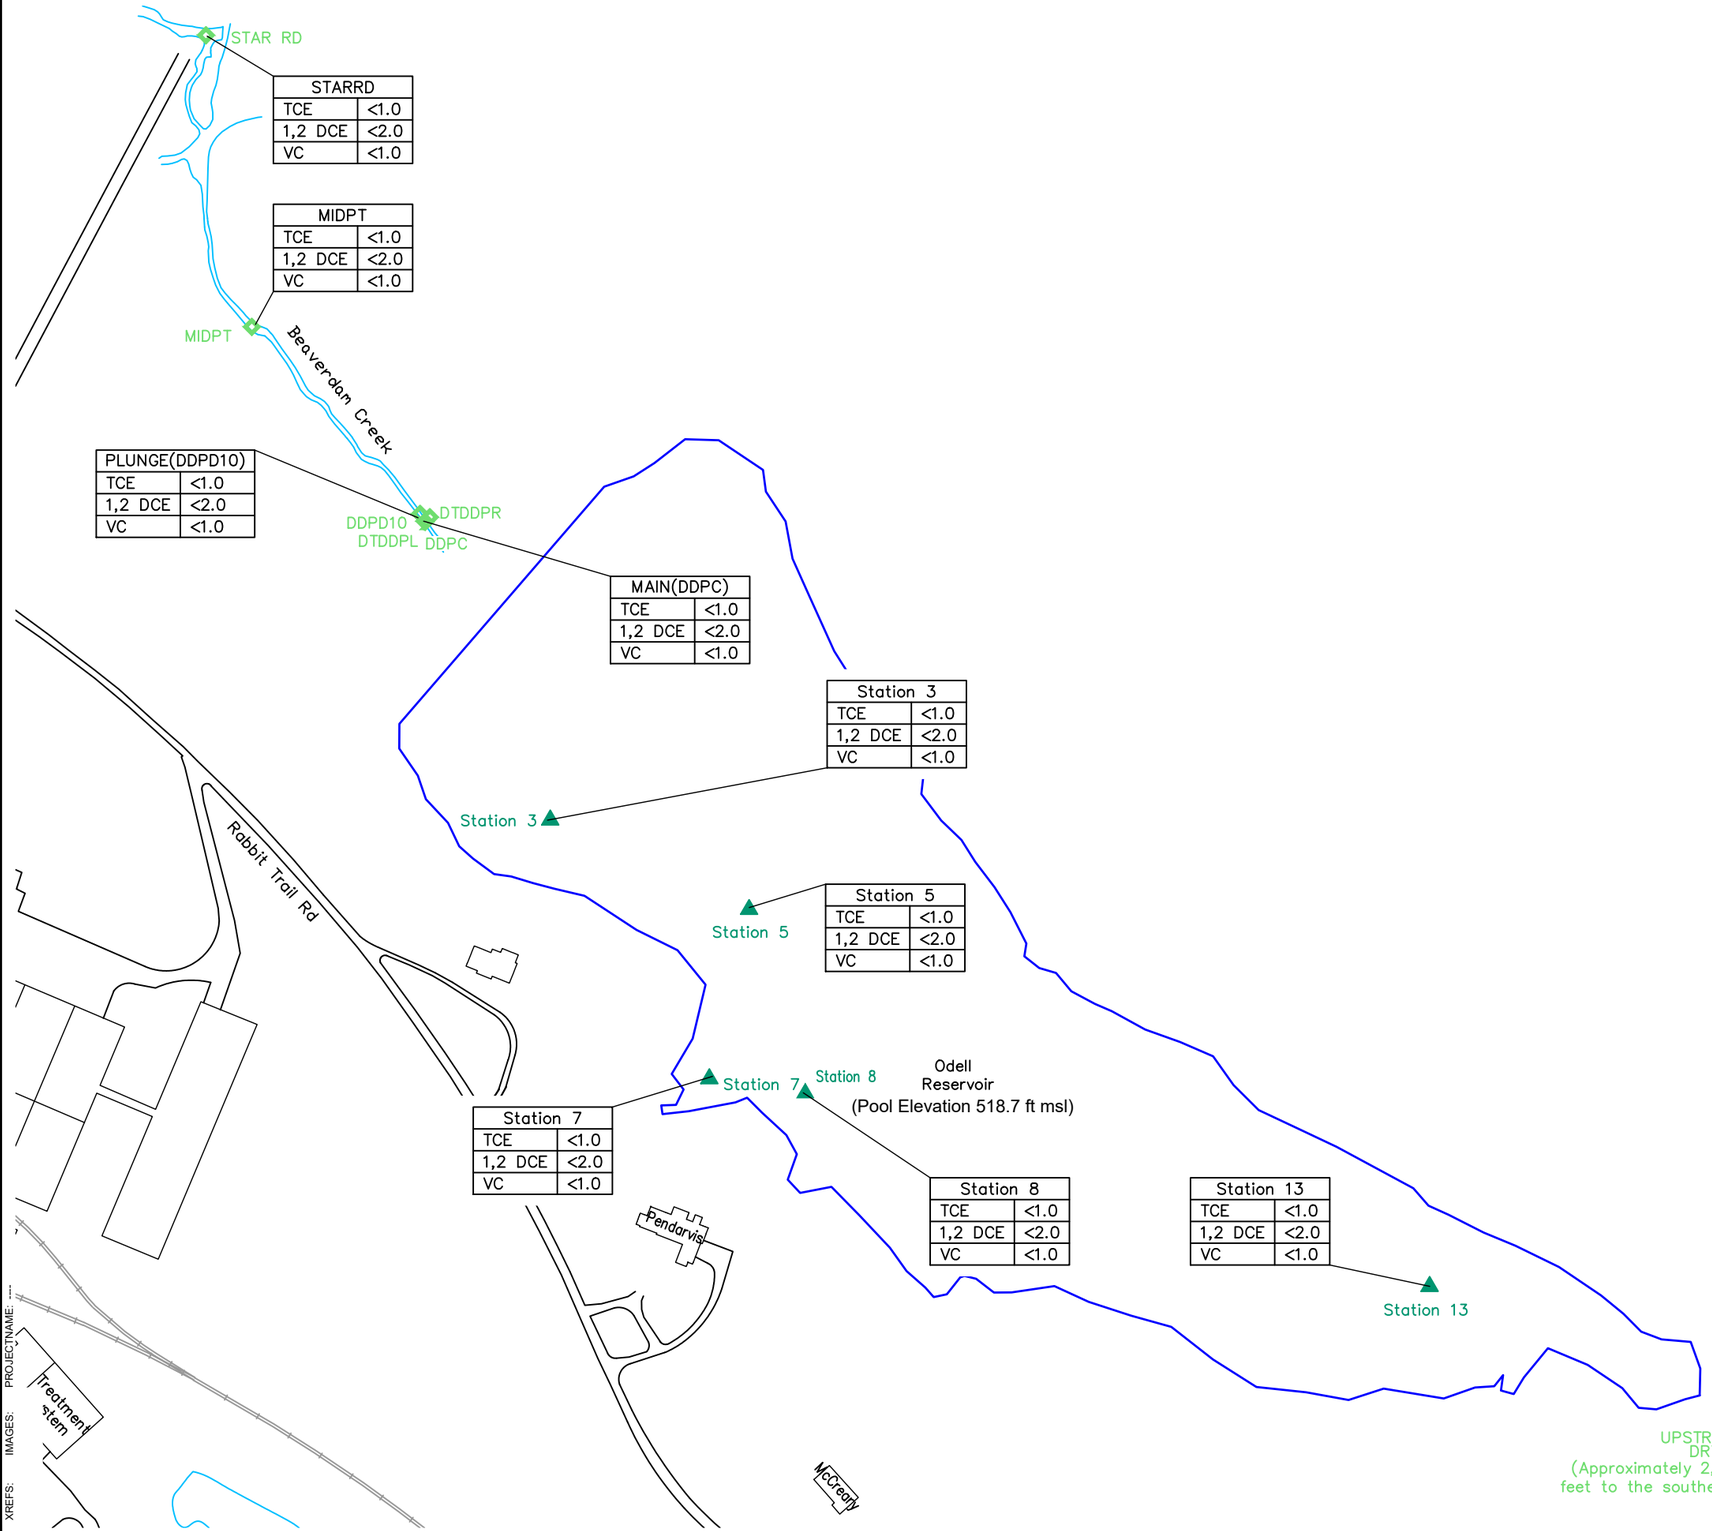

LEGEND

- ODELL RESERVOIR SAMPLING STATION
- TOE DRAIN SAMPLING LOCATION (ODELL PROGRAM)

SAMPLE LOCATION	
Constituent	Concentration in micrograms per Liter (µg/L)

TCE	TRICHLOROETHENE
1,2 DCE	TOTAL 1,2 DICHLOROETHENE
VC	VINYL CHLORIDE
FT MSL	FEET RELATIVE MEAN SEA LEVEL
<	LESS THAN LABORATORY REPORTING LIMIT
NS	NOT SAMPLED
J	ESTIMATED CONCENTRATION
DRY	WELL IS DRY

NOTES:

1. SAMPLES WERE COLLECTED APPROXIMATELY 1.5 FEET ABOVE THE BOTTOM OF THE RESERVOIR AT EACH SAMPLING LOCATION.
2. SITE MAP BASED ON FILES PROVIDED BY CDM, INC., MAY 2011.
3. HORIZONTAL DATUM IS SOUTH CAROLINA STATE PLANE, (NAD83, FEET).
4. ONLY TARGET CHLORINATED HYDROCARBONS CONCENTRATIONS ARE INCLUDED ON FIGURE.

0 250' 500'

GRAPHIC SCALE

FORMER FEDERAL PACIFIC ELECTRIC SITE
EDGEFIELD, SOUTH CAROLINA

2021 2nd SEMIANNUAL AND ANNUAL SUMMARY REPORT

SURFACE WATER SAMPLING LOCATIONS AND DATA SEPTEMBER 2021

ARCADIS

FIGURE 6

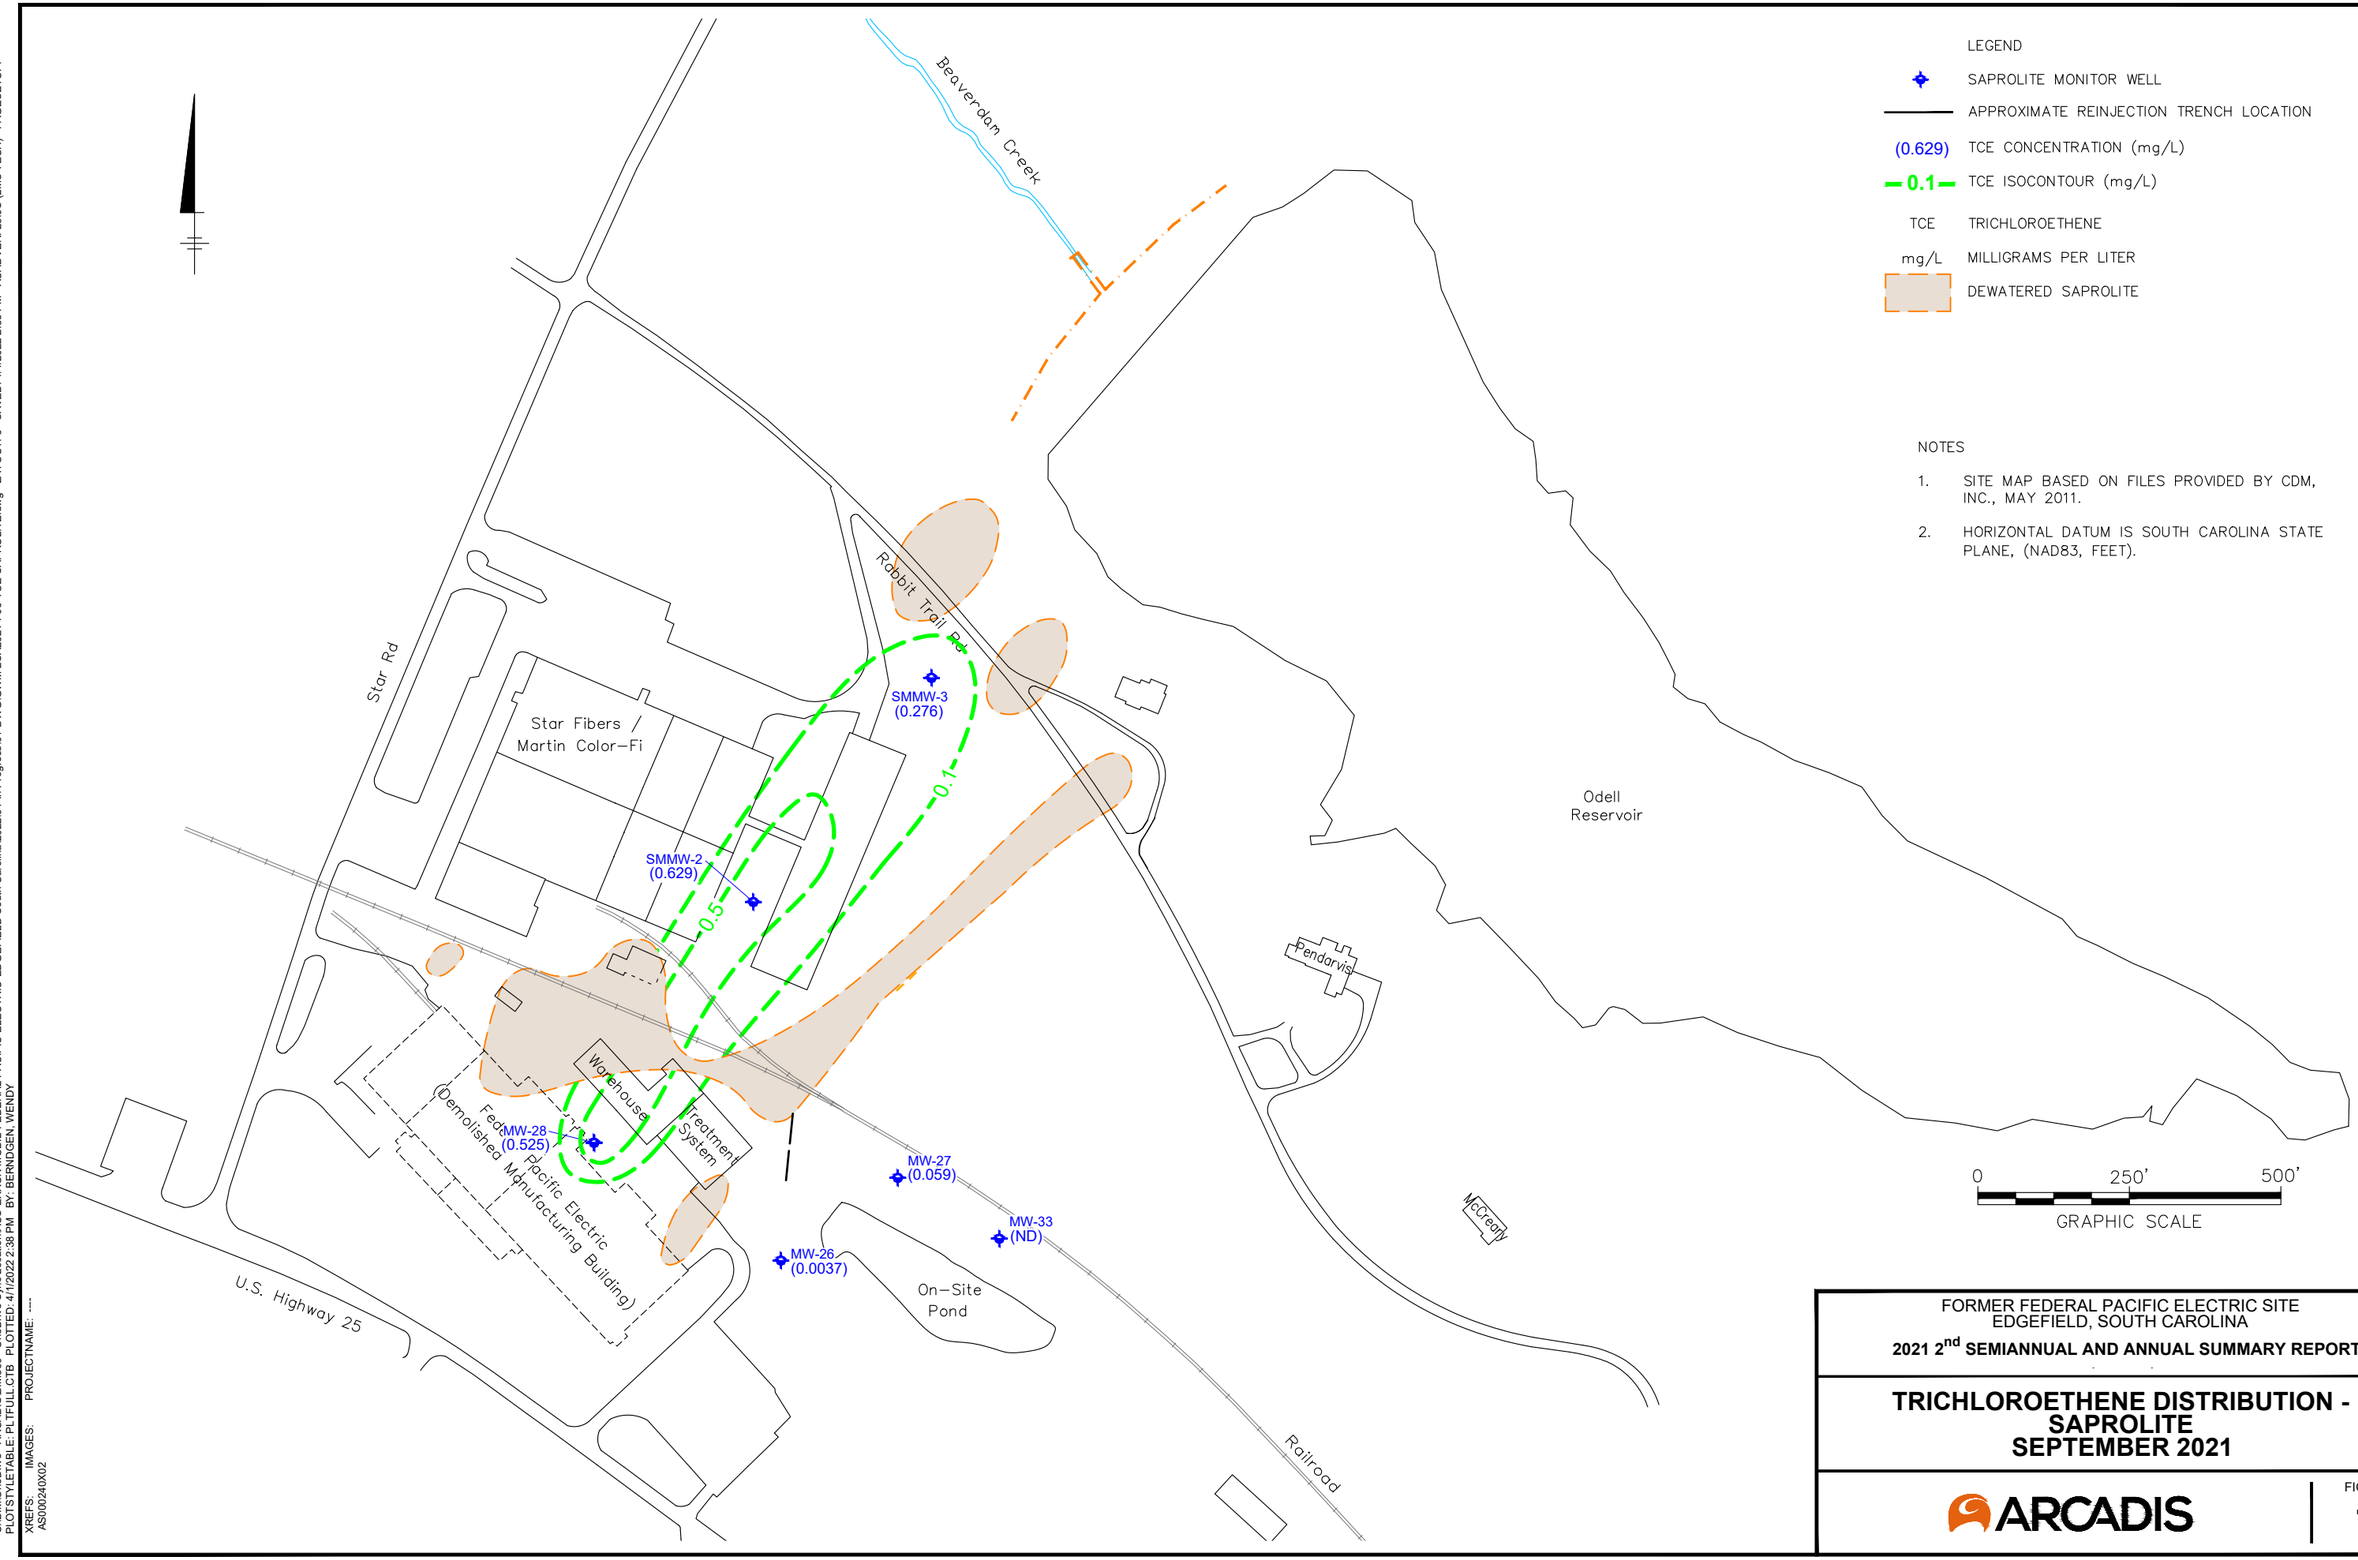

LEGEND

- SAPROLITE MONITOR WELL
- APPROXIMATE REINJECTION TRENCH LOCATION
- (0.629) TCE CONCENTRATION (mg/L)
- 0.1 TCE ISOCONTOUR (mg/L)
- TCE TRICHLOROETHENE
- mg/L MILLIGRAMS PER LITER
- DEWATERED SAPROLITE

NOTES

1. SITE MAP BASED ON FILES PROVIDED BY CDM, INC., MAY 2011.
2. HORIZONTAL DATUM IS SOUTH CAROLINA STATE PLANE, (NAD83, FEET).

FORMER FEDERAL PACIFIC ELECTRIC SITE
EDGEFIELD, SOUTH CAROLINA

2021 2nd SEMIANNUAL AND ANNUAL SUMMARY REPORT

TRICHLOROETHENE DISTRIBUTION - SAPROLITE SEPTEMBER 2021

ARCADIS

FIGURE 7

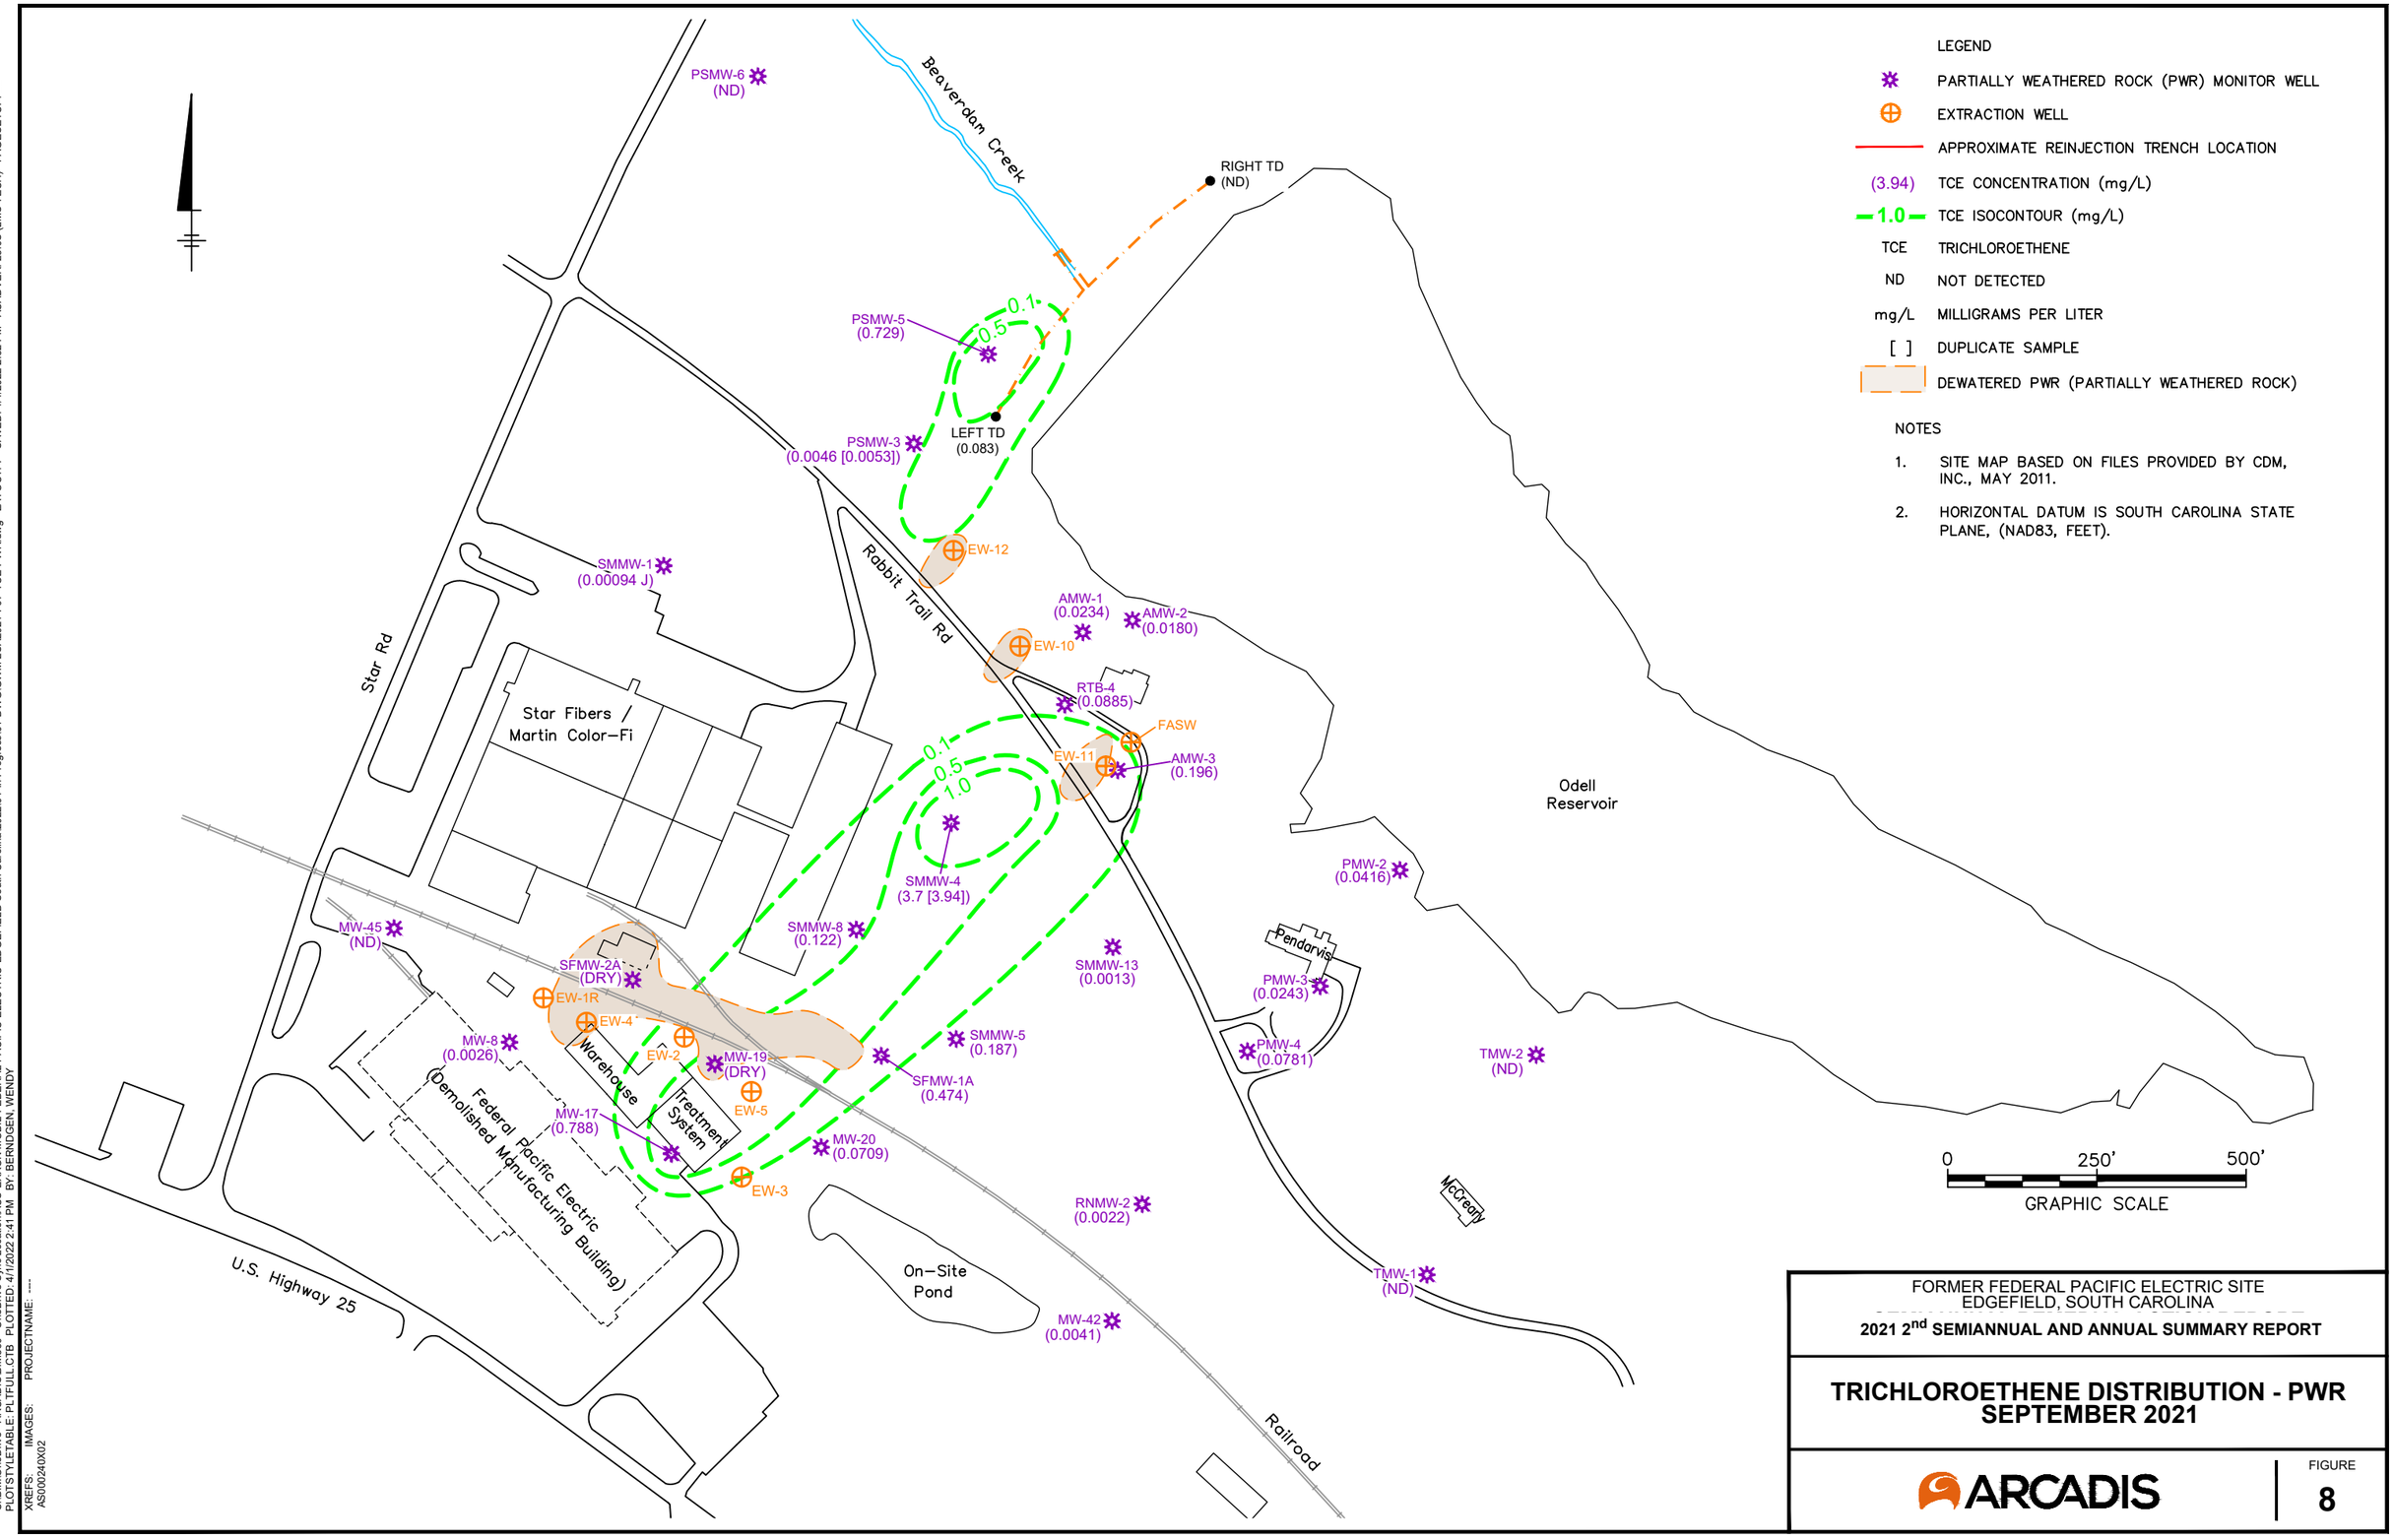

LEGEND

- PARTIALLY WEATHERED ROCK (PWR) MONITOR WELL
- EXTRACTION WELL
- APPROXIMATE REINJECTION TRENCH LOCATION
- (3.94) TCE CONCENTRATION (mg/L)
- 1.0 TCE ISOCONTOUR (mg/L)
- TCE TRICHLOROETHENE
- ND NOT DETECTED
- mg/L MILLIGRAMS PER LITER
- [ ] DUPLICATE SAMPLE
- DEWATERED PWR (PARTIALLY WEATHERED ROCK)

NOTES

1. SITE MAP BASED ON FILES PROVIDED BY CDM, INC., MAY 2011.
2. HORIZONTAL DATUM IS SOUTH CAROLINA STATE PLANE, (NAD83, FEET).

FORMER FEDERAL PACIFIC ELECTRIC SITE
EDGEFIELD, SOUTH CAROLINA

2021 2nd SEMIANNUAL AND ANNUAL SUMMARY REPORT

TRICHLOROETHENE DISTRIBUTION - PWR SEPTEMBER 2021

ARCADIS

FIGURE
8

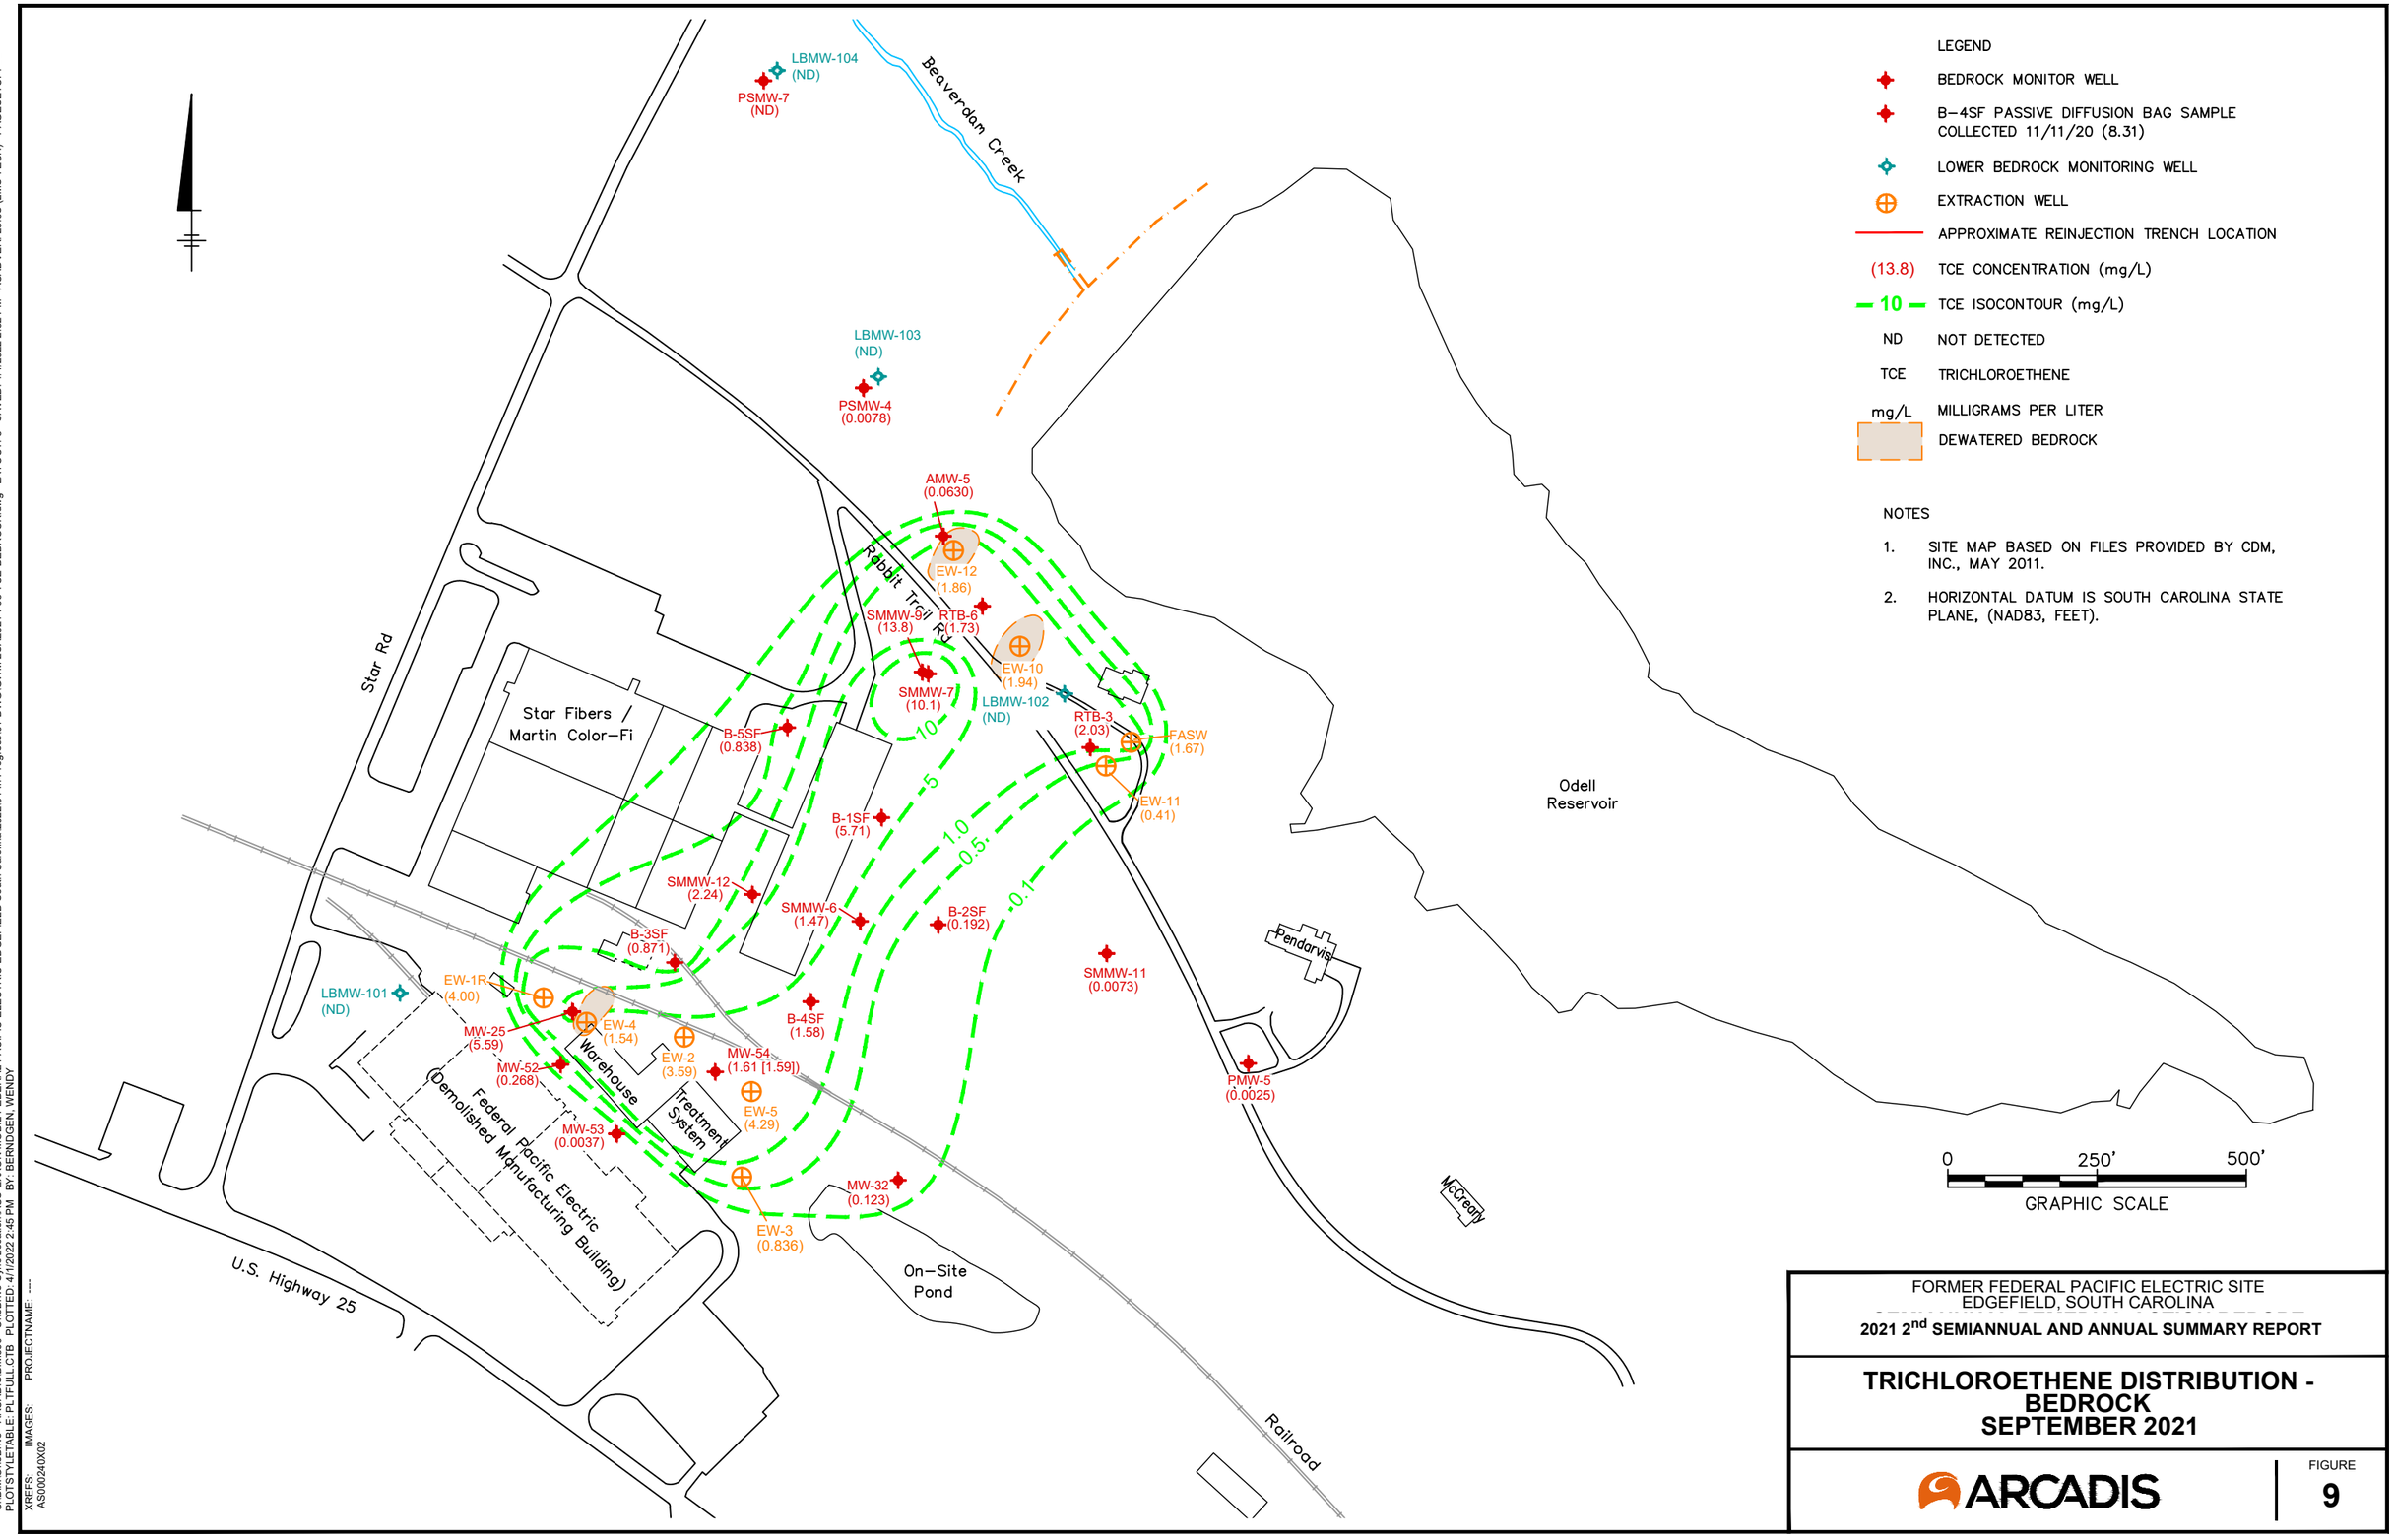

LEGEND

- BEDROCK MONITOR WELL
- B-4SF PASSIVE DIFFUSION BAG SAMPLE COLLECTED 11/11/20 (8.31)
- LOWER BEDROCK MONITORING WELL
- EXTRACTION WELL
- APPROXIMATE REINJECTION TRENCH LOCATION
- (13.8) TCE CONCENTRATION (mg/L)
- 10 TCE ISOCONTOUR (mg/L)
- ND NOT DETECTED
- TCE TRICHLOROETHENE
- mg/L MILLIGRAMS PER LITER
- DEWATERED BEDROCK

NOTES

1. SITE MAP BASED ON FILES PROVIDED BY CDM, INC., MAY 2011.
2. HORIZONTAL DATUM IS SOUTH CAROLINA STATE PLANE, (NAD83, FEET).

FORMER FEDERAL PACIFIC ELECTRIC SITE
EDGEFIELD, SOUTH CAROLINA

2021 2nd SEMIANNUAL AND ANNUAL SUMMARY REPORT

TRICHLOROETHENE DISTRIBUTION - BEDROCK SEPTEMBER 2021

ARCADIS

FIGURE 9

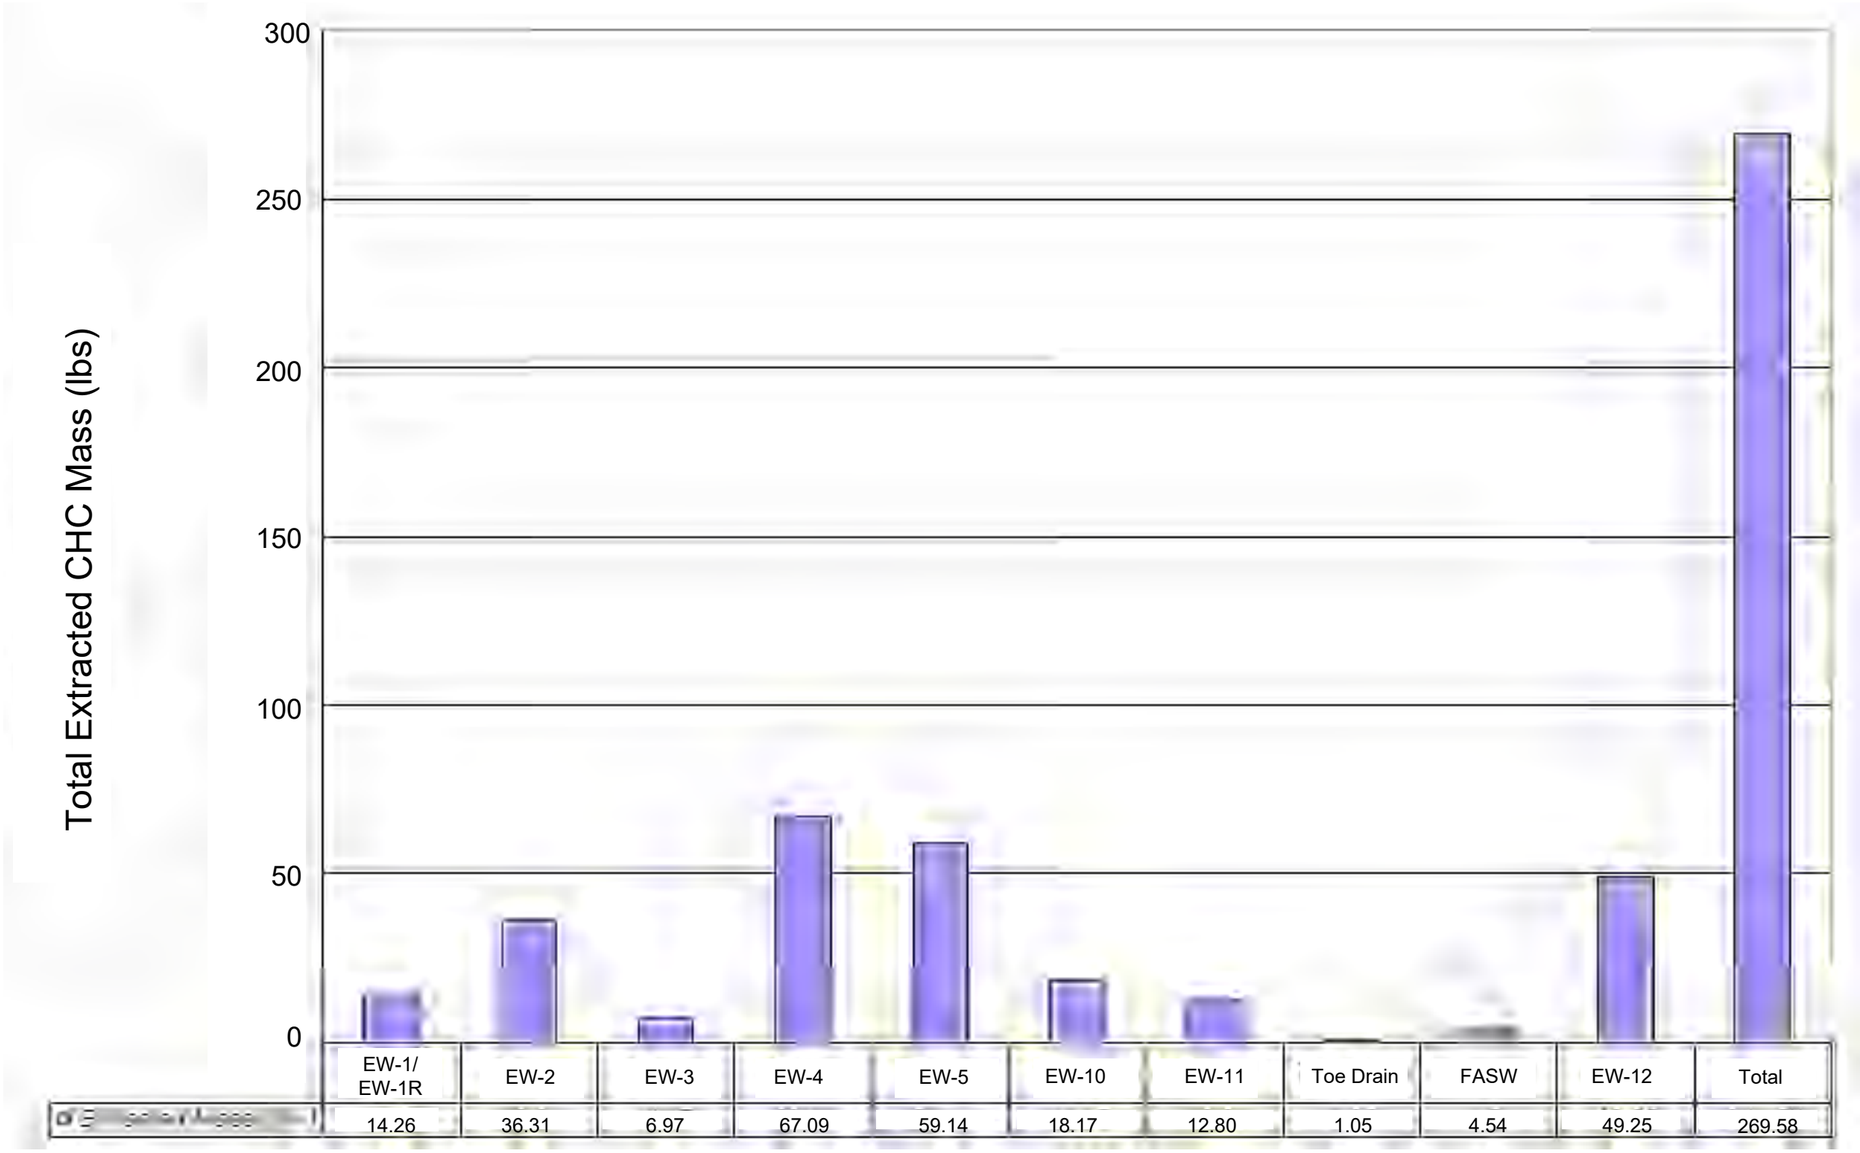

Notes:
1. lbs - Pounds
2. CHC - Chlorinated hydrocarbon

On-site: 183.78 lbs.
Off-site: 84.76 lbs.
Toe Drain: 1.05 lbs.

NewFields
Perspective. Vision. Solutions.
1980 Post Oak Blvd., Suite 227
Houston, Texas 77056
(713) 357-5244

FIGURE 10

TOTAL EXTRACTED CHC MASS
BY WELL: 2021

Former Federal Pacific Site, Edgefield, South Carolina

SEPTEMBER 2004

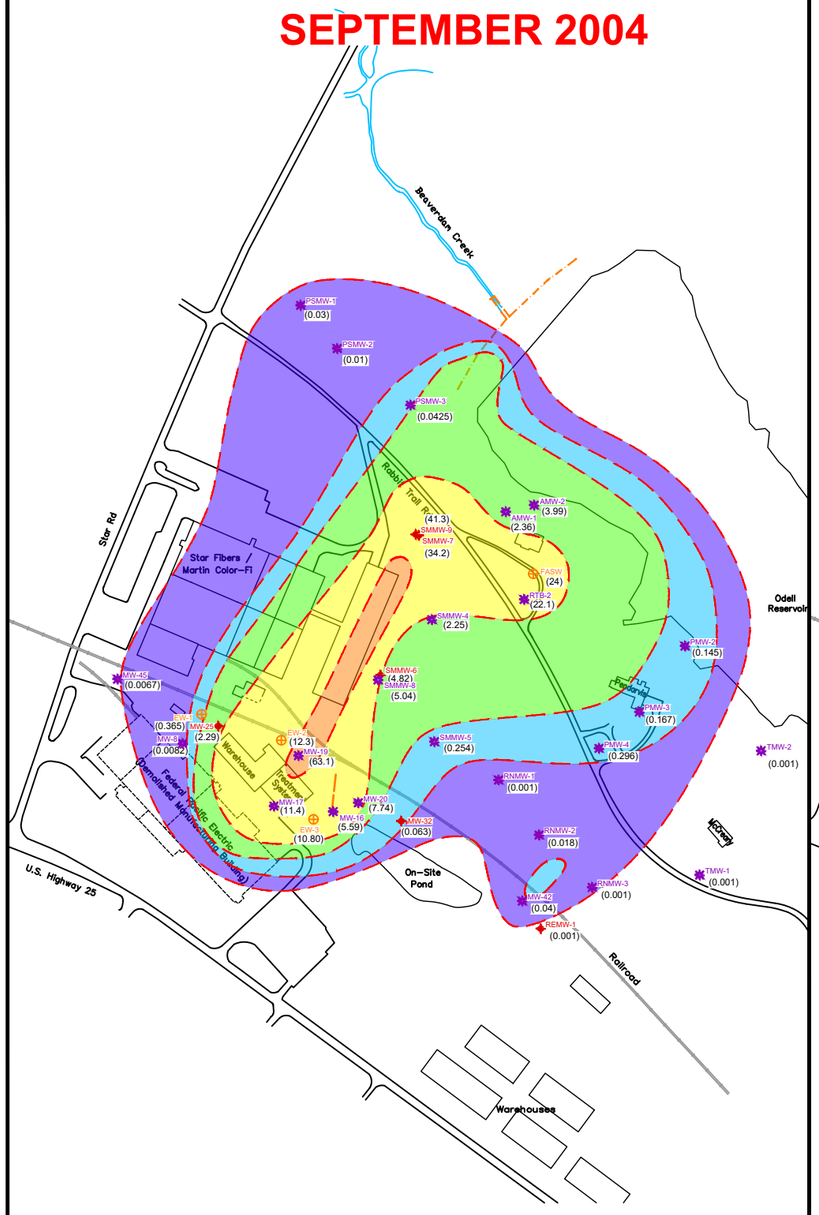

SEPTEMBER 2012

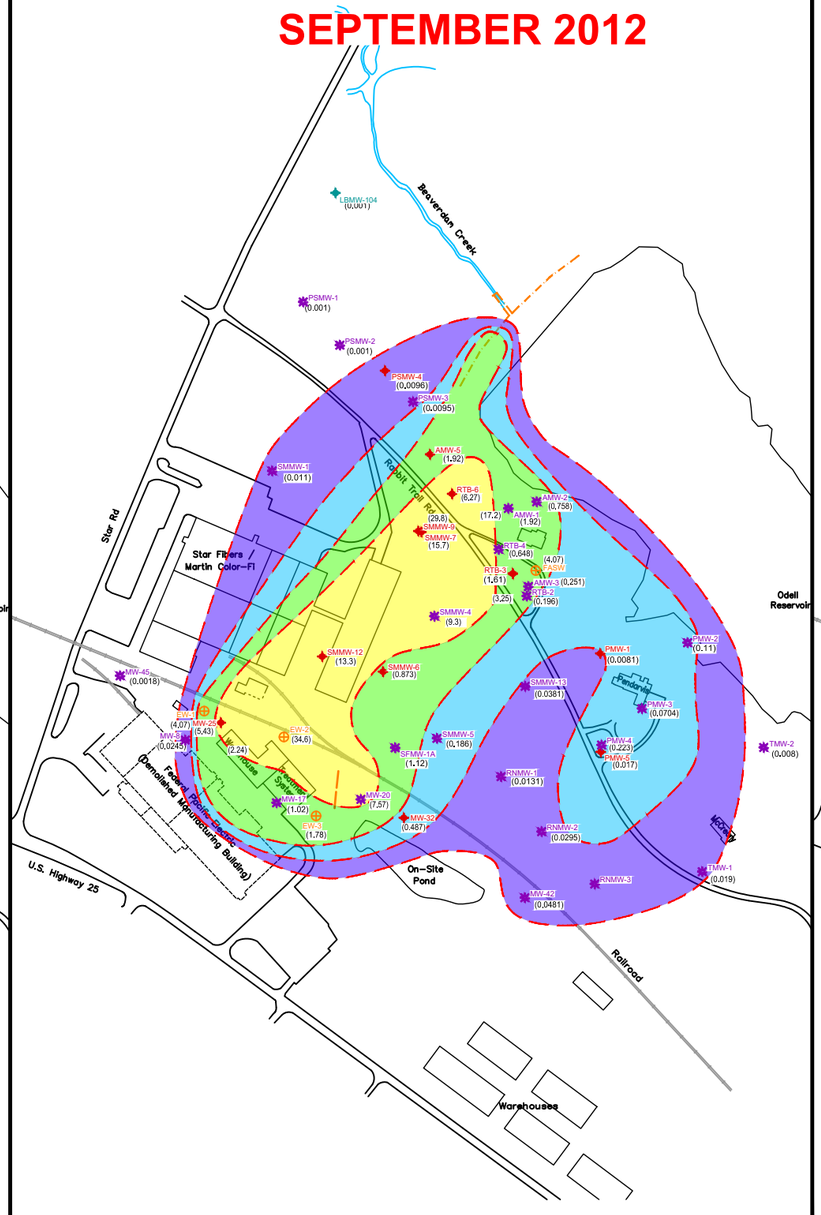

SEPTEMBER 2021

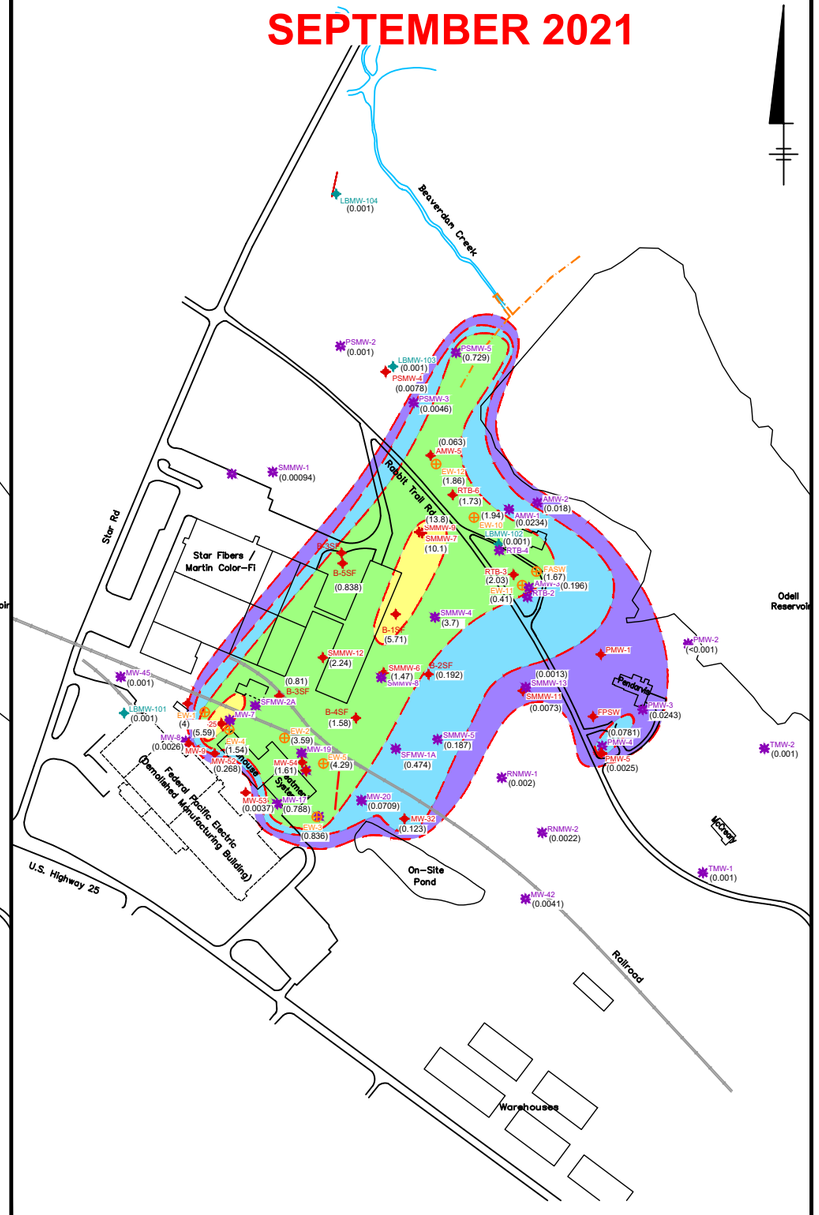

LEGEND

- PARTIALLY WEATHERED ROCK (PWR) MONITOR WELL
- BEDROCK MONITOR WELL
- EXTRACTION WELL
- LOWER BEDROCK MONITORING WELLS

TCE CONCENTRATION (mg/L)

- 0.005 - 0.05
- 0.05 - 0.5
- 0.5 - 5.0
- 5.0 - 50
- +50

NOTES

1. SITE MAP BASED ON FILES PROVIDED BY CDM, INC., MAY 2011.
2. HORIZONTAL DATUM IS SOUTH CAROLINA STATE PLANE, (NAD83, FEET).
3. mg/L = MILLIGRAMS PER LITER.
4. TCE = TRICHLOROETHENE
5. KRIGING VARIGRAM COMPONENTS, LINEAR WITH ANISOTROPY OF RATIO = 1, ANGLE = 0, AND SLOPE = 1.
6. PWR = PARTIALLY WEATHERED BEDROCK.

0 450' 800'

GRAPHIC SCALE

FORMER FEDERAL PACIFIC ELECTRIC SITE
EDGEFIELD, SOUTH CAROLINA

DISSOLVED TRICHLOROETHENE DISTRIBUTION BEDROCK AND PARTIALLY WEATHERED ROCK

ARCADIS

FIGURE 11

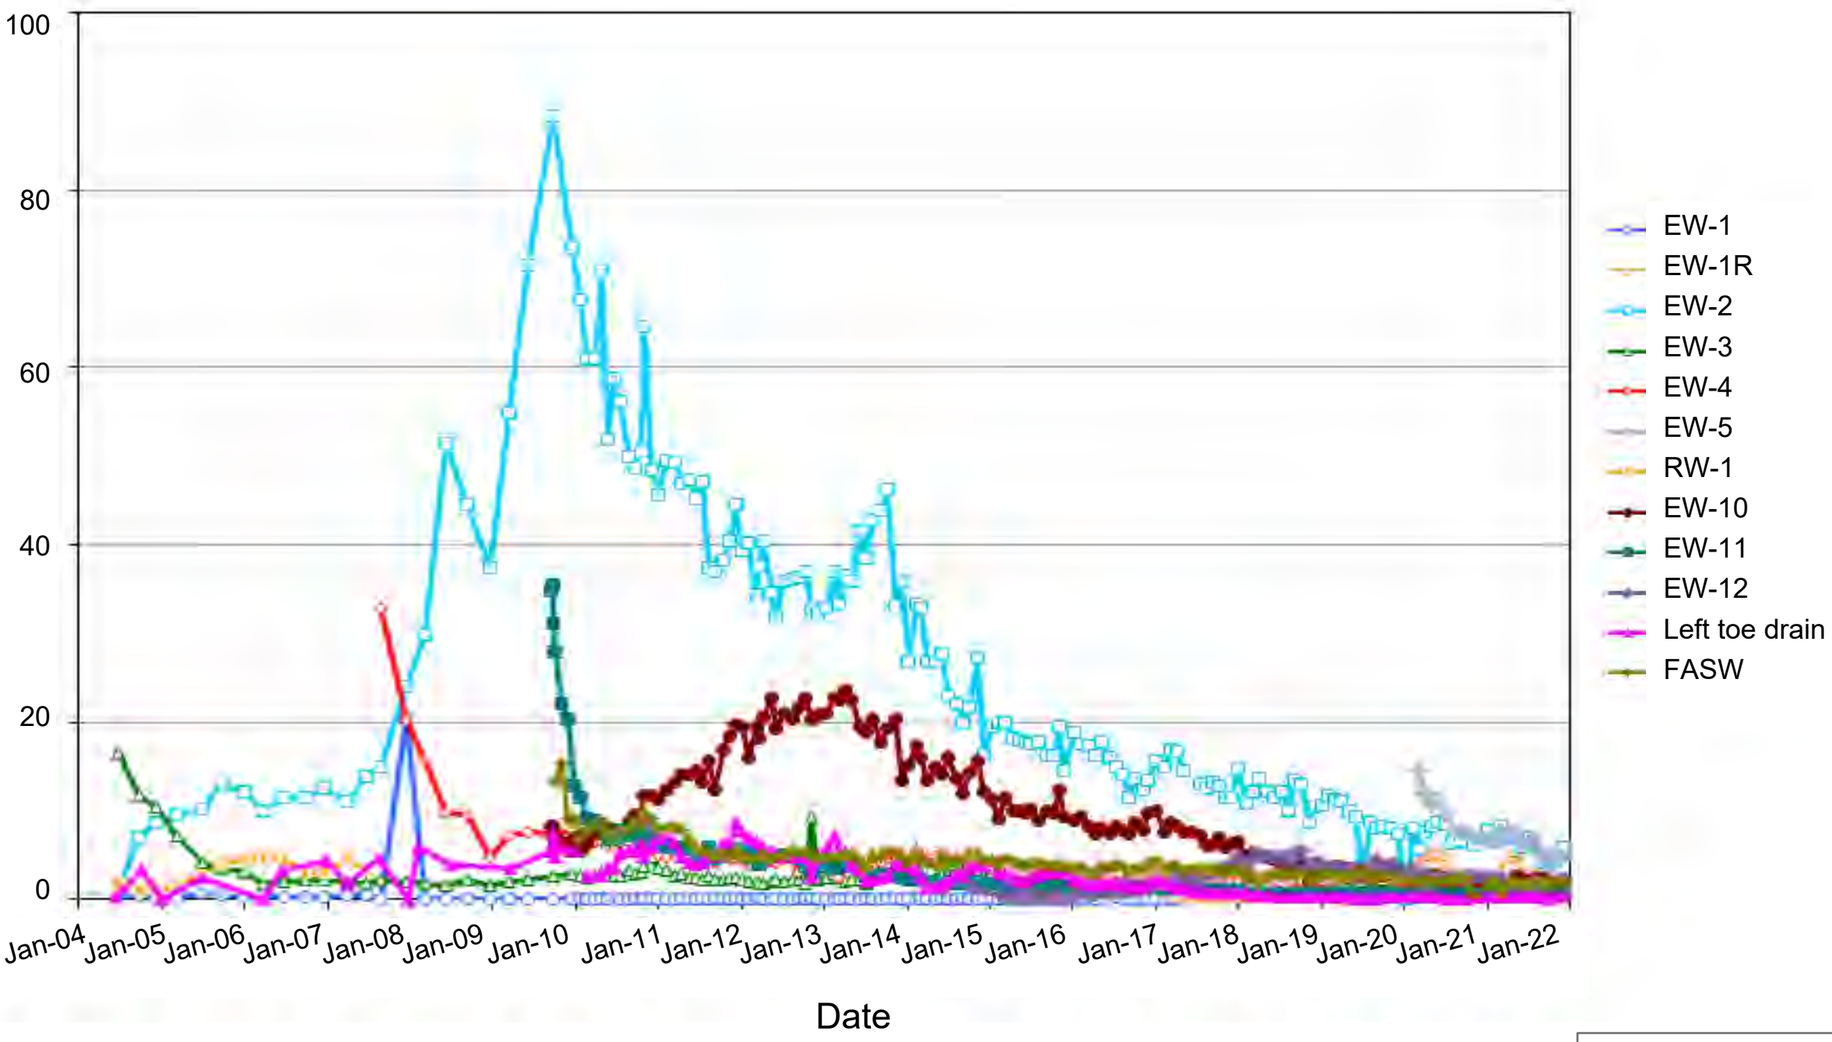

Notes:
1. mg/L - milligrams per Liter
2. CHCs - Chlorinated hydrocarbons

NewFields
Perspective. Vision. Solutions.
1980 Post Oak Blvd., Suite 227
Houston, Texas 77056
(713) 357-5244

FIGURE 12

INFLUENT CHC CONCENTRATION TRENDS
2004-2021

Former Federal Pacific Site, Edgefield, South Carolina

TABLES

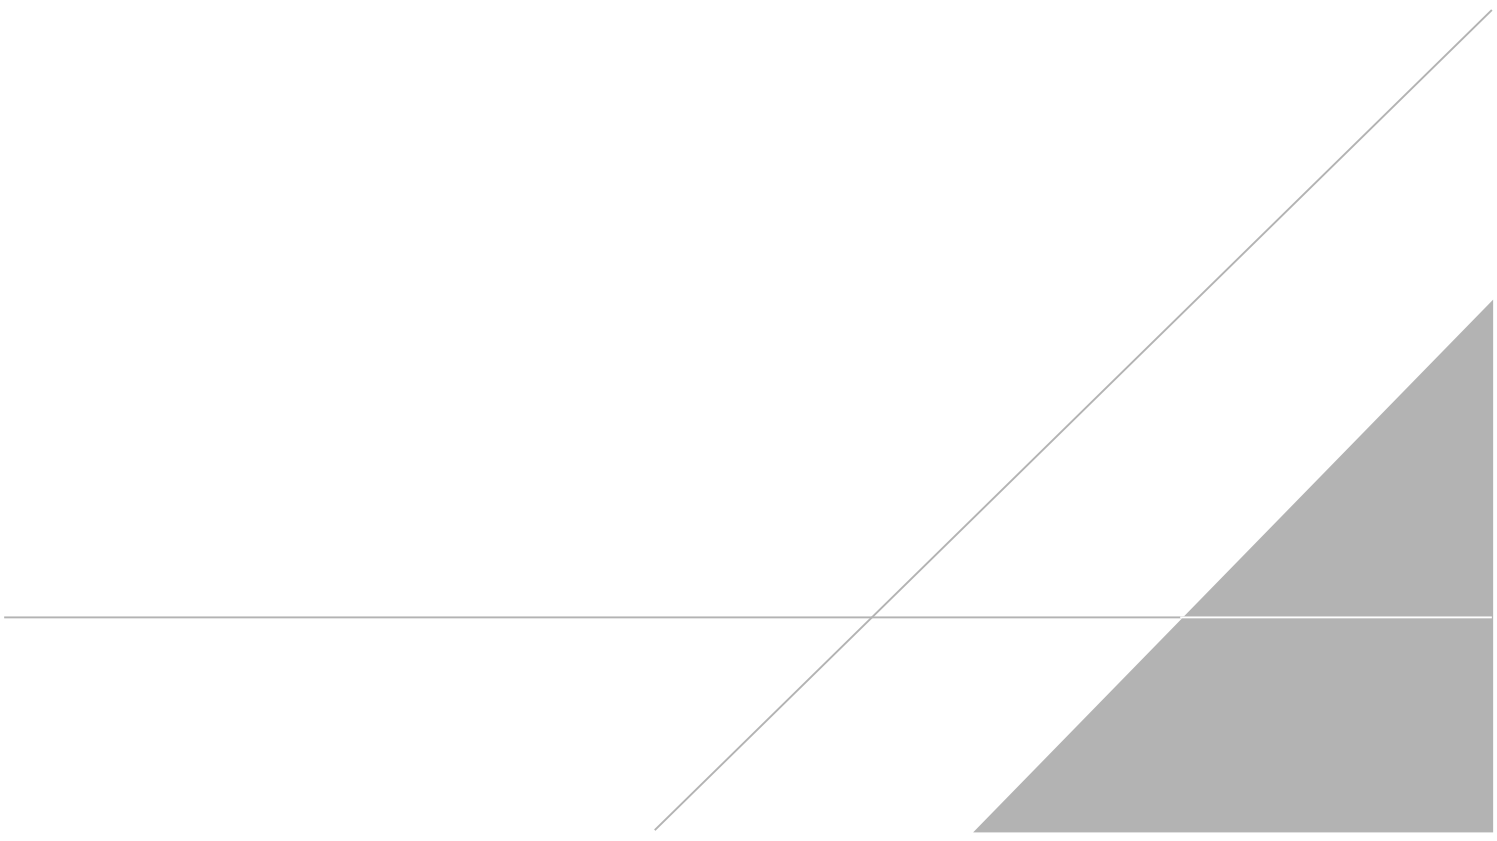

Table 1
2021 Reporting and Regulatory Correspondence
Edgefield, South Carolina
Site ID # 00346

Date	Title	Author
8/21/2021	Semiannual Remedial Action Report - 3Q20-4Q20	ARCADIS
8/23/2021	NPDES permit SC0047813 Notice of Violation AI-0004479	DHEC
9/21/2021	Notice of Alleged Violation/Notice of Enforcement Conference	DHEC
10/8/2021	Annual 2020 Summary Report	ARCADIS
10/21/2021	Enforcement Conference	DHEC/FPE
10/29/2021	Semiannual Remedial Action Report - 1Q21 - 2Q21	ARCADIS
11/8/2021	Semiannual Remedial Action Report - 1Q21 - 2Q21 approval	DHEC
11/23/2021	NOV Supplemental Information	De Maximis
12/10/2021	Comments on Off-Site Saturated Zone Report	DHEC
12/15/2021	Off-Site Saturated Zone Report	ARCADIS
12/17/2021	Sampling and Analysis Plan Revision 1	ARCADIS

Table 2
Groundwater Elevation Gauging Data - 2021
Former Federal Pacific Electric Co.
Edgefield, South Carolina

ARCADIS Design & Consultancy for natural and built assets

Well ID	Well Casing Elevation (ft msl)	March 15, 2021 Groundwater Elevation (ft msl)	June 4, 2021 Groundwater Elevation (ft msl)	September 13, 2021 Groundwater Elevation (ft msl)	December 7, 2021 Groundwater Elevation (ft msl)
AMW-01	524.70	518.86	517.50	517.88	517.34
AMW-02	522.23	519.47	518.70	518.98	518.75
AMW-03	542.25	515.12	514.67	514.88	514.65
AMW-04	541.81	516.11	515.49	NM	NM
AMW-05	536.41	509.79	508.16	507.65	507.13
B-1SF	553.50	NM	NM	NM	522.05
B-2SF	552.13	NM	NM	NM	517.74
B-3SF	554.75	NM	NM	NM	494.26
B-4SF	551.24	NM	NM	NM	477.44
B-5SF	549.35	NM	NM	NM	519.55
EW-1PZ	565.31	545.75	544.68	545.51	543.43
EW-1PRZ	565.44	516.97	512.29	NM	522.97
EW-2PZ	562.44	515.22	519.49	522.55	517.82
EW-3PZ	560.35	538.55	535.00	538.72	535.65
EW-4PZ	566.31	503.02	507.39	489.51	481.81
EW-5	562.05	NM	NM	NM	NM
EW-10PZ	531.91	472.29	472.00	472.02	471.95
EW-11PZ	541.65	487.97	486.86	487.43	488.60
EW-12PZ	532.73	469.73	469.73	466.28	471.34
FASW	541.43	NM	NM	NM	NM
FPSW	539.39	538.96	538.48	539.39	539.28
LBMW-101	566.61	530.14	530.26	525.63	527.27
LBMW-102	540.85	519.51	517.04	511.36	516.59
LBMW-103	524.48	518.89	516.74	516.49	516.08
LBMW-104	508.35	505.73	499.74	503.28	499.92
MW-01	567.44	DRY	DRY	DRY	DRY
MW-02	565.61	DRY	DRY	DRY	DRY
MW-03	565.75	DRY	DRY	DRY	DRY
MW-04	564.61	542.56	540.41	541.68	539.16
MW-05	564.74	542.29	540.20	541.52	538.96
MW-06	564.59	DRY	DRY	DRY	DRY
MW-07	565.63	DRY	DRY	DRY	DRY
MW-08	567.07	530.61	531.88	531.02	528.80
MW-09	567.06	527.94	529.27	527.50	525.29
MW-10	567.24	549.47	NG	DRY	DRY
MW-11	573.14	DRY	DRY	DRY	DRY
MW-12	563.23	DRY	DRY	544.32	DRY
MW-13	564.88	DRY	DRY	DRY	DRY
MW-14	564.01	548.74	NM	DRY	DRY
MW-15	562.03	DRY	DRY	DRY	DRY
MW-17	564.14	538.01	538.51	539.51	537.95
MW-18	559.64	DRY	DRY	DRY	DRY
MW-19	562.77	536.42	NM	DRY	DRY

Table 2
Groundwater Elevation Gauging Data - 2021
Former Federal Pacific Electric Co.
Edgefield, South Carolina

ARCADIS Design & Consultancy for natural and built assets

Well ID	Well Casing Elevation (ft msl)	March 15, 2021 Groundwater Elevation (ft msl)	June 4, 2021 Groundwater Elevation (ft msl)	September 13, 2021 Groundwater Elevation (ft msl)	December 7, 2021 Groundwater Elevation (ft msl)
MW-20	556.61	538.87	537.11	538.07	537.12
MW-23	562.03	DRY	DRY	DRY	DRY
MW-25	566.03	507.13	510.71	498.77	495.80
MW-26	563.02	541.67	539.77	541.09	539.85
MW-27	551.14	540.82	543.50	544.36	543.67
MW-28	565.51	533.53	536.91	537.64	535.97
MW-31	551.39	542.41	540.96	541.01	540.75
MW-32	554.04	539.18	536.75	537.21	537.03
MW-33	551.82	542.53	541.36	540.99	540.70
MW-34	553.78	543.73	542.66	542.22	541.70
MW-42	558.46	545.71	544.46	543.82	544.07
MW-43	561.06	551.26	548.94	549.42	547.90
MW-45	564.24	550.56	548.39	549.01	547.29
MW-46	565.99	555.28	553.32	553.33	551.90
MW-47	565.93	554.79	552.87	552.88	551.43
MW-48	568.60	556.05	554.40	555.30	553.84
MW-49	568.75	561.82	554.57	561.74	553.89
MW-50	569.65	546.88	546.37	546.19	544.95
MW-52	564.42	504.89	508.65	494.45	493.62
MW-53	564.22	533.33	534.38	535.58	534.06
MW-54	563.85	494.05	494.26	493.69	493.90
OW-21	568.24	546.59	546.18	545.99	544.72
OW-29	562.08	551.96	550.74	549.65	548.58
OW-30	565.26	548.89	547.81	546.82	545.89
OW-36	551.51	544.68	543.24	543.45	542.89
OW-37	555.10	NM	NM	NM	546.00
OW-38	557.76	539.22	537.44	538.55	537.56
OW-39	561.91	541.54	NM	NM	540.83
OW-40	561.28	552.88	551.24	550.66	549.55
PMW-01	527.22	523.76	522.44	522.47	522.51
PMW-02	522.76	522.49	522.29	522.76	522.55
PMW-03	539.72	534.41	533.49	533.56	533.23
PMW-04	546.58	538.65	537.52	537.53	537.01
PMW-05	546.55	538.86	537.72	537.70	537.22
PMW-06	531.64	527.31	527.19	527.10	527.11
PMW-07	538.72	Unable to locate	Unable to locate	Unable to locate	Unable to locate
PMW-08	539.36	528.98	528.88	528.85	528.87
PSMW-01	520.24	516.45	512.11	512.76	511.41
PSMW-02	521.25	514.78	510.52	511.51	511.22
PSMW-03	531.53	519.04	517.14	516.81	517.20
PSMW-04	525.30	519.47	517.36	517.48	516.74
PSMW-05	515.34	509.73	508.75	508.86	508.84
PSMW-06	531.64	525.38	522.14	523.51	522.74

Table 2
Groundwater Elevation Gauging Data - 2021
Former Federal Pacific Electric Co.
Edgefield, South Carolina

ARCADIS Design & Consultancy for natural and built assets

Well ID	Well Casing Elevation (ft msl)	March 15, 2021 Groundwater Elevation (ft msl)	June 4, 2021 Groundwater Elevation (ft msl)	September 13, 2021 Groundwater Elevation (ft msl)	December 7, 2021 Groundwater Elevation (ft msl)
PSMW-07	538.72	533.97	530.92	531.87	530.77
PZ1-PWR	561.75	DRY	DRY	537.37	DRY
PZ1-RCK	561.61	DRY	DRY	508.18	DRY
PZ1-S	561.65	538.64	NG	539.12	DRY
PZ2-PWR	561.16	NG	538.83	540.70	539.50
PZ2-RCK	560.94	NG	538.43	540.78	539.55
PZ2-S	561.21	Well Collapsed	Well Collapsed	Well Collapsed	Well Collapsed
REMW-01	559.81	542.91	544.77	544.06	543.21
RNMW-01	544.88	541.16	539.90	539.92	540.51
RNMW-02	557.35	543.87	542.46	542.20	541.43
RNMW-03	559.07	544.76	543.50	542.99	542.09
RTB-02	542.65	516.07	515.68	515.68	515.48
RTB-03	543.06	515.14	514.71	514.86	514.23
RTB-04	542.60	518.70	517.39	517.67	516.60
RTB-06	534.47	518.77	516.68	516.67	515.98
SFMW-01	550.97	DRY	DRY	DRY	DRY
SFMW-01A	551.08	533.26	532.19	531.86	531.20
SFMW-02	557.41	DRY	DRY	DRY	DRY
SFMW-02A	557.58	DRY	DRY	DRY	DRY
SFMW-05	545.45	538.07	NM	535.09	DRY
SFMW-06	545.43	538.77	535.07	536.03	534.33
SFMW-07	547.96	536.37	DRY	DRY	DRY
SMMW-01	544.00	537.15	533.09	534.70	532.35
SMMW-02	553.73	534.41	533.79	534.14	531.49
SMMW-03	543.05	522.36	519.92	519.60	518.22
SMMW-04	554.26	522.18	523.15	522.26	521.28
SMMW-05	550.15	532.42	530.36	529.91	529.42
SMMW-06	554.52	524.38	525.12	523.78	523.32
SMMW-07	542.59	522.39	520.19	519.59	518.33
SMMW-08	554.47	526.29	526.85	525.44	524.79
SMMW-09	542.34	523.29	521.15	520.97	519.74
SMMW-10	533.26	526.77	525.32	525.93	526.04
SMMW-11	540.12	528.78	526.25	526.30	525.89
SMMW-12	555.23	530.66	530.56	529.99	527.03
SMMW-13	540.56	529.12	526.48	526.48	526.03
TMW-01	540.41	536.85	532.57	532.42	530.66
TMW-02	523.88	522.83	522.16	522.39	522.12

Notes:

*=suspect measurement due to historic levels

ft msl = feet relative mean sea level

ft btoc = feet below top of casing

DRY = well was dry at the time of gauging

NM = not measured

Table 3
Summary Surface Water Analytical Results - 2021
Former Federal Pacific Electric Co.
Edgefield, South Carolina

ARCADIS Design & Consultancy for natural and built assets

Monitoring Well	Sample Date	Volatile Organic Compounds (SW-846 8260B)								
		1,1-DCE (µg/L)	1,2-DCE (total) (µg/L)	TCE (µg/L)	PCE (µg/L)	Vinyl Chloride (µg/L)	Chloroform (µg/L)	Carbon Disulfide (µg/L)	Toluene (µg/L)	Acetone (µg/L)
BEAVERDAM CREEK AND ODELL RESERVOIR										
Main Discharge (DDPC)	4/13/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/13/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
Plunge Pool (DDPD10)	4/13/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/13/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
Midpoint	4/13/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/13/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
Star Road	4/13/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/13/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
Upstream	4/13/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/13/2021	Not Sampled (Dry)								
Station 3	4/13/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/13/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
Station 5	4/13/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/13/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
Station 7	4/13/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/13/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
Station 8	4/13/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/13/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
Station 13	4/13/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/13/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND

Notes:

DCE = Dichloroethene

TCE = Trichloroethene

PCE = Tetrachloroethene

ug/L=micrograms/Liter

ND = Not Detected

Only those compounds that were detected in at least one sample above the Practical Quantitation Limit are included on this table.

Table 4
Summary Groundwater Analytical Results - 2021
Former Federal Pacific Electric Co.
Edgefield, South Carolina

ARCADIS Design & Consultancy for natural and built assets

Monitoring Well	Sample Date	Volatile Organic Compounds (SW-846 8260B)								
		1,1-DCE (µg/L)	1,1-DCA (µg/L)	cis-1,2-DCE (µg/L)	trans-1,2-DCE (µg/L)	1,1,1-TCA (µg/L)	TCE (µg/L)	PCE (µg/L)	Vinyl Chloride (µg/L)	Chloroform (µg/L)
FORMER FPE FACILITY										
MW-06	9/9/2021	Not Sampled (Dry)								
MW-07	9/9/2021	Not Sampled (Dry)								
MW-08	9/9/2021	0.72 J	ND	ND	ND	ND	2.6	0.45 J	ND	3.3
MW-14	9/9/2021	Not Sampled (Dry)								
MW-15	9/9/2021	Not Sampled (Dry)								
MW-17	4/10/2021	9.8 J	ND	5.6 J	ND	ND	387	14.3	ND	ND
	9/10/2021	14.8	ND	9.3 J	ND	ND	788	31.2	ND	ND
MW-19	4/10/2021	Not Sampled (Dry)								
	9/9/2021	Not Sampled (Dry)								
MW-20	9/9/2021	ND	ND	11.8	0.38 J	ND	70.9	ND	ND	3.4
MW-23	9/9/2021	Not Sampled (Dry)								
MW-25	4/10/2021	ND	ND	ND	ND	ND	3680	ND	ND	ND
	9/8/2021	ND	ND	2030	ND	ND	5590	ND	ND	ND
MW-26	9/9/2021	ND	ND	0.31 J	ND	ND	3.7	ND	ND	ND
MW-27	9/9/2021	ND	ND	1.7	ND	ND	5.9	ND	ND	ND
MW-28	4/10/2021	ND	ND	ND	ND	ND	157	10.6	ND	ND
	9/10/2021	10.6	ND	4.1 J	ND	ND	525	26.0	ND	ND
MW-32	9/9/2021	0.67 J	ND	108	ND	ND	123	ND	2.8	ND
MW-33	9/8/2021	ND	ND	1.2	ND	ND	ND	ND	ND	ND
MW-42	9/8/2021	ND	ND	ND	ND	ND	4.1	ND	ND	ND
MW-45	9/8/2021	1.3	ND	ND	ND	ND	ND	ND	ND	ND
MW-52	4/10/2021	ND	ND	39	ND	ND	207	1.5 J	ND	ND
	9/10/2021	ND	ND	52.7	ND	ND	268	7.1	ND	ND
MW-53	4/10/2021	20.9	0.47 J	ND	ND	ND	22.2	2.4	ND	0.51 J
	9/10/2021	9.4	ND	ND	ND	ND	3.7	ND	ND	ND
MW-54	4/10/2021	17.7 J	ND	84.9	ND	ND	1,380	54.1	ND	ND
	9/10/2021	22.7 J [22.3]	ND [ND]	162 [158]	ND [ND]	ND [ND]	1610 [1,590]	66.9 [70.0]	ND [ND]	ND [ND]
LBMW-101	9/7/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
STAR FIBERS/MARTIN										
B-1SF	9/9/2021	ND	ND	773	ND	ND	5710	ND	ND	ND
B-2SF	9/9/2021	1.9 J	ND	21.2	ND	ND	192	0.80 J	ND	8.7
B-3SF	9/10/2021	ND	ND	126	ND	ND	871	ND	ND	ND
B-4SF	9/9/2021	ND	ND	93.6	ND	ND	1580	ND	ND	ND
B-5SF	9/10/2021	ND	ND	66.9	ND	ND	838	ND	ND	ND
SMMW-01	9/7/2021	ND	ND	ND	ND	ND	0.94 J	ND	ND	1.1
SMMW-02	4/7/2021	ND	ND	6.3	ND	ND	29.2	ND	ND	ND
	9/8/2021	ND	ND	28.2	ND	ND	629	ND	ND	ND
SMMW-03	4/7/2021	ND	ND	52.4	ND	ND	295	2.5 J	ND	ND
	9/8/2021	2.0 J	ND	53.5	ND	ND	276	ND	ND	ND
SMMW-04	4/9/2021	ND	ND	645	ND	ND	4,690	ND	ND	ND
	9/9/2021	ND	ND	488	ND	ND	3,940	ND	ND	ND
SMMW-05	9/8/2021	ND	ND	60.9	ND	ND	187	ND	ND	ND

Table 4
Summary Groundwater Analytical Results - 2021
Former Federal Pacific Electric Co.
Edgefield, South Carolina

ARCADIS Design & Consultancy for natural and built assets

Monitoring Well	Sample Date	Volatile Organic Compounds (SW-846 8260B)								
		1,1-DCE (µg/L)	1,1-DCA (µg/L)	cis-1,2-DCE (µg/L)	trans-1,2-DCE (µg/L)	1,1,1-TCA (µg/L)	TCE (µg/L)	PCE (µg/L)	Vinyl Chloride (µg/L)	Chloroform (µg/L)
SMMW-06	4/9/2021	ND	ND	64.0	ND	ND	1,120	ND	ND	9.2 J
	9/9/2021	ND	ND	69.0	ND	ND	1470	ND	ND	ND
SMMW-07	4/7/2021	ND	ND	2,040	ND	ND	9,680	ND	ND	ND
	9/8/2021	ND	ND	2,180	ND	ND	10,100	ND	ND	ND
SMMW-08	9/9/2021	ND	ND	9.3	ND	ND	122	0.44 J	ND	5.6
SMMW-09	4/7/2021	ND	ND	2,140	ND	ND	14,500	ND	ND	ND
	9/8/2021	ND	ND	2,060	ND	ND	13,800	ND	ND	ND
SMMW-10	9/7/2021	ND	ND	4.0	ND	ND	1.2	ND	ND	0.47 J
SMMW-11	4/8/2021	0.61 J	0.50 J	65.5	0.35 J	ND	8.3	ND	12.4	ND
	9/7/2021	ND	ND	20.0	ND	ND	7.3	ND	ND	ND
SMMW-12	4/7/2021	ND	ND	209	ND	ND	1660	ND	ND	ND
	9/8/2021	ND	ND	216	ND	ND	2240	ND	ND	ND
SMMW-13	9/7/2021	ND	0.55 J	26.6	ND	ND	1.3	ND	ND	ND
SFMW-01A	9/8/2021	ND	ND	20.3	ND	ND	474	ND	ND	ND
SFMW-02A	4/7/2021	Not Sampled (Dry)								
	9/8/2021	Not Sampled (Dry)								
AMW-01	9/10/2021	ND	ND	7.3	ND	ND	23.4	ND	ND	ND
AMW-02	4/8/2021	ND	ND	3.5 [3.5]	ND	ND	12.9 [12.7]	ND	ND	ND
	9/10/2021	ND	ND	6.5	ND	ND	18.0	ND	ND	ND
AMW-03	4/9/2021	1.8 J	ND	48.1	ND	ND	202	ND	ND	ND
	9/10/2021	1.2 J	ND	35.5	ND	ND	196	ND	ND	ND
AMW-05	4/9/2021	4.8	2.9	10.6	ND	ND	97.3	ND	ND	ND
	9/10/2021	7.2	4.1	7.1	ND	ND	63.0	ND	0.56 J	ND
PMW-02	4/7/2021	ND	ND	1.2	ND	ND	41.6	ND	ND	ND
PMW-03	9/9/2021	ND	ND	0.53 J	ND	ND	24.3	ND	ND	ND
PMW-04	4/7/2021	ND	ND	29.0	ND	ND	73.0	ND	ND	ND
	9/9/2021	ND	ND	23.3	ND	ND	78.1	ND	ND	ND
PMW-05	9/9/2021	ND	ND	0.50 J	ND	ND	2.5	ND	ND	ND
PSMW-02	9/7/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
PSMW-03	9/9/2021	ND	ND	0.64 J	ND	ND	4.6	ND	ND	ND
PSMW-04	4/8/2021	ND	ND	1.1	ND	ND	17.3	ND	ND	ND
	9/9/2021	ND	ND	0.45 J	ND	ND	7.8	ND	ND	0.41 J
PSMW-05	4/8/2021	ND	ND	113 [118]	ND	ND	777 [868]	ND	ND	ND
	9/10/2021	ND	ND	122	ND	ND	729	ND	ND	ND
PSMW-06	9/7/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
PSMW-07	9/7/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
RNMW-01	9/7/2021	ND	ND	ND	ND	ND	2.0	ND	ND	ND
RNMW-02	9/7/2021	ND	ND	ND	ND	ND	2.2	ND	ND	ND
RTB-03	9/10/2021	ND	ND	469	ND	ND	2030	ND	ND	ND
RTB-04	9/10/2021	ND	ND	10.6	ND	ND	88.5	0.43 J	ND	ND
RTB-06	4/8/2021	ND	ND	196	ND	ND	1,540	ND	30.9	ND
	9/10/2021	11.4 J	ND	219	ND	ND	1730	ND	29.6	ND
TMW-01	9/10/2021	ND	ND	ND	ND	ND	ND	ND	ND	0.57 J

Table 4
Summary Groundwater Analytical Results - 2021
Former Federal Pacific Electric Co.
Edgefield, South Carolina

ARCADIS Design & Consultancy for natural and built assets

Monitoring Well	Sample Date	Volatile Organic Compounds (SW-846 8260B)								
		1,1-DCE (µg/L)	1,1-DCA (µg/L)	cis-1,2-DCE (µg/L)	trans-1,2-DCE (µg/L)	1,1,1-TCA (µg/L)	TCE (µg/L)	PCE (µg/L)	Vinyl Chloride (µg/L)	Chloroform (µg/L)
TMW-02	9/10/2021	ND	ND	ND	ND	ND	ND	ND	ND	0.61 J
LBMW-102	4/9/2021	ND	ND	4.9	ND	ND	1.3	ND	2.0	ND
	9/7/2021	ND	ND	1.7	ND	ND	ND	ND	1.2	ND
LBMW-103	9/8/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
LBMW-104	9/7/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND
R Toe Drain	4/13/2022	ND	ND	1.7	ND	ND	3.2	ND	1.3	ND
	9/16/2021	ND	ND	2.7	ND	ND	6.7	ND	ND	ND
L Toe Drain	4/13/2022	1.3	ND	58.8	ND	ND	182	ND	4.8	ND
	9/16/2021	ND	ND	60.7	ND	ND	96.1	ND	9.0	ND

Notes:

[118] = Duplicate sample
DCE = Dichloroethene
DCA = Dichloroethane
PCE = Tetrachloroethene
ug/L=micrograms/Liter
TCA = Trichloroethane
TCE = Trichloroethene
ND = Not Detected
R = Right
L = Left

Only those compounds that were detected in at least one sample above the Practical Quantitation Limit are included on this table.

Table 5
Groundwater Recovery Volumes - 2021
Former Federal Pacific Electric Co.
Edgefield, South Carolina

ARCADIS Design & Consultancy for natural and built assets

	On-Site Recovery System						Off-Site Recovery System					
Reporting Period	**EW-1R**	**EW-2**	**EW-3**	**EW-4**	**EW-5**	**Total Recovered Groundwater (gallons)**	**EW-10**	**EW-11**	**EW-12**	**FASW**	**Toe Drain**	**Total Recovered Groundwater (gallons)**
January-21	44,769	54,202	63,514	75,089	96,723	334,297	81,921	263,887	198,348	19,383	68,273	631,812
February-21	49,211	64,915	65,526	342,133	93,742	615,527	83,144	265,231	218,137	19,102	66,875	652,489
March-21	63,540	47,520	46,062	402,798	119,758	679,678	66,946	208,516	289,946	4,717	41,007	611,132
April-21	51,593	60,480	48,172	315,058	97,258	572,561	85,931	274,042	224,949	1,828	44,727	631,477
May-21	50,904	59,184	59,910	295,490	97,365	562,853	81,298	272,301	227,836	2,257	39,990	623,682
June-21	65,760	64,800	96,756	391,473	119,239	738,028	97,576	335,717	274,846	6,499	50,407	765,045
July-21	26,423	73,440	32,404	362,359	100,100	594,726	49,270	128,540	134,703	9,798	35,792	358,103
August-21	35,762	72,288	35,725	901,855	81,534	1,127,164	64,380	213,884	182,223	6,439	48,888	515,814
September-21	42,364	69,840	56,009	440,294	102,173	710,680	82,741	269,224	248,053	7,423	42,569	650,010
October-21	40,776	70,848	63,010	433,440	166,292	774,366	83,613	275,607	253,217	8,665	56,549	677,651
November-21	36,225	62,704	82,896	423,504	94,406	699,735	79,889	257,402	118,558	29,168	46,866	531,883
December-21	44,340	70,128	65,103	428,544	99,849	707,964	84,566	229,299	267,840	28,352	65,177	675,234
Totals:	551,667	770,349	715,087	4,812,036	1,268,439	8,117,578	941,275	2,993,650	2,638,656	143,631	607,120	7,324,332

Total Recovered Groundwater All Recovery Systems (Gallons) = 15,441,910

Notes:
EW=extraction well

APPENDIX A

Groundwater Recovery/Treatment System Operating and Monitoring Data

Appendix A Table 1
Cumulative Summary of Treatment System Downtime
FPE Groundwater Treatment System
Edgefield, South Carolina

Dates	Cause	Actions Taken
6/30/04 - 7/2/04	**Power Outage**: when power came back on for the system, the low pressure alarm for the air stripper blower was triggered. This shut down the influent equalization tank transfer pumps, and once the high level in the influent tank was reached, the extraction well pumps were shut down.	An automatic reset was programmed for the air stripper blower so that when a power outage occurs, the blower attempts to restart automatically before an alarm is triggered.
Effluent to ACPSA/ Trenches	**PLC Failure**: some condensate formed inside an electrical conduit and dripped onto one of the PLC modules, causing the module to fault and produce erroneous readings.	The conduit ends within the data control center were modified with drains so that no water can fall onto the electrical components of the control center.
	No significant downtime	
	No significant downtime	
	RW-1: a break was experienced where the extraction line connected to the well casing. A small amount of water (< 50 gallons) was lost from this line (underground) before the problem was diagnosed.	Repairs were made to the connection between the extraction line and the well casing. The well has been operating normally since the repairs.
5/1/05 - 7/31/05	No significant downtime	
8/1/05 - 10/31/05	No significant downtime	
11/1/05 - 1/31/06	No significant downtime	
2/1/06 - 4/30/06	No significant downtime	
7/16/06 - 7/17/06	**Power Outage**: the system was down for two days, and the downtime is believed to be associated with a power outage from a thunderstorm. The system did not properly reset when power was restored.	Further action has not been taken at this time since the automatic reset is currently functioning properly. CDM will continue to monitor the system closely.
10/19/06 - 10/22/06	**Sump Alarm**: the system was down for approximately four days due to inadvertently tripping the high-high level switch on the floor sump while transferring purge water from sampling activities. The autodialer did not call out when this occurred. The system was reset when the operator made his next visit to the site.	A contactor was replaced in the sump control panel. The sump pumps are now functioning normally, and the autodialer properly calls out when the high-high level switch is tripped.
1/21/07 - 2/12/07	**RW-1**: the extraction well pump stopped working due to a problem with the motor.	The motor was replaced on February 12, 2007, and the well is now operating normally.
4/10/2007	**Multi-media filter**: a small leak was discovered on a gasket line access port (side of filter) for one of the three multi-media filters.	The filter was taken off line, and extracted groundwater was rerouted through one of the two other filters.
7/17/07 - 7/23/07	**RW-1** was taken offline on July 17, 2007, and **EW-4** was started in its place on July 23, 2007.	This replacement was planned and not related to a problem with the treatment system.
8/1/07 - 10/31/07	No significant downtime	
1/10/2008	**EW-1**: Lower than normal extraction rates were observed for this well in late December.	The well pump and down-hole piping was replaced on January 10, 2008.
2/1/08 - 4/30/08	No significant downtime	
5/1/08 - 7/31/08	No significant downtime	
10/15/08 - 10/27/08	**EW-1**: offline due to pump failure	The well pump was replaced on October 27, 2008.
10/27/08 - 11/7/08	**EW-2**: offline due to pump failure	The well pump was replaced on November 7, 2008.
11/8/08 - 1/31/09	No significant downtime	
2/1/09 - 4/30/09	No significant downtime	

Appendix A Table 1
Cumulative Summary of Treatment System Downtime
FPE Groundwater Treatment System
Edgefield, South Carolina

Dates	Cause	Actions Taken
7/15/2009	Extraction wells turned off to allow tie-in of piping for the new offsite conveyance system.	No action necessary. System was restarted on July 16, 2009.
8/1/09 - 10/31/09	No significant downtime	
1/14/2010	**Sump Alarm**: the high level switch was accidentally tripped during carbon drum backwashing. The condition was brief and returned to normal before the autodialer called out. However, once tripped, all extraction wells and the treatment system turned off until they were manually reset.	A 10-minute delay has been programmed into the floor sump high level alarm. If the switch is accidentally tripped and then returns to normal within 10 minutes, no system shutdowns occur. CDM also tested the autodialer to ensure it was functioning properly.
2/9/2010	**Influent Tank High Level**: For a brief period, the incoming flow to the influent tank was higher than the outgoing flow, and the high level switch tripped. This caused all the extraction wells to shutdown until they could be manually reset.	The transfer pumps were not pumping at full capacity, and CDM has made programming modifications to prevent this event from happening again.
2/19/2010	**Air Stripper Blower Failure**: a suspected electrical surge caused the air stripper blower to shutdown.	The electrical setup was reviewed and confirmed to be ok. The blower has been monitored since this event, and the problem has not reoccurred.
3/3/10 - 3/5/10	**EW-10**: hose inside well became dislodged.	Hose connection to hard piping was repaired.
6/6/10 - 6/28/10	**EW-1**: offline due to pump failure	The well pump was replaced on June 28, 2010.
7/8/10 - 7/12/10	**EW-11**: offline due to pump failure	Troubleshooting revealed that some wiring inside the well electrical box needed to be repaired. This was done on Monday, July 12th.
8/19/2010	**Air Stripper High Level**: The air stripper level indicator malfunctioned, reporting erroneous high level readings to the control panel. This caused all the extraction wells to shutdown for a brief period.	The problem was corrected and the system was restarted within four hours of the extraction wells shutdown.
12/10/10 - 12/14/10	**EW-4**: offline to fix a minor leak at the wellhead	The small leak was fixed and EW-4 was put back online on 12/14/10.
12/15/10 - 12/30/10	**Modem Failure**: The offsite system communications modem failed. The offsite wells and toe drain pumps continued to function normally, but offsite performance data were not transferred to the main system computer in this period.	A new modem was installed on 12/30/10.
2/11/11 - 2/12/11	**Power outage:** The treatment system was without power for approximately 10 hours due to a car crash that damaged a power pole adjacent to the site.	Once power was restored, the system was reset and began functioning normally again.
2/23/2011	**EW-10:** low pumping rate and consequent high water level	Opened diaphragm valve wide open; cycled pump; pump issue resolved and well adjusted to 3.5 gpm
3/29/2011	**Agency inspections:** ACPSA collect effluent sample; Edgefield Water & Sewer on site to read meter	ARCADIS split effluent samples with ACPSA
4/5/2011	**Power outage:** Toe drain recovery system was without power for approximately 12 hours due to downed power lines along Rabbit Trail Rd.	Began arranging backup power source for toe system; power restored at approximately 1530 hrs; system back online; reset autodialer; notified SCDHEC of system upset and ~90 gallon of untreated toe drain influent escaped to Beaver Dam Creek.

Appendix A Table 1
Cumulative Summary of Treatment System Downtime
FPE Groundwater Treatment System
Edgefield, South Carolina

Dates	Cause	Actions Taken
4/10/2011	**Power outage:** storm in early AM caused short term power outage; influent and EW-4 pumps not reset automatically	Reset influent and EW-4 pumps; cleared all alarms; reset autodialer
4/22/2011	**Influent and EW-4 pump failure:** storm in early AM caused short term power outage; pumps not reset automatically	Reset influent and EW-4 pumps; cleared all alarms; reset autodialer
6/9/2011	**Recovery well EW-10 failure:** decrease in pumping rate over several days and ultimate failure	Replace bad pump/motor assembly
8/14/2011	**Power outage - short term**	computer UPS failed resulting in no data logging for ~ 8 hrs; replaced UPS 8/16
8/30/2011	**EW-4 pump failure alarm:** short term power outage; pump not reset automatically	Reset EW-4 pump; cleared alarm; reset autodialer
9/10/2011	**SCADA communication failure to offsite wells:**	Manually reset modem several times before repairs made to main phone line by AT&T
9/16/2011	**Air stripper filter alarm:** aged and clogged filter	Removed/cleaned/re-install filter; cleared alarm; reset autodialer
9/22/2011	**Toe drain effluent line moisture sensor alarm:** no moisture, sensor bad	Replaced sensor
10/4/2011	**SCADA communication failure to offsite wells:**	Remotely reset modem several times before repairs made to main phone line by AT&T
10/17/2011	**EW-4 pump failure alarm:** short term power outage; pump not reset automatically	Reset EW-4 pump; cleared alarm; reset autodialer
10/30/2011	**SCADA communication failure to offsite wells**	Remotely reset modem
11/1/2011	**Toe Drain sump influent line:** reduced flow from iron fouling	Opened and cleaned TD sump and influent lines
11/3/2011	**Alarm: Toe drain alarm**	Replaced leak detection sensor on toe drain piping
11/17/2011	**EW-1 Level Probe failure**	Replace level probe
11/22/2011	**Recovery well EW-11 pump failure;** pump and motor failure	Purchased/installed new pump/motor/piping - 12/13/11 (well down for 20 days)
12/1/2011	**Elevated GAC drum backpressure** **EW-2 Level Probe failure**	Replace GAC drums; Replace level probe
12/4-7/11	**Toe drain effluent line moisture sensor alarm:** no moisture	Cleaned sensor probe
1/5/2011	**Toe Drain Backup Power Supply:** grid power outages	Installed back-up generator on 12/20/11 and put on line 1/5/12
1/31/2012	**Toe Drain Pumps:** decreased pumping rates	Purchased and installed replacement pumps
2/29/2012	**System Backwash Sludge Tank:** full	Removed ~3,000 gal iron/water via vac truck and transport/dispose at EQ Augusta
3/2/2012	**Alarm:** for pipe leak; sensor wet from heavy rain. **Alarm:** for filter trouble, preset on.	Preset on.
3/5/2012	**Alarm:** Rabbit Trail power failure.	On.
4/1/2012	**Alarm:** Toe Drain pipe leak, caused by heavy rain.	On.
4/17/2012	Well EW-11 shut off.	Testing
4/19/2012	FASW off.	Testing
4/24/2012	Shut down EW-10 at 1310. Restart EW-11 at 1510 and shut down at 1715.	Testing
4/29/2012	**Security Alarm:** Unknown	Reset alarm, inspect system
6/1/2012	**Backwash Filter Alarm:** PLC fault	Adjust solenoid, reset alarm and restarted system
6/22/2012	**Backwash Filter Alarm:** PLC fault	Adjust solenoid, reset alarm and restarted system

Appendix A Table 1
Cumulative Summary of Treatment System Downtime
FPE Groundwater Treatment System
Edgefield, South Carolina

Dates	Cause	Actions Taken
6/24/2012	**FASW Failure Alarm**: and filter tank leak.	Reset alarm, fixed leak on filter tank, and inspect system
7/13/2012	**FASW Failure Alarm**: and filter tank leak.	Reset alarm, fixed leak on filter tank, and inspect system
7/18/2012	**Alarm:** Rabbit Trail power failure and filter system problem.	Checked system, drained influent tank, reset alarm, and system restart.
7/19/2012	**Alarm:** Rabbit Trail power failure and filter system problem.	Checked system, drained influent tank, reset alarm, and system restart.
7/30/2012	**Alarm:** Rabbit Trail power failure and filter system problem.	Reset alarm and restarted backwash filter
7/31/2012 to 8/2/2012	**Alarm:** EW-10 fail	Reset Pump
8/21/2012	**All onsite recovery wells down**	Auto system reset and wells back on line after 2 hours
10/27/2012 to 11/3/2012	**Alarm:** Rabbit Trail power failure. EW-10 and EW-11 down.	Reset alarm and pump restart. Repair off-site system PLC and reset EW-3 magnetic flow meter (11/3/12)
11/14/2012	**Alarm:** Filter system	Checked system, drained influent tank, reset alarm, and system restart. Reset filter system discharge pressure.
12/20/2012	**Alarm:** High discharge pressure on filter system	Reset set: monitored. Backwashed Filter C. Finish repair of mixer M1. Back in service.
12/21/2012	**Alarm:** High discharge pressure on filter system	Backwashed Filter C. Monitored twice. Filter A back in service.
12/22/2012	**Alarm:** Filter high pressure. Sludge holding tank valves would not open when filled.	Backwashed Filter A & C. Manually opened values and drained tank.
12/26/2012	**Alarm:** Filter system trouble. Filter B alarm showing valve P/C problem.	Checked system, drained influent tank, reset alarm, and system restart. Backwashed filter A & C.
1/24/2013	Water in containment area from a leak in filter A and buildup in air stripper trays	Backwash filters A & C and clean air stripper trays
1/30/2013	Water in containment area from a seal leak in filter A	replace seal
2/1/2013	**Alarm:** Power Surge. Filter system fault.	Checked system, reset alarm. Reset filters
2/2/2013 to 2/14/13	**Alarm:** PLC Fault; system down for filter replacement	Repair PLC; All run times reset to 11/15/12 recorded times; run air stripper in manual mode to treat Toe Drain water during filter repair; all systems back on line 2/14/13
2/20/2013	buildup in air stripper trays	clean air stripper trays
3/6/2013	**Alarm:** Filter pressure	Reset pressure differential on A, B, & C.
3/12/2013	buildup in air stripper trays	clean air stripper trays
3/14/2013	**Alarm:** Filter pressure, EW-4 offline	Reset backwash filters & alarms. Back in service.
3/18/2013	**Alarm:** Filter system trouble. (Storm/heavy rain)	System filter fault reset filter, monitor.
3/23/2013	**Alarm:** Power failure and filter system fault	Reset alarm and system restart
3/27/2013	Toe Drain system down for maintenance	Cleaned toe drain sump; replaced TD sump pumps; cleaned TD lines and replaced four Fernco couplings on piping; system back up same day.
5/2/2013	SCADA upgrades completed	Resume off-site recovery
5/7/2013	buildup in air stripper trays	clean air stripper trays
5/24/2013	**Alarm**: Filter system trouble	System filter fault reset filter, monitor.

Appendix A Table 1
Cumulative Summary of Treatment System Downtime
FPE Groundwater Treatment System
Edgefield, South Carolina

Dates	Cause	Actions Taken
6/6/2013	Pressure transducer is causing pump to short cycle because it's pressure signal is intermittent	Replace pressure transducer
6/23/2013	**Alarm:** Toe drain pump overload	Checked system, reset alarm. Reset filters
6/24/2013	**Alarm:** Toe drain pump overload	Checked system, reset alarm. Reset filters
6/29/2013	**Alarm:** Toe drain high level (P100 failed)	Reset alarm
6/30/2013	**Alarm:** Toe drain high level (P100 failed)	Reset alarm
7/6/2013	**Alarm:** Toe drain high level (P100:P150)	Reset alarm
7/8/2013	**Alarm:** Toe drain high level	Reset alarm
7/11/2013	Redox level low	Added 4 buckets of redox
7/14/2013	**Alarm:** Toe drain sump high level	Reset alarm
7/18/2013	Toe Drain system down for maintenance	Cleaned toe drain sump; replaced TD sump pumps; system back up same day.
8/6/2013	**Alarm:** Toe drain communication alarm	Remotely reset modem
9/23/2013	**Alarm:** Toe drain power fail	Reset alarm
10/24/2013	Shut down toe drain return pumps	Restart Pumps on 10/29/13
11/14/2013	**Alarm:** Power failure and modem communication problems	Restart system; work with AT&T per modem issues
2/2/2014	**Alarm:** Toe drain high level	Changed out P-100 pump/motor; restart
2/9/2014	Toe Drain system down for maintenance	Cleaned toe drain sump and jetted line; system back up same day.
2/21/2014	**Alarm:** Toe drain high level (P100 failed)	Reset alarm
2/12/2014	Lost power from ice and snow storm	2/14/14 power back on
3/11/2014	FASW flow meter giving erratic readings	Cleaned FASW flow meter
3/25/2014	Power surge; air compressor power fault	reset breaker and power up unit
4/6/2014	**Alarm:** Short term power failure	Reset UPS and Rabbit Trail control panel; system back on line
5/8/2014	Annual SCDHEC compliance inspection	No findings
5/26/2014	**Alarm:** Short term power failure	Reset EW-1; system back on line; change GAC units
6/13/2014	SCADA system not responding remotely	reboot system; change out modem
8/9/2014	**Alarm:** EW-11 down from apparent power surge	Reset EW-11 and back on line
8/23/2014	SCADA system not responding remotely	reboot system; change out modem
8/30/2015	**Alarm:** TE sump high level	Connections in P100 pump control box cleaned; pump back in service and operating
9/9/2014	TD communication failure	Reset dial up at residence; communication back in service
9/15/2014	**Alarm:** EW-4 down	Reset EW-4 and back on line
11/24/2014	**Alarm:** Rabbit Trail communication failure	Replaced APC and system back on line
12/17/2014	EW-10, EW-11, and FASW offline; tapping into influent line for EW-12	influent conveyance line back in service; EW-10, EW-11, and FASW back on line
12/29/2014	**Alarm:** Rabbit Trail communication failure	Rewired APC and system back on line
12/31/2014	**Alarm:** Communication failure at Rabbit Trail Road; phone line down at treatment facility	TD UPS replaced 1/2/15; treatment facility phone line repaired 1/3/15
1/4/2015	**Alarm:** Well EW-11 down	Reset EW-11 and back on line
1/23/2015	**Alarm:** Communication failure	Reboot computer and back online
1/26/2015	**Alarm:** Filter system	Reset and back online
2/1/2015	**Alarm:** Well EW-10 down	Reset EW-10 and back on line
2/5/2015	SCE&G cut power to treatment facility 0955 hrs	Power back on and systems back up at 1037 hrs
2/16/2015	**Alarm:** Well EW-2 down (pump bad); EW-11 shutdown due to effluent line leak	Replaced EW-11 effluent line on 2/24/15; replaced EW-2 pump/motor on 3/13/15

Appendix A Table 1
Cumulative Summary of Treatment System Downtime
FPE Groundwater Treatment System
Edgefield, South Carolina

Dates	Cause	Actions Taken
2/19/2015	Offsite extraction wells on and off during line pressure testing - 4 hours	All wells back in service same day - 2/19/15
3/9/2015	**Alarm:** Toe Drain high level	Replaced TD pump 3/9/15; TD back in service
4/3/2015	**Alarm:** EW-11 down	Reset EW-11 and back on line
5/21/2015	**Security Alarm:** Unknown	reset sensitivity of security cameras
6/16/2015	**Alarm:** EW-4 overload fault	Reset EW-4 and back on line
6/18/2015	**Alarm:** EW-4 tripped off, will not stay running	Replaced pump and motor 6/30/15, well back on line
6/30/2015	**Alarm:** EW-10 faulted	Reset EW-10 and back on line same day
7/26/2015	**Alarm:** Transfer pump VFD fault	Reset VFD and monitored system
7/28/2015	**Alarm**: Transfer pump VFD Failed	Replaced VFD and system back on line
8/13/2015	**Alarm:** EW-10 tripped off	Reset VFD, back on.
8/14/2015	Remote system login issue	Trouble shot PLC, rebooted computer;
8/19/2015	**Alarm:** EW-10 fault	Installed a new pump/motor and well placed back online
8/20/2015	**Alarm**: Toe Drain PLC	Reset PLC and system back on line-TD offline <24 hours
8/24/2015	TD PLC issue	Replace PLC in-out module; system back online
10/5/2015	**Alarm:** EW-10 tripped off	Reset EW-10 and back in service
10/12/2105	**Alarm:** EW-10 and EW-11 tripped off	Reset EW-10 and EW-11, monitored, and back in service
11/4/2015	**Alarm:** Remote access communication failure	AT&T troubleshoot phone line and fixed the problem
11/8/2015	**Alarm:** EW-12 tripped off	Reset EW-12 and rebooted computer
11/18-19/2015	Routine maintenance: Offsite extraction wells and Toe Drain shut down	Conveyance line jetting/cleaning; restart all offsite systems following maintenance
11/28/2015	**Alarm:** SCADA and HMI Panel not working	Systems rebooted and back online-systems offline<24 hours
1/30/2016	**Alarm:** EW-12 fault	Pump/motor pulled and replaced on 2/9/16
1/30/2016	EW-12 off for troubleshooting pump	Pump/motor pulled and replaced on 2/9/17
2/9/2016	**Alarm:** EW-12 pump shaft broken	Pump replaced
2/19/2016	**Alarm:** EW-10 tripped off	Reset EW-10 and back in service
2/25/2016	EW-10 motor fault	EW-10 pump and motor replaced on 3/4/16
3/7/2016	**Alarm:** EW-10 tripped off	Electrical trouble-shoot and repair for EW-10
4/21/2016	**Alarm:** Filter reset	Filter reset cleared out on filter panel
5/3/2016	EW-1 turned off for rebound testing	EW-1 turned on before sampling on 5/12/16
5/21/2016	**Alarm:** Toe Drain P100 tripped off	Toe Drain P100 pump and motor replaced
5/29/2016	**Alarm:** FSW pump faulted; computer down	Rebooted and back in service
5/31/2016	**Alarm:** EW-12 tripped off	Reset and back online
6/8/2016	**Alarm:** Toe Drain P150 stopped running	Replaced capacitor box, pump and motor and back in service
7/18/2016	**Alarm:** Rabbit Trail communication failure	Phone service repaired phone lines on 7/21/16
7/18/2016	**Alarm:** Toe drain communication alarm	Phone service repaired phone lines on 7/21/16
7/18/2016	EW-1 will not start in auto troubleshoot	EW-1 replaced level transmitter
8/2/2016	Troubleshoot EW-12 flow meter	Reset and back online
8/4/2016	Trench #2's transducer is bad	Installed new transducer in Trench #2 on 9/22/16; still not working
8/16/2016	Pump P7A leaking	P7A transfer pump swapped out on 8/25/16
9/3/2016	**Alarm:** EW-10 and EW-11 tripped off due to weather	Both reset and back online

Appendix A Table 1
Cumulative Summary of Treatment System Downtime
FPE Groundwater Treatment System
Edgefield, South Carolina

Dates	Cause	Actions Taken
9/7/2016	**Alarm:** PLC shut down due to bad UPS power supply	Disconnected bad UPS power supply and redirected power to P/C power; plant back online; restarted pumps, wells, and plant; bad UPS replaced on 9/8/16 with new battery back-up
9/12-14/2016	Toe Drain modification	Reconfigured Toe Drain influent header for easier sampling; installed second port in sump housing
9/22/2016	New transducer installed in Trench #2	Transducer in Trench #2 still not working - PLC needs addressing
10/8/2016	**Alarm:** EW-11 tripped off	EW-11 reset and back in service
11/12/2016	**Alarm:** EW-11 tripped off	EW-11 reset and back in service
12/3/2016	Treatment system down for one day for carbon system piping installation	Carbon system piping installed and restarted treatment system; effluent flow meter reset
12/10/2016	Treatment system down for one day for carbon system piping installation	Carbon system piping installed and restarted treatment system
1/29/2017	**Alarm:** Toe Drain high level	Changed P150 motor; bad control box
3/1/2017	**Alarm:** Air Stripper high level	Reset pump and pulled level down; restart plant
5/1/2017	**Alarm:** EW-12 tripped off	EW-12 reset and back in service
6/6/2017	**Alarm:** EW-12 tripped off	EW-12 reset and back in service
6/15/2017	EW-2 level transducer malfunction; well shut down	Transducer replaced and well back in service
6/16/2017	**Alarm:** EW-10 and EW-11 tripped off	Reset both and back in service
6/20/2017	**Alarm:** EW-11 tripped off	EW-11 reset and back in service
8/8/2017	**Alarm:** EW-10 tripped off	EW-10 reset and back in service
8/9/2017	**Alarm:** Air stripper effluent pump failure. Treatment system down	Reset pump. Treatment system back in service
8/14/2017	**Alarm:** EW-11 tripped off	EW-11 reset and back in service
8/20/2017	**Alarm:** EW-10 and EW-11 tripped off	Reset both and back in service
8/23/2017	**Alarm:** EW-11 tripped off due to NFP signal	EW-11 fault and transducer changed, well reset and back in service
8/29/2017	Trench #1's motor not working properly	Adjusted motor in Trench #1
9/12/2017	**Alarm:** Rabbit Trail communication down due to power outage	ATT repaired phone lines and back in service on 9/14/18
10/13/2017	**Alarm:** EW-10 and EW-11 tripped off	Reset both and back in service
11/6/2017	**Alarm:** EW-10 and EW-11 faults	Restricted operation of wells during daylight working hours; replaced transducer bellows on 11/28/17 and returned to operating full-time
1/4/2018	**Alarm**: Air stripper effluent pump failed; treatment system down	Installed new pump P-4A; treatment system back in service on 1/5/18
1/5/2018	P-4B pump troubleshoot - pump has a leak	Effluent fail safe for tank and throughout system installed
3/12/2018	**Alarm**: EW-12 faulting and can't achieve desired drawdown	Installed pressure gauges on EW-10, EW-11, and EW-12 to monitor line pressures for diagnosis
4/15/2018	**Alarm**: Effluent pump (P-4A and -4B) failed	Replaced pump P-4B and repaired shaft coupling of P-4A; system back in service 4/16/18
5/4/2018	**Alarm**: Offsite extraction system communication fa	Contacted ATT for phone service inspection; ATT reported phone and internet service issues resolved 5/10/18
5/15/2018	Increasing Toe Drain influent line pressures and decreasing flows	Cleaned TD influent/effluent lines, replaced TD sump pumps, and cleaned offsite extraction well influent line; all placed back in service 5/15/18

Appendix A Table 1
Cumulative Summary of Treatment System Downtime
FPE Groundwater Treatment System
Edgefield, South Carolina

Dates	Cause	Actions Taken
5/18/2018	**Alarm**: EW-12 faulting and can't achieve desired drawdown	Replaced with larger pump/motor; back in service 5/18/18
6/15/2018	Continued EW-12 faulting and performance issues	Replaced flow meter and adjust VFD; back in service and operating normally 6/21/18
7/1/2018	**Alarm**: AS discharge pump P3B fault resulted in air stripper and sump high level alarms	Cleared fault, toggled to P3A pump and system back on line 7/1/18; reprogrammed PLC so P3 pumps would automatically toggle to backup pump if one fails.
8/14/2018	Persistent communication issues between Rabbit Trail Rd systems and on-site treatment system since April 2018.	AT&T determined issues on their side and resolved com issues on 8/24/18
9/8/2018	**Alarm**: EW-12 fault	Reset fault and placed EW-12 back in service; adjusted pumping levels in EW-10 and EW-11
9/13/2018	Shut down all system due to pending hurricane	No effects from storm; all systems place back in service 9/17/18
10/8/2018	**Alarm**: EW-12 fault	Reset fault and placed EW-12 back in service; adjusted pumping level in EW-12 from 33' to 36'
10/10/2018	Shut down all systems due to pending hurricane	No effects from storm; all systems place back in service 10/11/18
12/6/2018	**Alarm**: Influent pump P2B faulting;	Switch to P2A; P2B seized and needs replacement, purchase/replacement scheduled for 1Q19
12/17/2018	**Alarm**: continued EW-12 faulting	Upgraded surge protection on EW-12 VFD and reprogrammed; EW-12 placed back in service 12/17/18
1/3/2019	**Alarm**: FASW fault due to influent line backpressure	Changed pumping level of EW-11 to reduce backpressure same day
4/3/2019	**Alarm**: AS transfer pump P-2B fault	Toggled to pump P-3B and system back online same day
4/24/2019	**Alarm**: EW-1R pump/motor fault	Replaced pump/motor 5/1/19 and placed back in operation
4/26/2019	**Alarm**: EW-10 pump motor overloading	Replaced pump/motor 5/3/19 and placed back in service
6/3/2019	**Alarm**: AS transfer pump P-3B fault	Toggled to pump P-3A and system back online same day
6/7/2019	**Alarm:** EW-12 PLC input card faulty, needs replacement	EW-10, EW-11, and EW-12 PLC input cards replaced 7/24/19 and placed back online
7/18/2019	**Alarm**: AS transfer pump P-3A/3B fault; treatment system shutdown	Replaced AS transfer pump P-3B; made programming adjustments to VFD/PLC; treatment system placed back online 7/30/19
8/14/2019	**Alarm**: AS transfer pump P-3A fault;	Toggled to pump P-3B and system back online same day
8/16/2019	**Alarm:** EW-12 Rabbit Trail Road VFD faults	Replaced I/O modules and systems placed back in operation 8/29/19
12/13/2019	**Alarm**: EW-3 pump motor overloading	Replaced EW-3 pump/motor and placed back in operation 1/9/20
1/10/2020	**Alarm**: EW-2 pump/motor fault	Replaced EW-2 pump/motor and placed back in operation 1/16/20
2/6/2020	**Alarm:** Airstripper transfer pump P-3B fault	Reset VFD and placed back in operation 2/7/20
2/14/2020	**Alarm:** Airstripper transfer pump P-3B fault	Reset VFD and placed back in operation 2/16/20
3/17/2020	**Alarm:** Airstripper transfer pump P-3A fault	Reset VFD and placed back in operation 3/7/20
3/29/2020	**Alarm:** Airstripper transfer pump P-3A/-3B fault	Reloaded PLC parameters in both VFDs and placed back into operation 3/30/20

Appendix A Table 1
Cumulative Summary of Treatment System Downtime
FPE Groundwater Treatment System
Edgefield, South Carolina

Dates	Cause	Actions Taken
4/12/2020	**Alarm:** Power and offsite communitication failure	Reboot recovery/treatment systems and placed back in operation 4/13/20
4/21/2020	**Alarm:** Power and offsite communitication failure	Reboot recovery/treatment systems and placed back in operation 4/23/20
4/25/2020	**Alarm:** Power and offsite communitication failure	Reboot recovery/treatment systems and placed back in operation 4/27/20
6/5/2020	**Alarm:** Airstripper transfer pump P-3A fault	Reset VFD and placed back in operation 6/5/20
7/19/2020	**Alarm:** Airstripper transfer pump P-3A fault	Reset VFD and placed back in operation 7/20/20
8/14/2020	**Alarm:** Power and offsite communitication failure	Reboot recovery/treatment systems and placed back in operation 8/15/20
9/26/2020	**Alarm:** Power and offsite communitication failure	Reboot recovery/treatment systems and placed back in operation 9/27/20; control room communication restored 9/29/20.
10/16/2020	Offsite extraction wells off due to panel and communication system replacement	Offsite extraction well system restarted and placed in operation 10/17/20.
11/10/2020	**Alarm:** Extraction well FASW fault	Replaced pump/motor 12/17/20
11/30/2020	**Alarm:** Main plant power failure	System reset itself and back in operation 11/30/20
1/26/2021	**Alarm:** Power and offsite communitication failure	Reboot offsite recovery systems and placed back in operation 1/26/21
2/25/2021	**Alarm:** FASW extration well fault	Reset and placed back in service 2/25/21
3/7/2021	**Alarm:** Airstripper transfer pump P-3A/P-3B fault and shut system down	Reset all pumps and VFDs and placed back in service 3/7/21
4/16/2021	**Alarm:** EW-12 extraction well fault	Reset VFD and UPS and placed back in service
5/5/2021	**Alarm:** Main plant power failure	Reset systems and place back in service 5/5/21
5/17/2021	Take GAC vessels offline for carbon change out	GAC replaced and vessels placed back in service 5/26/21
6/7/2021	**Alarm:** Airstripper transfer pump P-3A/P-3B fault and shut system down	Reset all pumps and VFDs and placed back in service 6/8/21
6/14/2021	**Alarm:** EW-2 extraction well fault	Reset and placed back in service 6/14/21
1/28/2021	**Alarm:** Airstripper sump high level	Restart P-3 pumps and pump down AS sump; placed system back in service 1/28/21
2/25/2021	**Alarm:** Airstripper sump high level	Restart P-3 pumps and pump down AS sump; placed system back in service 2/26/21
5/5/2021	**Alarm:** Airstripper sump high level	Restart P-3 pumps and pump down AS sump; placed system back in service 5/5/21
6/7/2021	**Alarm:** Floor sump high level	Pumped down EQ tank, reset P-2 pumps, placed back in service 5/5/2021
7/10/2021	All recovery/treatment systems offline for main control panel/PLC changeout	Complete control panel installation and systems restart 7/18/21
8/6/2021	**Alarm:** Air stripper blower fault	Replaced blower starter in panel; placed back in service 8/8/21
9/14/2021	**Alarm:** Effluent P-4B pump fault	Reset all pumps and VFDs and placed back in service 9/14/21
12/16/2021	**Alarm:** Power outage at Rabbit Trail and Toe Drain	Restart well EW-12 and all other wells restart in auto; placed back in service 12/17/21
12/23/2021	**Alarm:** Power outage at main plant	Restart P-3 VFD; placed back in service 12/23/21
12/28/2021	Received effluent data with TCE exceedance	Shut all systems down; reroute Toe Drain influent to sewer outfall

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
Effluent to Outfall #2/ACPSA/ Trenches	9/23/2009	ND	ND	ND	ND	3.4	ND	ND	ND	ND	ND	ND	2	ND
	10/15/2009	ND	ND	ND	ND	19.9	ND	ND	ND	ND	ND	ND	**12**	ND
	11/12/2009	ND	ND	ND	ND	1.1	ND	ND	ND	ND	ND	ND	1	ND
	12/15/2009	ND	ND	ND	ND	5.1	ND	ND	ND	ND	ND	ND	4	ND
	1/21/2010	ND	ND	ND	ND	1.1	ND	ND	ND	ND	ND	ND	1	ND
	2/18/2010	ND	ND	ND	ND	0.71 J	ND	ND	ND	ND	ND	ND	0.75 J	ND
	3/30/2010	ND	ND	ND	ND	18.1	ND	ND	ND	ND	ND	ND	**26**	ND
	4/26/2010	ND	ND	ND	ND	0.89 J	ND	ND	ND	ND	ND	ND	1	ND
	5/27/2010	ND	ND	ND	ND	7.8	ND	ND	ND	ND	ND	ND	**12**	ND
	6/22/2010	ND	ND	ND	ND	5.3	ND	ND	ND	ND	ND	ND	**7**	ND
	7/23/2010	ND	ND	ND	ND	23.4	ND	ND	ND	ND	ND	ND	**37**	ND
	8/25/2010	ND	ND	ND	ND	2.1	ND	ND	ND	ND	ND	ND	3	ND
	9/22/2010	0.93 J*	ND	0.79 J*	0.82 J*	151*	ND	ND	ND	ND	ND	1.3 J*	328*	ND
	10/14/2010	ND	ND	ND	ND	0.71 J	ND	ND	ND	ND	ND	ND	0.81 J	ND
	10/20/2010	ND	ND	ND	ND	1.8	ND	ND	ND	ND	ND	ND	2	ND
	11/2/2010	ND	ND	ND	ND	2.3	ND	ND	ND	ND	ND	ND	3	ND
	12/7/2010	ND	ND	ND	ND	1.6	ND	ND	ND	ND	ND	ND	2	ND
	1/6/2011	ND	ND	ND	ND	1.3	ND	ND	ND	ND	ND	ND	1	ND
	2/10/2011	ND	ND	ND	ND	2.0	ND	ND	ND	ND	ND	ND	3	ND
	3/16/2011	ND	ND	ND	ND	3.0	ND	ND	ND	ND	ND	ND	3	ND
	4/12/2011	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.34J	ND
	5/19/2011	ND	ND	ND	ND	0.73 J	ND	ND	ND	ND	ND	ND	0.92 J	ND
	6/16/2011	ND	ND	ND	ND	0.61 J	ND	ND	ND	ND	ND	ND	0.73 J	ND
	7/14/2011	ND	ND	ND	ND	1.1	ND	ND	ND	ND	ND	ND	2	ND
	8/11/2011	ND	ND	ND	ND	1.2	ND	ND	ND	ND	ND	ND	2	ND
	9/8/2011	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0	ND
	10/13/2011	ND	ND	ND	ND	1.8	ND	ND	ND	ND	ND	ND	2	ND
	11/10/2011	ND	ND	ND	ND	0.84 J	ND	ND	ND	ND	ND	ND	1	ND
	12/8/2011	ND	ND	ND	ND	2.7	ND	ND	ND	ND	ND	ND	3	ND
	1/12/2012	ND	ND	ND	ND	1.1	ND	ND	ND	ND	ND	ND	1	ND
	2/9/2012	ND	ND	ND	ND	1.1	ND	ND	ND	ND	ND	ND	1	ND
	3/15/2012	ND	ND	ND	ND	1.7	ND	ND	ND	ND	ND	ND	4	ND
	4/13/2012	ND	ND	ND	ND	1.1	ND	ND	ND	ND	ND	ND	2	ND
	5/15/2012	ND	ND	ND	ND	1.2	ND	ND	ND	ND	ND	ND	2	ND
	6/7/2012	ND	ND	ND	ND	1.3	ND	ND	ND	ND	ND	ND	3	ND
	7/17/2012	ND	ND	ND	ND	1.1	ND	ND	ND	ND	ND	ND	2	ND
	8/16/2012	ND	ND	ND	ND	1.2	ND	ND	ND	ND	ND	ND	3	ND
	9/13/2012	ND	ND	ND	ND	1.1	ND	ND	ND	ND	ND	ND	3	ND
	10/11/2012	ND	ND	ND	ND	0.93 J	ND	ND	ND	ND	ND	ND	3	ND
	11/8/2012	ND	ND	ND	ND	0.85 J	ND	ND	ND	ND	ND	ND	1	ND
	12/6/2012	ND	ND	ND	ND	1.0	ND	ND	ND	ND	ND	ND	2	ND
	1/10/2013	ND	ND	ND	ND	1.5	ND	ND	ND	ND	ND	ND	4	ND
	2/21/2013	ND	ND	ND	ND	0.8 J	ND	ND	ND	ND	ND	ND	2	ND
	3/14/2013	ND	ND	ND	ND	0.43 J	ND	ND	ND	ND	ND	ND	0.59 J	ND
	4/4/2013	ND	ND	ND	ND	0.67 J	ND	ND	ND	ND	ND	ND	2	ND
	5/9/2013	ND	ND	ND	ND	0.63 J	ND	ND	3.7 J	ND	ND	ND	2	ND
	6/13/2013	ND	ND	ND	ND	3	ND	ND	ND	ND	ND	ND	27	ND
	7/11/2013	ND	ND	ND	ND	0.54 J	ND	ND	ND	ND	ND	ND	2	ND
	8/8/2013	ND	ND	ND	ND	0.86 J	ND	ND	ND	ND	ND	ND	3	ND
	9/12/2013	ND	ND	ND	ND	1.2	ND	ND	ND	ND	ND	ND	5	ND
	10/24/2013	ND	ND	ND	ND	0.81 J	ND	ND	ND	ND	ND	ND	3	ND
	11/14/2013	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	12/12/2013	ND	ND	ND	ND	0.74 J	ND	ND	ND	ND	ND	ND	1	ND
	1/16/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	2/17/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2	ND
	3/6/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2	ND
	4/3/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
Effluent to Outfall #2/ACPSA/ Trenches	5/8/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2	ND
	6/17/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1	ND
	7/10/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	3	ND
	8/14/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2	ND
	9/11/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2	ND
	10/9/2014	ND	ND	ND	ND	1.1	ND	ND	ND	ND	ND	ND	4	ND
	11/13/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2	ND
	12/11/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1	ND
	1/15/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1	ND
	2/12/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1	ND
	3/19/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	4/16/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2	ND
	5/14/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2	ND
	6/11/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2	ND
	7/1/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	8/13/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/17/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	10/15/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	11/12/2015	ND	ND	ND	ND	1.2	ND	ND	ND	ND	ND	ND	2	ND
	12/4/2015	ND	ND	ND	ND	3.1	ND	ND	ND	ND	ND	ND	5	ND
	1/14/2016	ND	ND	ND	ND	ND	ND	ND	NDb	ND	ND	ND	ND	ND
	2/11/2016	ND	ND	ND	ND	ND	ND	ND	NDb	ND	ND	ND	ND	ND
	3/17/2016	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	4/14/2016	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1	ND
	5/12/2016	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2	ND
	6/16/2016	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1	ND
	7/14/2016	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2	ND
	8/11/2016	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2	ND
	9/9/2016	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1	ND
	10/13/2016	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1	ND
	11/17/2016	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1	ND
	12/7/2016	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1	ND
	1/12/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1	ND
	2/16/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	3/12/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	4/13/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	5/11/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	6/15/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	7/25/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	8/16/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/19/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	10/12/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	11/16/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	12/14/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	1/11/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	2/15/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	3/15/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	4/12/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	5/17/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	6/14/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	7/19/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	8/17/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/13/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	10/10/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	11/15/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	12/13/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	1/17/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
Effluent to Outfall #2/ACPSA/ Trenches (continued)	2/14/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	3/14/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	4/11/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	5/16/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	6/13/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	7/11/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	8/15/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/12/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	10/10/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	11/13/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	12/12/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	1/16/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	2/13/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	3/30/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1	ND
	4/16/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	5/15/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	6/10/2020	ND	ND	ND	ND	0.28 J	ND	ND	ND	ND	ND	ND	0.72 J	ND
	7/16/2020	ND	ND	ND	ND	0.30 J	ND	ND	ND	ND	ND	ND	0.59 J	ND
	8/13/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.70 J	ND
	9/17/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.76 J	ND
	10/15/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.61 J	ND
	11/12/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.89 J	ND
	12/16/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.62 J	ND
	1/14/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.88 J	ND
	2/11/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.88 J	ND
	3/11/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.89 J	ND
	4/15/2021	ND	ND	ND	ND	5.2	ND	ND	ND	ND	ND	ND	13	ND
	5/4/2021	ND	ND	ND	ND	1.9	ND	ND	ND	ND	ND	ND	6	ND
	5/13/2021	ND	ND	ND	ND	1.1	ND	ND	ND	ND	0.62	ND	5	ND
	6/14/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	7/20/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	8/19/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/16/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	10/14/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	11/20/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	12/16/2021	ND	ND	ND	ND	2.9	ND	ND	ND	ND	ND	ND	12	ND
Effluent to NPDES Outfall #001	1/1/2009	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	2/1/2009	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	3/1/2009	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	4/1/2009	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	5/1/2010	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	6/1/2009	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	7/1/2009	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	8/1/2009	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/1/2009	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	10/1/2009	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	11/1/2009	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	12/1/2009	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	1/1/2010	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	2/1/2010	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	3/1/2010	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	4/1/2010	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	5/1/2010	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	6/1/2010	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	7/1/2010	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	8/1/2010	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/1/2010	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	10/1/2010	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
Effluent to NPDES Outfall #001 (continued)	11/1/2010	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	12/1/2010	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	1/6/2011	ND	ND	ND	ND	1.3	ND	ND	ND	ND	ND	ND	1	ND
	2/10/2011	ND	ND	ND	ND	2.0	ND	ND	ND	ND	ND	ND	ND	ND
	3/16/2011	ND	ND	ND	ND	3.0	ND	ND	ND	ND	ND	ND	3	ND
	4/12/2011	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.34	ND
	5/19/2011	ND	ND	ND	ND	0.73	ND	ND	ND	ND	ND	ND	0.92	ND
	6/22/2011	ND	ND	ND	ND	1.3	ND	ND	ND	ND	ND	ND	2	ND
	7/14/2011	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	8/11/2011	ND	ND	ND	ND	1.2	ND	ND	ND	ND	ND	ND	2	ND
	9/8/2011	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	10/13/2011	ND	ND	ND	ND	0.35	ND	ND	ND	ND	ND	ND	2	ND
	11/10/2011	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.26	ND
	12/8/2011	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	1/12/2012	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	2/9/2012	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	3/20/2012	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	4/12/2012	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	5/15/2012	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	6/7/2012	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0	ND
	7/17/2012	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	.22	ND
	8/16/2012	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/13/2012	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	10/11/2012	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	11/8/2012	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	12/6/2012	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	1/10/2013	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	.34	ND
	2/21/2013	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	.35	ND
	3/14/2013	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	4/4/2013	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	5/9/2013	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	6/13/2013	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	7/11/2013	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	8/8/2013	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/12/2013	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	10/24/2013	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	11/8/2013	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	12/6/2013	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	1/16/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	2/17/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	3/6/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	4/3/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	5/8/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	6/12/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	7/10/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	8/14/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/11/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1	ND
	10/9/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	11/13/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	12/11/2014	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	1/15/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	2/12/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	3/19/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	4/16/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	5/14/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	6/11/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	7/1/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
Effluent to NPDES Outfall #001 (continued)	8/13/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/17/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	10/15/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	11/12/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	NDb	ND
	12/4/2015	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	1/14/2016	ND	ND	ND	ND	ND	ND	ND	NDb	ND	ND	ND	ND	ND
	2/11/2016	ND	ND	ND	ND	ND	ND	ND	NDb	ND	ND	ND	ND	ND
	3/17/2016	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	4/14/2016	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	5/12/2016	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	6/16/2016	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	7/14/2016	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	8/11/2016	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/9/2016	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	10/13/2016	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	11/16/2016	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	12/7/2016	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	1/12/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	2/16/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	3/12/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	4/13/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	5/11/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	6/15/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	7/25/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	8/17/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/19/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	10/12/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	11/16/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	12/14/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	1/11/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	2/15/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	3/15/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	4/12/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	5/17/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	6/14/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	7/19/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	8/17/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/13/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	10/10/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	11/15/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	12/13/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	1/17/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	2/14/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	3/14/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	4/11/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	5/16/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	6/13/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	7/11/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	8/15/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	9/12/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	10/10/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	11/13/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	12/12/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	1/16/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	2/13/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	3/30/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.87 J	ND
	4/16/2020	ND	ND	ND	ND	0.36 J	ND	ND	ND	ND	ND	ND	1	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
Effluent to NPDES Outfall #001 (continued)	5/15/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.49 J	ND
	6/10/2020	ND	ND	ND	ND	0.28 J	ND	ND	ND	ND	ND	ND	0.72 J	ND
	7/16/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.81 J	ND
	8/13/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1	ND
	9/17/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.98 J	ND
	10/15/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.62 J	ND
	11/12/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1	ND
	12/16/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.72 J	ND
	1/14/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.78 J	ND
	2/11/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.98 J	ND
	3/11/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.96 J	ND
	4/15/2021	ND	ND	ND	ND	5.9	ND	ND	ND	ND	ND	ND	12	ND
	5/4/2021	ND	ND	ND	ND	1.8	ND	ND	ND	ND	ND	ND	6	ND
	5/13/2021	ND	ND	ND	ND	1.1	ND	ND	ND	ND	ND	ND	5	ND
	6/14/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.75 J	ND
	7/20/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.69 J	ND
	8/19/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1	ND
	9/16/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	10/14/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.53 J	ND
	11/20/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.42 J	ND
	12/16/2021	ND	ND	ND	ND	1.1	ND	ND	ND	ND	ND	ND	5.2	ND
EW-1	9/23/2009	14.6	1.6	ND	ND	1.6	ND	ND	ND	ND	ND	ND	57	ND
	12/15/2009	13.8	2.1	ND	ND	4.8	ND	ND	ND	0.24 J	ND	ND	97	ND
	1/21/2010	12.7	2.0	ND	ND	5.7	ND	ND	ND	ND	ND	ND	89	ND
	2/18/2010	8.6	1.8	ND	ND	7.6	ND	ND	ND	0.24 J	ND	ND	122	ND
	3/30/2010	8.5	1.6	ND	ND	7.9	ND	ND	ND	ND	ND	ND	107	ND
	4/26/2010	13.2	2.4	ND	ND	6.2	ND	ND	ND	ND	ND	ND	93	ND
	5/27/2010	15.1	2.4	ND	ND	2.3	ND	ND	ND	ND	ND	ND	58	ND
	6/22/2010	EW-1 Offline - Pump Failure												
	7/23/2010	18.5	3.0	ND	ND	1.1	ND	ND	ND	ND	ND	ND	40	ND
	8/25/2010	15.4	2.5	ND	ND	1.1	ND	ND	ND	ND	ND	ND	53	ND
	9/22/2010	21.4	3.3	ND	ND	0.89 J	ND	ND	ND	0.34 J	ND	ND	36	ND
	10/20/2010	21.7	3.6	ND	ND	0.83 J	ND	ND	ND	0.41 J	ND	ND	32	ND
	11/2/2010	19.4	3.4	ND	ND	0.42 J	ND	ND	ND	0.38 J	ND	ND	28	ND
	12/7/2010	26.3	4.7	ND	ND	0.62 J	ND	ND	ND	0.48 J	ND	ND	28	ND
	1/6/2011	22.3	4.2	ND	ND	0.73 J	ND	ND	ND	0.46 J	ND	ND	24	ND
	2/10/2011	22.0	3.8	ND	ND	0.68 J	ND	ND	ND	0.39 J	ND	ND	32	ND
	3/16/2011	21.6	4.3	ND	ND	1.0	ND	ND	ND	0.52J	ND	ND	34	ND
	4/12/2011	16.5	3.2	ND	ND	1.6	ND	ND	ND	0.40J	ND	ND	53	ND
	5/19/2011	18.4	3.8	ND	ND	2.1	ND	ND	ND	ND	ND	ND	43	ND
	6/16/2011	18.6	3.7	ND	ND	0.90 J	ND	ND	ND	0.29 J	ND	ND	29	ND
	7/14/2011	25.9	4.2	ND	ND	0.72 J	ND	ND	ND	0.32 J	ND	ND	23	ND
	8/11/2011	25.7	4.7	ND	ND	0.54 J	ND	ND	ND	ND	ND	ND	21	ND
	9/8/2011	25.6	5.2	ND	ND	0.58 J	ND	ND	ND	0.43 J	ND	ND	18	ND
	10/13/2011	25.1	5.2	ND	ND	0.59 J	ND	ND	ND	0.50 J	ND	ND	22	ND
	11/10/2011	22.9	4.9	ND	ND	ND	ND	ND	ND	0.37 J	ND	ND	21	ND
	12/8/2011	20.6	4.5	ND	ND	0.53 J	ND	ND	ND	0.57 J	ND	ND	20	ND
	1/12/2012	19.1	3.6	ND	ND	0.73 J	ND	ND	ND	0.37 J	ND	ND	26	ND
	2/9/2012	16.9	3.4	ND	ND	0.54 J	ND	ND	ND	0.47 J	ND	ND	26	ND
	3/15/2012	15.4	2.8	ND	ND	0.51 J	ND	ND	ND	ND	ND	ND	30	ND
	4/12/2012	16.2	3.3	ND	ND	0.59 J	ND	ND	ND	0.28 J	ND	ND	31	ND
	5/15/2012	19.1	3.8	ND	ND	0.38 J	ND	ND	ND	0.24 J	ND	ND	30	ND
	6/7/2012	18.1	3.8	ND	ND	1.1	ND	ND	ND	0.30 J	ND	ND	30	ND
	7/17/2012	16	4.0	ND	ND	0.78 J	ND	ND	ND	0.30 J	ND	ND	31	ND
	8/16/2012	17.3	3.6	ND	ND	0.41 J	ND	ND	ND	ND	ND	ND	32	ND
	9/13/2012	14.9	3.0	ND	ND	0.40 J	ND	ND	ND	ND	ND	ND	29	ND
	10/11/2012	15.4	3.1	ND	ND	0.23 J	ND	ND	ND	ND	ND	ND	27	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
EW-1 (continued)	11/8/2012	19.2[p]	3.7[p]	ND	ND	0.60 J[p]	ND	ND	ND	0.29 J[p]	ND	ND	20.4[p]	ND
	12/6/2012	18.1	3.9	ND	ND	0.31 J	ND	ND	ND	0.25 J	ND	ND	20	ND
	1/10/2013	14.4	2.9	ND	ND	0.64 J	ND	ND	ND	ND	ND	ND	31	ND
	2/21/2013	13.2	2.5	ND	ND	3.3	ND	ND	ND	0.23 J	ND	ND	45	ND
	3/14/2013	13.7	2.3	ND	ND	1.2	ND	ND	ND	ND	ND	ND	30	ND
	4/4/2013	11.3	2.0	ND	ND	1.1	ND	ND	ND	ND	ND	ND	29	ND
	5/9/2013	11.1	2.0	ND	ND	1.2	ND	ND	ND	ND	ND	ND	36	ND
	6/13/2013	8.3	1.4	ND	ND	1.3	ND	ND	ND	ND	ND	ND	37	ND
	7/11/2013	9.2	1.6	ND	ND	1.6	ND	ND	ND	ND	ND	ND	46	ND
	8/8/2013	6.1	1.3	ND	ND	1.8	ND	ND	ND	ND	ND	ND	45	ND
	9/12/2013	7.6	1.4	ND	ND	1.7	ND	ND	ND	ND	ND	ND	41	ND
	10/10/2013	8.7	1.5	ND	ND	1.1	ND	ND	ND	ND	ND	ND	32	ND
	11/14/2013	15.2	2.5	ND	ND	0.52 J	ND	ND	ND	ND	ND	ND	25	ND
	12/12/2013	10.9	1.9	ND	ND	0.51 J	ND	ND	ND	ND	ND	ND	22	ND
	1/16/2014	10.4	1.8	ND	ND	ND	ND	ND	ND	ND	ND	ND	27	ND
	2/17/2014	13.4	2.1	ND	ND	4.1	ND	ND	ND	ND	ND	ND	52	ND
	3/6/2014	9.6	1.6	ND	ND	ND	ND	ND	ND	ND	ND	ND	26	ND
	4/3/2014	10.5	1.6	ND	ND	1.1	ND	ND	ND	ND	ND	ND	27	ND
	5/8/2014	9.0	1.5	ND	ND	ND	ND	ND	ND	ND	ND	ND	27	ND
	6/12/2014	9.8	1.7	ND	ND	ND	ND	ND	ND	ND	ND	ND	24	ND
	7/10/2014	12.2	2.0	ND	ND	ND	ND	ND	ND	ND	ND	ND	16	ND
	8/14/2014	11.1	2.0	ND	ND	ND	ND	ND	ND	ND	ND	ND	15	ND
	9/11/2014	11.8	2.4	ND	ND	ND	ND	ND	ND	ND	ND	ND	19	ND
	10/9/2014	13.6	2.6	ND	ND	ND	ND	ND	ND	ND	ND	ND	15	ND
	11/13/2014	16.5	2.9	ND	ND	ND	ND	ND	ND	ND	ND	ND	10	ND
	12/11/2014	13.2	2.3	ND	ND	ND	ND	ND	ND	ND	ND	ND	15	ND
	1/15/2015	11.9	1.9	ND	ND	ND	ND	ND	ND	ND	ND	ND	26	ND
	2/12/2015	10.4	2.0	ND	ND	5.5	ND	ND	ND	ND	ND	ND	33	ND
	3/19/2015	9.6	1.6	ND	ND	ND	ND	ND	ND	ND	ND	ND	21	ND
	4/16/2015	10.5	1.7	ND	ND	ND	ND	ND	ND	ND	ND	ND	18	ND
	5/14/2015	7.7	1.4	ND	ND	ND	ND	ND	ND	ND	ND	ND	18	ND
	6/11/2015	8.9	1.6	ND	ND	ND	ND	ND	ND	ND	ND	ND	16	ND
	7/1/2015	10.7	1.7	ND	ND	ND	ND	ND	ND	ND	ND	ND	11	ND
	8/13/2015	14.5	2.1	ND	ND	ND	ND	ND	ND	ND	ND	ND	5	ND
	9/17/2015	11.9	2.2	ND	ND	ND	ND	ND	ND	ND	ND	ND	11	ND
	10/15/2015	10.9	1.9	ND	ND	ND	ND	ND	ND	ND	ND	ND	15	ND
	11/12/2015	8.0	1.2	ND	ND	ND	ND	ND	ND	ND	ND	ND	15	ND
	12/3/2015	8.0	1.5	ND	ND	ND	ND	ND	ND	ND	ND	ND	16	ND
	1/14/2016	8.2	1.2	ND	ND	ND	ND	ND	NDb	ND	ND	ND	19	ND
	2/11/2016	7.7	1.2	ND	ND	ND	ND	ND	NDb	ND	ND	ND	19	ND
	3/17/2016	7.0	1.1	ND	ND	ND	ND	ND	ND	ND	ND	ND	17	ND
	4/14/2016	6.2	1.2	ND	ND	ND	ND	ND	ND	ND	ND	ND	15	ND
	5/26/2016	8.3	1.4	ND	ND	2.0	ND	ND	ND	ND	ND	ND	21	ND
	6/23/2016	Not Sampled												
	7/14/2016	10.8	1.4	1.3	ND	8.0	ND	ND	ND	ND	ND	4.2	139[a]	ND
	8/11/2016	7.9	1.4	ND	ND	2.3	ND	ND	ND	ND	ND	ND	40	ND
	9/9/2016	8.5	1.5	ND	ND	ND	ND	ND	ND	ND	ND	ND	12	ND
	10/13/2016	8.7	1.6	ND	ND	ND	ND	ND	ND	ND	ND	ND	8	ND
	11/17/2016	9.4	1.6	ND	ND	ND	ND	ND	ND	ND	ND	ND	5	ND
	12/7/2016	9.1	1.6	ND	ND	13.2	ND	ND	ND	ND	ND	1.4	73	ND
	1/12/2017	7.3	1.3	ND	ND	ND	ND	ND	ND	ND	ND	ND	13	ND
EW-1R start-up	2/16/2017	2.4	1.0	ND	ND	1.7	ND	ND	ND	ND	ND	ND	28	ND
	3/12/2017	5.8	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	11	ND
	4/13/2017	5.4	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	14	ND
	5/11/2017	7.7	ND	ND	ND	2.4	ND	ND	ND	ND	ND	ND	194	ND
	6/15/2017	7.1	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	315	ND
	7/25/2017	5.9	ND	ND	ND	4.1	ND	ND	ND	ND	ND	ND	358b	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
EW-1R (continued)	8/16/2017	5.7	ND	ND	ND	3.9	ND	ND	ND	ND	ND	ND	338	ND
	9/19/2017	5.6	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	281	ND
	10/12/2017	6.2	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	301	ND
	11/16/2017	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	288	ND
	12/14/2017	7.2	1.5	ND	ND	2.1	ND	ND	ND	ND	ND	ND	193	ND
	1/11/2018	6.7	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	333	ND
	2/15/2018	5.9	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	405	ND
	3/15/2018	5.7	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	299	ND
	4/12/2018	5.4	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	353	ND
	5/17/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	549	ND
	6/14/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	698	ND
	7/19/2018	5.3	1.0	ND	ND	4.6	ND	ND	ND	ND	ND	ND	756	ND
	8/17/2018	5.7	ND	ND	ND	3.9	ND	ND	ND	ND	ND	ND	338	ND
	9/13/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	959	ND
	10/10/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1,100	ND
	11/15/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1,660	ND
	12/13/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1,160	ND
	1/17/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2,350	ND
	2/14/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2,550	ND
	3/14/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2,570	ND
	4/11/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	3,590	ND
	5/16/2019	--	--	--	--	--	--	--	--	--	--	--	--	--
	6/13/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2,050	ND
	7/11/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1,860	ND
	8/15/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	3,000	ND
	9/12/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1,910	ND
	10/10/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1,430	ND
	11/13/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1,500	ND
	12/12/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1,040	ND
	1/16/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1,610	ND
	2/13/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2,590	ND
	3/12/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	3,950	ND
	4/16/2020	ND	ND	ND	ND	59 J	ND	ND	ND	ND	ND	ND	5,360	ND
	5/15/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	5,020	ND
	6/10/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	5,150	ND
	7/16/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	4,920	ND
	8/13/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1,620	ND
	9/17/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2,640	ND
	10/15/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2,440	ND
	11/12/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1,780	ND
	12/16/2020	ND	ND	ND	ND	17.5 J	ND	ND	ND	ND	ND	ND	1,820	ND
	1/14/2021	ND	ND	ND	ND	7.9 J	ND	ND	ND	ND	ND	ND	2,240	ND
	2/11/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2,000	ND
	3/11/2021	ND	ND	ND	ND	14.0 J	ND	ND	ND	ND	ND	ND	3,330	ND
	4/15/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	4,770	ND
	5/13/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	5,380	ND
	6/14/2021	ND	ND	ND	ND	25.2 J	ND	ND	ND	ND	ND	ND	3,960	ND
	7/20/2021	ND	ND	ND	ND	6.0 J	ND	ND	ND	ND	ND	ND	1,180	ND
	8/19/2021	ND	ND	ND	ND	ND	ND	ND	ND	23.8	ND	ND	2,440	ND
	9/16/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	138 J	ND	4,000	ND
	10/14/2021	ND	ND	ND	ND	12.6 J	ND	ND	ND	ND	ND	ND	2,390	ND
	11/20/2021	ND	ND	ND	ND	10.4 J	ND	ND	ND	ND	ND	ND	1,850	ND
	12/16/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2,090	ND
EW-2	9/23/2009	533	ND	653	ND	1,180	ND	ND	ND	ND	ND	579	85,400	ND
	12/15/2009	668	ND	786	ND	1,210	ND	ND	ND	ND	ND	692	70,100	ND
	1/21/2010	430	ND	477	ND	893	ND	ND	ND	ND	ND	559	65,400	ND
	2/18/2010	349	ND	605	ND	808	ND	ND	ND	ND	ND	548	58,600	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
EW-2 (continued)	3/30/2010	384	ND	581	ND	896	ND	ND	ND	ND	ND	627	58,400	ND
	4/26/2010	440	ND	483	ND	1,020	ND	ND	ND	ND	ND	636	68,400	ND
	5/27/2010	337	ND	392	ND	820	ND	ND	ND	ND	ND	502	49,900	ND
	6/22/2010	292 J	ND	435 J	ND	683	ND	ND	ND	ND	ND	546	56,900	ND
	7/23/2010	ND	ND	498 J	ND	808	ND	ND	ND	ND	ND	510	54,300	ND
	8/25/2010	389	ND	498	ND	668	ND	ND	ND	ND	ND	627	47,800	ND
	9/22/2010	380	ND	453	ND	715	ND	ND	ND	ND	ND	546	46,500	ND
	10/20/2010	385	ND	440	ND	659	ND	ND	ND	ND	ND	627	48,500	ND
	11/2/2010	435	ND	607	ND	732	ND	ND	ND	ND	ND	746	62,100	ND
	12/7/2010	497	ND	508	ND	718	ND	ND	ND	ND	ND	650	46,000	ND
	1/6/2011	433	ND	465	ND	613	ND	ND	ND	ND	ND	539	43,500	ND
	2/10/2011	405	ND	401	ND	587	ND	ND	ND	ND	ND	559	47,600	ND
	3/16/2011	391	ND	359	ND	639	ND	ND	ND	ND	ND	577	47,400	ND
	4/12/2011	411	6.3J	439	9.9J	598	ND	ND	ND	6.3J	ND	699	44,800	ND
	5/19/2011	404	ND	415	ND	677	ND	ND	ND	ND	ND	584	45,300	ND
	6/16/2011	399	ND	415	ND	641	ND	ND	ND	ND	ND	496	43,300	ND
	7/14/2011	458	ND	501	ND	657	ND	ND	ND	ND	ND	622	44,900	ND
	8/11/2011	387	ND	467	ND	631	ND	ND	ND	ND	ND	659	35,300	ND
	9/8/2011	50.6*	ND	58.3*	ND	57.3*	ND	ND	ND	ND	ND	65.6*	3,460*	ND
	10/13/2011	445	ND	473	ND	604	ND	ND	ND	ND	ND	730	36,000	ND
	11/10/2011	446	ND	426	ND	538	ND	ND	ND	ND	ND	680	38,300	ND
	12/8/2011	460	ND	438	ND	606	ND	ND	ND	ND	ND	735	42,400	ND
	1/12/2012	406	ND	392	6.5 J	527	ND	ND	ND	ND	ND	640	37,300	ND
	2/9/2012	332	ND	335	ND	390	ND	ND	ND	ND	ND	531	38,600[a]	ND
	3/15/2012	349	ND	323	ND	443	ND	ND	ND	ND	ND	652	32,700	ND
	4/12/2012	407	ND	372	ND	497	ND	ND	ND	ND	ND	770	38,300[a]	ND
	5/15/2012	355	ND	332	ND	440	ND	ND	ND	ND	ND	647	32,900[a]	ND
	6/7/2012	389	ND	383	ND	469	ND	ND	ND	ND	ND	670	29,800[a]	ND
	7/17/2012	388	ND	390	ND	476	ND	ND	ND	ND	ND	588	34,000[a]	ND
	8/16/2012	380	ND	389	ND	474	ND	ND	ND	ND	ND	580	34,400[a]	ND
	9/13/2012	372	ND	410	ND	465	ND	ND	ND	ND	ND	572	34,600	ND
	10/11/2012	377	ND	373	ND	460	ND	ND	ND	ND	ND	561	35,200[a]	ND
	11/8/2012	401	ND	394	ND	469	ND	ND	ND	ND	ND	561	30,800	ND
	12/6/2012	359	ND	374	ND	445	ND	ND	ND	ND	ND	612	30,500	ND
	1/10/2013	419	ND	356	ND	468	ND	ND	ND	ND	ND	609	31,100	ND
	2/21/2013	464	ND	467	ND	444	ND	ND	ND	ND	ND	834	34,800[a]	ND
	3/14/2013	375	ND	329	ND	423	ND	ND	ND	ND	ND	624	31,500[a]	ND
	4/4/2013	447	ND	352	ND	440	ND	ND	ND	ND	ND	699	34,700[a]	ND
	5/9/2013	421	ND	398	ND	454	ND	ND	ND	ND	ND	718	34,000	ND
	6/13/2013	429	ND	422	ND	496	ND	ND	ND	ND	ND	694	39,500	ND
	7/11/2013	365	ND	305	ND	493	ND	ND	ND	ND	ND	632	36,700	ND
	8/8/2013	300	ND	324	ND	523	ND	ND	ND	ND	197 J	565	41,200	ND
	9/12/2013	417	ND	356	ND	613	ND	ND	ND	ND	ND	585	41,900[a]	ND
	10/10/2013	387	ND	343	ND	541	ND	ND	ND	ND	ND	543	44,400[a]	ND
	11/14/2013	499	ND	402	ND	581	ND	ND	ND	ND	ND	716	31,000[a]	ND
	12/12/2013	474	ND	499	ND	543	ND	ND	ND	ND	ND	762	33,700[a]	ND
	1/16/2014	308	ND	311	ND	421	ND	ND	ND	ND	ND	484	25,200	ND
	2/17/2014	432[a]	7.0	359[a]	7.0	531[a]	1.9	ND	ND	5.5	ND	698[a]	31,300	ND
	3/6/2014	325	ND	265	ND	353	ND	ND	ND	ND	ND	655	31,300[a]	ND
	4/3/2014	384	ND	227	ND	429	ND	ND	ND	ND	ND	490	25,400	ND
	5/8/2014	259	ND	202	ND	407	ND	ND	ND	ND	ND	534	25,400[a]	ND
	6/12/2014	336	ND	213	ND	448	ND	ND	ND	ND	ND	519	26,200	ND
	7/10/2014	304	ND	228	ND	304	ND	ND	ND	ND	ND	481	21,700[a]	ND
	8/14/2014	ND	ND	212	ND	361	ND	ND	ND	ND	ND	440	21,000	ND
	9/11/2014	254	ND	195	ND	325	ND	ND	ND	ND	ND	509	18,600	ND
	10/9/2014	372	ND	248	ND	425	ND	ND	ND	ND	ND	579	20,000[a]	ND
	11/13/2014	394	ND	300	ND	488	ND	ND	ND	ND	ND	570	25,400	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
EW-2 (continued)	12/11/2014	244	ND	203	ND	276	ND	ND	ND	ND	ND	447	15,100	ND
	1/15/2015	337	ND	226	ND	322	ND	ND	ND	ND	ND	587	18,000[a]	ND
	2/12/2015	337	ND	228	ND	363	ND	ND	ND	ND	ND	571	18,500[a]	ND
	3/19/2015	349	ND	220	ND	360	ND	ND	ND	ND	ND	737	18,200[a]	ND
	4/16/2015	310	ND	153	ND	289	ND	ND	ND	ND	ND	457	16,900	ND
	5/14/2015	262	ND	146	ND	308	ND	ND	ND	ND	ND	444	16,800	ND
	6/11/2015	359	ND	ND	ND	425	ND	ND	ND	ND	ND	382	16,500	ND
	7/1/2015	307	ND	156	ND	357	ND	ND	ND	ND	ND	519	16,200	ND
	8/13/2015	315	ND	443	ND	302	ND	ND	ND	ND	ND	443	16,600	ND
	9/17/2015	302	ND	164	ND	324	ND	ND	ND	ND	ND	433	15,100	ND
	10/15/2015	327	ND	ND	ND	306	ND	ND	ND	ND	ND	425	15,100	ND
	11/12/2015	290b	5.3	170b	3.7	255b	1.4	ND	ND	4.3	ND	502b	18,200	ND
	12/3/2015	284	ND	ND	ND	ND	ND	ND	ND	ND	ND	424	13,700	ND
	1/14/2016	342	ND	210	ND	267	ND	ND	NDb	ND	ND	477	17,600	ND
	2/11/2016	323	ND	ND	ND	308	ND	ND	NDb	ND	ND	439	16,400	ND
	3/17/2016	331	ND	166	ND	318	ND	ND	ND	ND	ND	401	16,200	ND
	4/14/2016	302	ND	168	ND	334	ND	ND	ND	ND	ND	382	15,000	ND
	5/12/2016	269	ND	149	ND	292	ND	ND	ND	ND	ND	372	16,700	ND
	6/23/2016	320	ND	162	ND	322	ND	ND	ND	ND	ND	402	14,900	ND
	7/14/2016	285	ND	148	ND	285	ND	ND	ND	ND	ND	401	13,900	ND
	8/11/2016	252	ND	ND	ND	297	ND	ND	ND	ND	ND	423	13,200	ND
	9/9/2016	296	ND	ND	ND	274	ND	ND	ND	ND	ND	421	10,600	ND
	10/13/2016	268	ND	152	ND	238	ND	ND	ND	ND	ND	442	12,600	ND
	11/17/2016	269	ND	145	ND	210	ND	ND	ND	ND	ND	444	11,300	ND
	12/7/2016	279	ND	ND	ND	213	ND	ND	ND	ND	ND	402	12,500	ND
	1/12/2017	337	ND	ND	ND	233	ND	ND	ND	ND	ND	483	14,600	ND
	2/16/2017	317	ND	ND	ND	280	ND	ND	ND	ND	ND	520	13,800	ND
	3/12/2017	333	ND	ND	ND	229	ND	ND	ND	ND	ND	503	15,800	ND
	4/13/2017	334	ND	161	ND	213	ND	ND	ND	ND	ND	446	15,500	ND
	5/11/2017	322	ND	173	ND	291	ND	ND	ND	ND	ND	536	13,100	ND
	6/15/2017	EW-2 Offline - Pump Failure												
	7/25/2017	274	ND	142	ND	263	ND	ND	ND	ND	ND	347	11,900	ND
	8/17/2017	267	ND	153	ND	263	ND	ND	ND	ND	ND	463	11,500b	ND
	9/19/2017	400	ND	246	ND	254	ND	ND	ND	ND	ND	523	11,800b	ND
	10/12/2017	320	ND	ND	ND	255	ND	ND	ND	ND	ND	460	11,700	ND
	11/16/2017	244	ND	154	ND	232	ND	ND	ND	ND	ND	418	10,400b	ND
	12/14/2017	303	ND	153	ND	253	ND	ND	ND	ND	ND	410	10,400	ND
	1/11/2018	331	ND	159	ND	284	ND	ND	ND	ND	ND	542	13,400	ND
	2/15/2018	268	ND	136	ND	260	ND	ND	ND	ND	ND	395	9,860	ND
	3/15/2018	257	ND	ND	ND	271	ND	ND	ND	ND	ND	474	11,200	ND
	4/12/2018	298	ND	137	ND	289	ND	ND	ND	ND	ND	436	12,500	ND
	5/17/2018	269	ND	128	ND	236	ND	ND	ND	ND	ND	426	11,000	ND
	6/14/2018	243	ND	109	ND	236	ND	ND	ND	ND	ND	405	10,400	ND
	7/19/2018	241	5.2	115	2.6	250	ND	ND	ND	ND	ND	362	11,100	ND
	8/17/2018	239	ND	154	ND	261	ND	ND	ND	ND	ND	364	9,010	ND
	9/13/2018	351	ND	ND	ND	337	ND	ND	ND	ND	ND	516	12,200	ND
	10/10/2018	291	ND	186	ND	309	ND	ND	ND	ND	ND	428	11,800	ND
	11/15/2018	212	ND	131	ND	232	ND	ND	ND	ND	ND	291	7,840	ND
	12/13/2018	310	ND	175	ND	304	ND	ND	ND	ND	ND	470	9,140	ND
	1/17/2019	341	ND	173	ND	319	ND	ND	ND	ND	ND	501	9,250	ND
	2/14/2019	284	ND	ND	ND	277	ND	ND	ND	ND	ND	428	10,900	ND
	3/14/2019	313	ND	ND	ND	343	ND	ND	ND	ND	ND	434	10,500	ND
	4/11/2019	269	ND	ND	ND	270	ND	ND	ND	ND	ND	399	10,400	ND
	5/16/2019	261	ND	128	ND	254	ND	ND	ND	ND	ND	424	8,860	ND
	6/13/2019	241	ND	130	ND	202	ND	ND	ND	ND	ND	357	8,450	ND
	7/11/2019	ND	ND	ND	ND	501	ND	ND	ND	ND	ND	ND	1,770	ND
	8/15/2019	192	ND	ND	ND	259	ND	ND	ND	ND	ND	370	7,860	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
EW-2 (continued)	9/12/2019	212	ND	112	ND	193	ND	ND	ND	ND	ND	374	7,440	ND
	10/10/2019	192	ND	99.8	ND	177	ND	ND	ND	ND	ND	299	7,390	ND
	11/13/2019	232	ND	121	ND	201	ND	ND	ND	ND	ND	308	7,240	ND
	12/12/2019	184	ND	111	ND	191	ND	ND	ND	ND	ND	358	6,490	ND
	1/17/2020	Not Sampled												
	2/13/2020	250	ND	124	ND	181	ND	ND	ND	ND	ND	340	7,140	ND
	3/12/2020	166	ND	84.2 J	ND	88.8 J	ND	ND	ND	ND	ND	313	5,280	ND
	4/16/2020	242	ND	118	ND	144	ND	ND	ND	ND	ND	337	6,670	ND
	5/15/2020	244	ND	124	ND	166	ND	ND	ND	ND	ND	369	7,350	ND
	6/10/2020	281	ND	138	ND	168	ND	ND	ND	ND	ND	397	7,690	ND
	7/16/2020	283	ND	136	ND	173 J	ND	ND	ND	ND	ND	409	7,410	ND
	8/13/2020	211	ND	119	ND	ND	ND	ND	ND	ND	ND	328	5,710	ND
	9/17/2020	186	ND	98.3 J	ND	110 J	ND	ND	ND	ND	ND	331	5,820	ND
	10/15/2020	224	ND	119	ND	ND	ND	ND	ND	ND	ND	364	6,720	ND
	11/12/2020	202	ND	109	ND	128 J	ND	ND	ND	ND	ND	317	5,240	ND
	12/16/2020	250	ND	127	ND	141 J	ND	ND	ND	ND	ND	363	6,320	ND
	1/14/2021	272	ND	147	ND	137	ND	ND	ND	ND	ND	459	6,790	ND
	2/11/2021	241	ND	107	ND	ND	ND	ND	ND	ND	ND	427	5,720	ND
	3/11/2021	284	ND	131	ND	173	ND	ND	ND	ND	ND	455	7,220	ND
	4/15/2021	227	ND	104	ND	149	ND	ND	ND	ND	ND	334	6,180	ND
	5/13/2021	268	ND	130	ND	118	ND	ND	ND	ND	ND	330	6,350	ND
	6/14/2021	239	ND	141	ND	142	ND	ND	ND	ND	ND	292	5,150	ND
	7/20/2021	260	ND	159	ND	145	ND	ND	ND	ND	ND	408	5,900	ND
	8/19/2021	168 [b]	ND	103	ND	146	ND	ND	ND	ND	ND	341	5,270	ND
	9/16/2021	146	ND	81.4	ND	83.9	ND	ND	ND	ND	ND	217	3,590	ND
	10/14/2021	159	ND	91	ND	98.8	ND	ND	ND	ND	ND	222	3,210	ND
	11/20/2021	163	ND	99.5	ND	109	ND	ND	ND	ND	ND	238	3,700	ND
	12/16/2021	279	ND	138	ND	135	ND	ND	ND	ND	ND	323	4,900	ND
EW-3	9/23/2009	ND	ND	ND	ND	295	3.1 J	ND	ND	2.9 J	ND	51.5	2,340	ND
	12/15/2009	ND	ND	ND	ND	359	4.3 J	ND	ND	3.6 J	ND	52.6	2,400	ND
	1/21/2010	ND	ND	ND	ND	249	4.1 J	ND	ND	4.1 J	ND	37.8	2,340	ND
	2/18/2010	ND	ND	ND	ND	216	ND	ND	ND	4 J	ND	26.7	2,080	ND
	3/30/2010	ND	ND	ND	ND	252	7.5	ND	ND	3.7 J	ND	43	2,350	ND
	4/26/2010	ND	ND	ND	ND	241	4.2 J	ND	ND	4.8 J	ND	33.7	2,690	ND
	5/27/2010	ND	ND	ND	ND	222	4.5 J	ND	ND	3.8 J	ND	35	2,440	ND
	6/22/2010	ND	ND	ND	ND	229	4.7 J	ND	ND	4.1 J	ND	43.2	2,350	ND
	7/23/2010	ND	ND	ND	ND	287	27.1	ND	ND	ND	ND	50.5	2,300	ND
	8/25/2010	ND	ND	ND	ND	354	2.9 J	ND	ND	4.9 J	ND	57.9	2,900	ND
	9/22/2010	ND	ND	ND	ND	337	ND	ND	ND	5 J	ND	45.4	2,440	ND
	10/20/2010	ND	ND	ND	ND	260	9	ND	ND	4.8	ND	40.3	2,660	ND
	11/2/2010	ND	ND	ND	ND	336	4.8 J	ND	ND	5.2	ND	55.7	3,410	ND
	12/7/2010	13.5	ND	11.5	ND	527	5.3 J	ND	ND	7.9 J	ND	75.6	4,160	ND
	1/6/2011	ND	ND	ND	ND	505	2.9 J	ND	ND	5.9 J	ND	88.8	2,900	ND
	2/10/2011	ND	ND	ND	ND	459	9.2 J	ND	ND	ND	ND	76.5	2,630	ND
	3/16/2011	1 J	ND	ND	ND	308	2.3 J	ND	ND	5.1	ND	43.7	2,280	ND
	4/12/2011	ND	ND	ND	ND	334	3.5 J	ND	ND	5.4 J	ND	53.2	2,410	ND
	5/19/2011	ND	ND	ND	ND	299	13.0	ND	ND	4.7 J	ND	51.7	2,140	ND
	6/16/2011	ND	ND	ND	ND	248	9.1	ND	ND	4.5 J	ND	41.7	2,020	ND
	7/14/2011	ND	ND	ND	ND	306	4.3 J	ND	ND	3.9 J	ND	55.1	1,750	ND
	8/11/2011	ND	ND	ND	ND	388	ND	ND	ND	4.1 J	ND	78.3	2,270	ND
	9/8/2011	1.4 J	ND	ND	ND	377	4.0 J	ND	ND	4.8 J	ND	65.1	1,740	ND
	10/13/2011	2.0 J	ND	ND	ND	377	2.9	ND	ND	4.9	ND	78.5	1,840	ND
	11/10/2011	1.8	0.27 J	ND	ND	452	5.0	ND	ND	4.7	ND	73.2	1,940	0.40 J
	12/8/2011	2.2 J	ND	ND	ND	380	8.5	ND	ND	4.1 J	ND	72.4	1,970	ND
	1/12/2012	ND	ND	ND	ND	344	2.9 J	ND	ND	4 J	ND	51.8	1,910	ND
	2/9/2012	ND	ND	ND	ND	285	5.3 J	ND	ND	4.3 J	ND	46.4	1,630	ND
	3/15/2012	ND	ND	ND	ND	269	ND	ND	ND	3.3 J	ND	40.2	1,670 [a]	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
EW-3 (continued)	4/12/2012	ND	ND	ND	ND	268	ND	ND	ND	3.1 J	ND	43.6	1,440	ND
	5/15/2012	ND	ND	ND	ND	246	ND	ND	ND	3.2 J	ND	56.2	1,680[a]	ND
	6/7/2012	ND	ND	ND	ND	331	ND	ND	ND	3.7 J	ND	60.9	1,860[a]	ND
	7/17/2012	1.2J	ND	ND	ND	306 J	5.1	ND	ND	4.1 J	ND	61	1,690[a]	ND
	8/16/2012	ND	ND	ND	ND	387	2.1 J	ND	ND	3.6 J	ND	65.8	1,730[a]	ND
	9/13/2012	ND	ND	ND	ND	355	5.6 J	ND	ND	3 J	ND	73.1	1,780	ND
	10/11/2012	ND	ND	ND	ND	339	8	ND	ND	3.3 J	ND	78.1	1,310[a]	ND
	11/8/2012	190	4.2 J	203	4.1 J	380	3.2 J	ND	ND	5	ND	338	8,240	ND
	12/6/2012	ND	ND	ND	ND	322	ND	ND	ND	2.9 J	ND	65.8	1,830	ND
	1/10/2013	ND	ND	ND	ND	412	ND	ND	ND	17.5	ND	91.6	1,830	ND
	2/21/2013	ND	ND	ND	ND	548	25.5	ND	ND	10.4	ND	102	2,280[a]	ND
	3/14/2013	1.5 J	ND	ND	ND	486	1.9 J	ND	ND	7.6	ND	71	1,810[a]	ND
	4/4/2013	ND	ND	ND	ND	398	ND	ND	ND	7.8 J	ND	69.1	1,560	ND
	5/9/2013	ND	ND	ND	ND	357	ND	ND	ND	6.4 J	ND	71.1	1,880	ND
	6/13/2013	ND	ND	ND	ND	297	2 J	ND	ND	6.1	ND	62.7	1,750[a]	ND
	7/11/2013	ND	ND	ND	ND	367	1.6 J	ND	ND	4.8 J	ND	87.9	1,380[a]	ND
	8/8/2013	ND	ND	ND	ND	299	ND	ND	ND	5.6 J	ND	77.4	1,740	ND
	9/12/2013	ND	ND	ND	ND	349	9.5	ND	ND	5.8	ND	73	2,340[a]	ND
	10/10/2013	ND	ND	ND	ND	256	7.9 J	ND	ND	5.6 J	ND	46.5	2,480	ND
	11/14/2013	ND	ND	ND	ND	308	6.0	ND	ND	6.9	ND	65	2,450[a]	ND
	12/12/2013	ND	ND	ND	ND	487	ND	ND	ND	ND	ND	178	2,660	ND
	1/16/2014	ND	ND	ND	ND	440	10.4	ND	ND	ND	ND	101	2,210[a]	ND
	2/17/2014	ND	ND	ND	ND	704	ND	ND	ND	23	ND	142	4,880[a]	ND
	3/6/2014	ND	ND	ND	ND	214	ND	ND	ND	ND	ND	54.9	2,030	ND
	4/3/2014	ND	ND	ND	ND	235	ND	ND	ND	ND	ND	37.1	1,790	ND
	5/8/2014	ND	ND	ND	ND	229	ND	ND	ND	5.9	ND	36.3	2,190[a]	ND
	6/12/2014	ND	ND	ND	ND	313	ND	ND	ND	ND	ND	52	2,570	ND
	7/10/2014	ND	ND	ND	ND	209	ND	ND	ND	ND	ND	37.3	2,680[a]	ND
	8/14/2014	ND	ND	ND	ND	428	ND	ND	ND	ND	ND	78.8	2,790	ND
	9/11/2014	1.2	ND	ND	ND	306[a]	2.9	ND	ND	6.1	ND	76.9	2,590[a]	ND
	10/9/2014	ND	ND	ND	ND	322	9.8	ND	ND	ND	ND	81.3[a]	2,530[a]	ND
	11/13/2014	ND	ND	ND	ND	351	ND	ND	ND	ND	ND	47.4	2,770	ND
	12/11/2014	1.4	ND	ND	ND	388[a]	ND	ND	ND	ND	ND	74.6	2,230	ND
	1/15/2015	ND	ND	ND	ND	364	ND	ND	ND	ND	ND	57.3	2,620	ND
	2/12/2015	ND	ND	ND	ND	417	12.5	ND	ND	6.8	ND	66.4	2,660[a]	ND
	3/19/2015	ND	ND	ND	ND	298	ND	ND	ND	ND	ND	46	2,070	ND
	4/16/2015	ND	ND	ND	ND	2.8	ND	ND	ND	ND	ND	ND	22	ND
	5/14/2015	ND	ND	ND	ND	251	ND	ND	ND	ND	ND	44.6	1,960	ND
	6/11/2015	ND	ND	ND	ND	200	ND	ND	ND	ND	ND	ND	1,510	ND
	7/1/2015	ND	ND	ND	ND	293	ND	ND	ND	ND	ND	42.3	2,250b	ND
	8/13/2015	ND	ND	ND	ND	341	ND	ND	ND	ND	ND	66.1	2,360	ND
	9/17/2015	ND	ND	ND	ND	431	ND	ND	ND	ND	ND	92.5	2,040	ND
	10/15/2015	ND	ND	ND	ND	346	ND	ND	ND	ND	ND	69.9	1,880	ND
	11/12/2015	1.2	ND	ND	ND	313b	2.5	ND	ND	3.5	ND	84.6	1,170b	ND
	12/3/2015	ND	ND	ND	ND	265	ND	ND	ND	ND	ND	56.7	1,450b	ND
	1/14/2016	ND	ND	ND	ND	235	ND	ND	NDb	ND	ND	47.2	1,670	ND
	2/11/2016	ND	ND	ND	ND	233	ND	ND	NDb	ND	ND	46.9	1,320	ND
	3/17/2016	ND	ND	ND	ND	214	ND	ND	ND	ND	ND	35.4	1,270	ND
	4/14/2016	ND	ND	ND	ND	235	ND	ND	ND	ND	ND	42.5	1,360	ND
	5/12/2016	ND	ND	ND	ND	266	ND	ND	ND	ND	ND	46.6	1,770	ND
	6/23/2016	ND	ND	ND	ND	368	ND	ND	ND	ND	ND	83.1	1,730	ND
	7/14/2016	ND	ND	ND	ND	265	ND	ND	ND	ND	ND	63.9	1,720	ND
	8/11/2016	ND	ND	ND	ND	294	ND	ND	ND	ND	ND	72.9	1,650	ND
	9/9/2016	ND	ND	ND	ND	301	ND	ND	ND	ND	ND	83.8	1,430	ND
	10/13/2016	ND	ND	ND	ND	292	ND	ND	ND	ND	ND	76.5	1,720	ND
	11/17/2016	ND	ND	ND	ND	183	ND	ND	ND	ND	ND	52.2	1,280	ND
	12/7/2016	ND	ND	ND	ND	242	ND	ND	ND	ND	ND	59.7	1,670	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
EW-3 (continued)	1/12/2017	ND	ND	ND	ND	309	ND	ND	ND	ND	ND	68.0	1,540	ND
	2/16/2017	ND	ND	ND	ND	252	ND	ND	ND	ND	ND	46.6	1,280	ND
	3/12/2017	ND	ND	ND	ND	179	ND	ND	ND	ND	ND	29.3	1,310	ND
	4/13/2017	ND	ND	ND	ND	215	ND	ND	ND	ND	ND	40.4	1,460	ND
	5/11/2017	ND	ND	ND	ND	256	ND	ND	ND	ND	ND	57.8	1,350	ND
	6/15/2017	ND	ND	ND	ND	34	ND	ND	ND	ND	ND	106	1,750	ND
	7/25/2017	ND	ND	ND	ND	248	ND	ND	ND	ND	ND	64.1	1,230	ND
	8/16/2017	ND	ND	ND	ND	202	ND	ND	ND	ND	ND	62.5	1,180	ND
	9/19/2017	ND	ND	ND	ND	221	ND	ND	ND	ND	ND	63.0	1,120	ND
	10/12/2017	ND	ND	ND	ND	224	ND	ND	ND	ND	ND	71.9	1,070	ND
	11/16/2017	ND	ND	ND	ND	273	ND	ND	ND	ND	ND	76.6	1,040	ND
	12/14/2017	ND	ND	ND	ND	299	ND	ND	ND	ND	ND	86.9	1,270	ND
	1/11/2018	ND	ND	ND	ND	369	ND	ND	ND	ND	ND	105	1,280	ND
	2/15/2018	ND	ND	ND	ND	297	ND	ND	ND	ND	ND	75.2	1,020	ND
	3/15/2018	ND	ND	ND	ND	283	ND	ND	ND	ND	ND	84.7	1,080	ND
	4/12/2018	ND	ND	ND	ND	257	ND	ND	ND	ND	ND	73.4	1,030	ND
	5/17/2018	ND	ND	ND	ND	204	ND	ND	ND	ND	ND	74.5	1,050	ND
	6/14/2018	ND	ND	ND	ND	272	ND	ND	ND	ND	ND	99.9	1,130	ND
	7/19/2018	1.5	ND	ND	ND	195	1.7	ND	ND	ND	ND	97.5	921	ND
	8/17/2018	ND	ND	ND	ND	202	ND	ND	ND	ND	ND	62.5	1,180	ND
	9/13/2018	ND	ND	ND	ND	228	ND	ND	ND	ND	ND	88.3	894	ND
	10/10/2018	ND	ND	ND	ND	269	ND	ND	ND	ND	ND	97.8	1,110	ND
	11/15/2018	ND	ND	ND	ND	274	ND	ND	ND	ND	ND	96.7	936	ND
	12/13/2018	ND	ND	ND	ND	206	ND	ND	ND	ND	ND	84.1	885	ND
	1/17/2019	ND	ND	ND	ND	216	ND	ND	ND	ND	ND	85.5	889	ND
	2/14/2019	ND	ND	ND	ND	206	ND	ND	ND	ND	ND	59.3	1,010	ND
	3/14/2019	ND	ND	ND	ND	185	ND	ND	ND	ND	ND	35.0	871	ND
	4/11/2019	ND	ND	ND	ND	212	ND	ND	ND	ND	ND	45.6	1,220	ND
	5/16/2019	ND	ND	ND	ND	243	ND	ND	ND	ND	ND	61.2	1,300	ND
	6/13/2019	ND	ND	ND	ND	209	ND	ND	ND	ND	ND	45.9	1,130	ND
	7/11/2019	ND	ND	ND	ND	224	ND	ND	ND	ND	ND	63.7	1,380	ND
	8/15/2019	ND	ND	ND	ND	178	ND	ND	ND	ND	ND	50.6	1,100	ND
	9/12/2019	ND	ND	ND	ND	227	ND	ND	ND	ND	ND	76.4	1,140	ND
	10/10/2019	ND	ND	ND	ND	173	ND	ND	ND	ND	ND	42.6	871	ND
	11/13/2019	ND	ND	ND	ND	343	ND	ND	ND	ND	ND	84.6	1,360	ND
	12/12/2019	ND	ND	ND	ND	322	ND	ND	ND	ND	ND	75.3	952	ND
	1/16/2020	ND	ND	ND	ND	201	ND	ND	ND	ND	ND	47.4	943	ND
	2/13/2020	ND	ND	ND	ND	214	ND	ND	ND	ND	ND	50.3	896	ND
	3/12/2020	ND	ND	ND	ND	140	ND	ND	ND	ND	ND	41.4	726	ND
	4/16/2020	ND	ND	ND	ND	198	ND	ND	ND	ND	ND	32.6	938	ND
	5/15/2020	ND	ND	ND	ND	203	2.3 J	ND	ND	ND	ND	34.5	956	ND
	6/10/2020	ND	ND	ND	ND	191	ND	ND	ND	ND	ND	38.9	1,020	ND
	7/16/2020	ND	ND	ND	ND	175	ND	ND	ND	ND	ND	32.3	954	ND
	8/13/2020	ND	ND	ND	ND	163	ND	ND	ND	ND	ND	29.5	994	ND
	9/17/2020	ND	ND	ND	ND	151	ND	ND	ND	ND	ND	37.2	1,140	ND
	10/15/2020	ND	ND	ND	ND	154	ND	ND	ND	ND	ND	36.9	1,060	ND
	11/12/2020	ND	ND	ND	ND	184	ND	ND	ND	ND	ND	52.9	848	ND
	12/16/2020	ND	ND	ND	ND	220	ND	ND	ND	ND	ND	78.3	858	ND
	1/14/2021	ND	ND	ND	ND	181	ND	ND	ND	ND	ND	68.3	833	ND
	2/11/2021	ND	ND	ND	ND	189	ND	ND	ND	ND	ND	72.6	751	ND
	3/11/2021	ND	ND	ND	ND	184	ND	ND	ND	3.6 J	ND	53.1	863	ND
	4/15/2021	ND	ND	ND	ND	215	ND	ND	ND	ND	ND	68.5	907	ND
	5/13/2021	ND	ND	ND	ND	218	ND	ND	ND	ND	ND	58.8	1,100	ND
	6/14/2021	ND	ND	ND	ND	234	ND	ND	ND	ND	ND	56.4	976	ND
	7/20/2021	ND	ND	ND	ND	158	ND	ND	ND	ND	ND	19.4 J	1,020	ND
	8/19/2021	ND	ND	ND	ND	113	ND	ND	ND	ND	ND	40.5	624	ND
	9/16/2021	ND	ND	ND	ND	201	ND	ND	ND	ND	ND	80.6	836	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
EW-3 (continued)	10/14/2021	1.2 J	ND	ND	ND	176 [b] J	1.3 J	ND	ND	1.0 J	ND	64.9	650 [b]	ND
	11/20/2021	ND	ND	ND	ND	214	ND	ND	ND	ND	ND	62.6	855	ND
	12/16/2021	ND	ND	ND	ND	214	ND	ND	ND	ND	ND	67.8	826 [c]	ND
EW-4	9/23/2009	ND	ND	ND	ND	2,280	ND	ND	ND	ND	ND	ND	5,130	ND
	12/15/2009	11 J	ND	ND	ND	2,320	12.1 J	ND	ND	ND	ND	7.4 J	5,380	ND
	1/21/2010	ND	ND	ND	ND	2,180	14.5 J	ND	ND	ND	ND	ND	4,420	ND
	2/18/2010	ND	ND	ND	ND	2,190	10.5 J	ND	ND	ND	ND	ND	3,650	ND
	3/30/2010	6.4 J	ND	ND	ND	2,000	15.5	ND	ND	ND	ND	6.3 J	4,430	ND
	4/26/2010	7.9 J	ND	ND	ND	1,900	11.7	ND	ND	ND	ND	7.1 J	4,560	ND
	5/27/2010	5.6 J	ND	ND	ND	2,000	15.3	ND	ND	ND	ND	7.2 J	5,200	ND
	6/22/2010	ND	ND	ND	ND	1,710	20.7 J	ND	ND	ND	ND	ND	3,860	ND
	7/23/10[1]	ND	ND	ND	ND	1,760	154	ND	ND	ND	ND	ND	4,510	ND
	8/25/10[2]	5.4 J	ND	ND	ND	1,780	56.3	ND	ND	ND	ND	7.2 J	4,740	ND
	9/22/2010	6.9 J	ND	ND	ND	1,970	37.5	ND	ND	ND	ND	7.2 J	4,730	ND
	10/20/2010	6.3	ND	ND	ND	1,730	22.0	ND	ND	ND	ND	6.7	4,330	ND
	11/2/2010	6.0	ND	ND	ND	1,870	20.8	ND	ND	ND	ND	7.1	4,950	ND
	12/7/2010	8.2 J	ND	ND	ND	1,830	16.2	ND	ND	ND	ND	6.9 J	4,570	ND
	1/6/2011	ND	ND	ND	ND	1,440	7 J	ND	ND	ND	ND	ND	3,560	ND
	2/10/2011	ND	ND	ND	ND	1,330	33.1	ND	ND	ND	ND	ND	3,410	ND
	3/16/2011	5.5	ND	ND	ND	1,510	6.0	ND	ND	ND	ND	5.6	4,220	ND
	4/12/2011	8.0 J	ND	ND	ND	1,390	7.7 J	ND	ND	ND	ND	7.8J	4,580	ND
	5/19/2011	ND	ND	ND	ND	1,490	198	ND	ND	ND	ND	6.0	3,750	ND
	6/16/2011	5.0 J	ND	ND	ND	1,430	30.3	ND	ND	ND	ND	5.9 J	3,720	ND
	7/14/2011	5.6	ND	ND	ND	1,150	6.4	ND	ND	ND	ND	5.8	3,030	ND
	8/11/2011	ND	ND	ND	ND	1,380	64.4	ND	ND	ND	ND	7.5 J	3,640	ND
	9/8/2011	6.5	ND	ND	ND	1,230	24.4	ND	ND	ND	ND	7.3	2,850	ND
	10/13/2011	6.2 J	ND	ND	ND	1,250	21.8	ND	ND	ND	ND	7.3 J	3,430	ND
	11/10/2011	2	0.49 J	ND	ND	1,230	105	ND	ND	1 J	ND	6.5	3,140	0.69 J
	12/8/2011	7 J	ND	ND	ND	1,290	12.1	ND	ND	ND	ND	7.5 J	3,230	ND
	1/12/2012	4.1 J	ND	ND	ND	1,270	49.7	ND	ND	ND	ND	5.6	3,320	ND
	2/9/2012	6.1 J	ND	ND	ND	1,070	12.5	ND	ND	ND	ND	7.4 J	2,790[a]	ND
	3/15/2012	5.3 J	ND	ND	ND	1,210	17.1	ND	ND	ND	ND	8.0 J	3,100[a]	ND
	4/12/2012	5.2 J	ND	ND	ND	1,080	7.8 J	ND	ND	ND	ND	7.4 J	2,830[a]	ND
	5/15/2012	6.0 J	ND	ND	ND	1,180	8.7 J	ND	ND	ND	ND	7.4 J	3,220[a]	ND
	6/7/2012	ND	ND	ND	ND	1,070	13.5	ND	ND	ND	ND	6.6 J	3,040[a]	ND
	7/17/2012	7.0 J	ND	ND	ND	1,140	18.5	ND	ND	ND	ND	8.0 J	3,380[a]	ND
	8/16/2012	5.6 J	ND	ND	ND	1,200	5 J	ND	ND	ND	ND	5.9 J	3,430[a]	ND
	9/13/2012	ND	ND	ND	ND	706	9.2 J	ND	ND	ND	ND	6.7 J	2,240	ND
	10/11/2012	5.2 J	ND	ND	ND	1,060	27.1	ND	ND	ND	ND	7.7 J	3,440[a]	ND
	11/8/2012	8.2 J	ND	ND	ND	1,000	8.8 J	ND	ND	ND	ND	7.4 J	3,220	ND
	12/6/2012	5.1 J	ND	ND	ND	1,120	8.2 J	ND	ND	ND	ND	8.1 J	3,050	ND
	1/10/2013	6.5 J	ND	ND	ND	850	5.9 J	ND	ND	ND	ND	9.4 J	2,920	ND
	2/21/2013	3.5 J	ND	ND	ND	904	57.8	ND	ND	ND	ND	7.2 J	3,500[a]	ND
	3/14/2013	5.8	ND	ND	ND	569	3.0 J	ND	ND	1.3 J	ND	7.4	1,770[a]	ND
	4/4/2013	14.1	ND	ND	ND	765	10	ND	ND	ND	ND	5.0	3,220[a]	ND
	5/9/2013	ND	ND	ND	ND	846	ND	ND	ND	ND	ND	ND	3,810	ND
	6/13/2013	ND	ND	ND	ND	842	ND	ND	ND	ND	ND	ND	3,520	ND
	7/11/2013	7.0	ND	ND	ND	941	4.9 J	ND	ND	1.3 J	ND	8.8	2,780[a]	ND
	8/8/2013	ND	ND	ND	ND	1,000	ND	ND	ND	ND	ND	ND	4,110	ND
	9/12/2013	5.3 J	ND	ND	ND	881	4.6 J	ND	ND	ND	ND	5.9 J	3,260	ND
	10/10/2013	ND	ND	ND	ND	931	23.3	ND	ND	ND	ND	7.0 J	4,600[a]	ND
	11/14/2013	5.6	ND	ND	ND	861	9.9	ND	ND	ND	ND	9.1	3,220[a]	ND
	12/12/2013	7.3 J	ND	ND	ND	782	5.4 J	ND	ND	ND	ND	9.6 J	4,220[a]	ND
	1/16/2014	ND	ND	ND	ND	989	ND	ND	ND	ND	ND	ND	3,330	ND
	2/17/2014	ND	ND	ND	ND	1,260	ND	ND	ND	ND	ND	ND	4,090	ND
	3/6/2014	ND	ND	ND	ND	865	ND	ND	ND	ND	ND	ND	3,830[a]	ND
	4/3/2014	ND	ND	ND	ND	1,120	ND	ND	ND	ND	ND	ND	3,400	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
EW-4 (continued)	5/8/2014	5.7	ND	ND	ND	1,190	6.5	ND	ND	ND	ND	6.3	3,540[a]	ND
	6/12/2014	ND	ND	ND	ND	313	ND	ND	ND	ND	ND	52.0	4,090[a]	ND
	7/10/2014	ND	ND	ND	ND	829	24.2	ND	ND	ND	ND	ND	3,790[a]	ND
	8/14/2014	ND	ND	ND	ND	1,280	ND	ND	ND	ND	ND	ND	3,620	ND
	9/11/2014	ND	ND	ND	ND	1,120	ND	ND	ND	ND	ND	ND	3,190	ND
	10/9/2014	ND	ND	ND	ND	1,460	39.4	ND	ND	ND	ND	ND	3,350[a]	ND
	11/13/2014	ND	ND	ND	ND	1,490	ND	ND	ND	ND	ND	ND	3,450	ND
	12/11/2014	ND	ND	ND	ND	1,170	ND	ND	ND	ND	ND	ND	2,950	ND
	1/15/2015	ND	ND	ND	ND	928	ND	ND	ND	ND	ND	ND	2,650	ND
	2/12/2015	5.1	ND	ND	ND	1,070[a]	32.1	ND	ND	ND	ND	6.3	2,530[a]	ND
	3/19/2015	ND	ND	ND	ND	1,020	ND	ND	ND	ND	ND	ND	2,430	ND
	4/16/2015	ND	ND	ND	ND	953	ND	ND	ND	ND	ND	ND	2,180	ND
	5/14/2015	ND	ND	ND	ND	955	ND	ND	ND	ND	ND	ND	2,430	ND
	6/11/2015	ND	ND	ND	ND	831	ND	ND	ND	ND	ND	ND	1,990	ND
	7/1/2015	ND	ND	ND	ND	1,060	ND	ND	ND	ND	ND	ND	2,620b	ND
	8/13/2015	ND	ND	ND	ND	872	ND	ND	ND	ND	ND	ND	2,740	ND
	9/17/2015	ND	ND	ND	ND	843	ND	ND	ND	ND	ND	ND	2,110	ND
	10/15/2015	ND	ND	ND	ND	861	ND	ND	ND	ND	ND	ND	2,150b	ND
	11/12/2015	6.1	ND	ND	ND	897b	5.4	ND	ND	1.4	ND	7.0	2,350b	ND
	12/3/2015	ND	ND	ND	ND	827	ND	ND	ND	ND	ND	ND	2,210b	ND
	1/14/2016	ND	ND	ND	ND	881	ND	ND	NDb	ND	ND	ND	2,250	ND
	2/11/2016	ND	ND	ND	ND	826	ND	ND	NDb	ND	ND	ND	1,960	ND
	3/17/2016	ND	ND	ND	ND	803	ND	ND	ND	ND	ND	ND	1,950	ND
	4/14/2016	ND	ND	ND	ND	881	ND	ND	ND	ND	ND	ND	2,120	ND
	5/12/2016	ND	ND	ND	ND	1,050	ND	ND	ND	ND	ND	ND	2,740b	ND
	6/23/2016	ND	ND	ND	ND	782	ND	ND	ND	ND	ND	ND	1,840	ND
	7/14/2016	ND	ND	ND	ND	1,000	ND	ND	ND	ND	ND	ND	2,900b	ND
	8/11/2016	ND	ND	ND	ND	964	ND	ND	ND	ND	ND	ND	2,750	ND
	9/9/2016	ND	ND	ND	ND	877	ND	ND	ND	ND	ND	ND	2,290	ND
	10/13/2016	ND	ND	ND	ND	858	ND	ND	ND	ND	ND	ND	2,080	ND
	11/17/2016	ND	ND	ND	ND	816	ND	ND	ND	ND	ND	ND	2,100	ND
	12/7/2016	ND	ND	ND	ND	958	ND	ND	ND	ND	ND	ND	2,160	ND
	1/12/2017	ND	ND	ND	ND	828	ND	ND	ND	ND	ND	ND	2,130	ND
	2/16/2017	ND	ND	ND	ND	822	ND	ND	ND	ND	ND	ND	1,830	ND
	3/12/2017	ND	ND	ND	ND	822	ND	ND	ND	ND	ND	ND	2,280	ND
	4/13/2017	ND	ND	ND	ND	730	ND	ND	ND	ND	ND	ND	1,940	ND
	5/11/2017	ND	ND	ND	ND	636	ND	ND	ND	ND	ND	ND	1,580	ND
	6/15/2017	ND	ND	ND	ND	706	ND	ND	ND	ND	ND	ND	1,750	ND
	7/25/2017	ND	ND	ND	ND	574	ND	ND	ND	ND	ND	ND	1,640	ND
	8/16/2017	ND	ND	ND	ND	536	ND	ND	ND	ND	ND	ND	1,470	ND
	9/19/2017	ND	ND	ND	ND	564	ND	ND	ND	ND	ND	ND	1,420	ND
	10/12/2017	ND	ND	ND	ND	598	ND	ND	ND	ND	ND	ND	1,600	ND
	11/16/2017	ND	ND	ND	ND	473	ND	ND	ND	ND	ND	ND	1,270	ND
	12/14/2017	ND	ND	ND	ND	545	ND	ND	ND	ND	ND	ND	1,530	ND
	1/11/2018	ND	ND	ND	ND	537	ND	ND	ND	ND	ND	ND	1,430	ND
	2/15/2018	ND	ND	ND	ND	423	ND	ND	ND	ND	ND	ND	1,260	ND
	3/15/2018	ND	ND	ND	ND	349	ND	ND	ND	ND	ND	ND	1,090	ND
	4/12/2018	ND	ND	ND	ND	485	ND	ND	ND	ND	ND	ND	1,500	ND
	5/17/2018	ND	ND	ND	ND	351	ND	ND	ND	ND	ND	ND	1,260	ND
	6/14/2018	ND	ND	ND	ND	455	ND	ND	ND	ND	ND	ND	1,580	ND
	7/19/2018	5.6	ND	ND	ND	387	3.3	ND	ND	1.6	ND	ND	1,400	ND
	8/17/2018	ND	ND	ND	ND	536	ND	ND	ND	ND	ND	ND	1,470	ND
	9/13/2018	ND	ND	ND	ND	441	ND	ND	ND	ND	ND	ND	1,440	ND
	10/10/2018	ND	ND	ND	ND	465	ND	ND	ND	ND	ND	ND	1,710	ND
	11/15/2018	ND	ND	ND	ND	368	ND	ND	ND	ND	ND	ND	1,350	ND
	12/13/2018	ND	ND	ND	ND	448	ND	ND	ND	ND	ND	ND	1,430	ND
	1/17/2019	ND	ND	ND	ND	499	ND	ND	ND	ND	ND	ND	1,430	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
EW-4 (continued)	2/17/2019	ND	ND	ND	ND	552	ND	ND	ND	ND	ND	ND	1,680	ND
	3/14/2019	ND	ND	ND	ND	533	ND	ND	ND	ND	ND	ND	1,600	ND
	4/11/2019	ND	ND	ND	ND	604	ND	ND	ND	ND	ND	ND	1,940	ND
	5/16/2019	ND	ND	ND	ND	571	ND	ND	ND	ND	ND	ND	1,910	ND
	6/13/2019	ND	ND	ND	ND	538	ND	ND	ND	ND	ND	ND	1,850	ND
	7/11/2019	ND	ND	ND	ND	528	ND	ND	ND	ND	ND	ND	1,840	ND
	8/15/2019	ND	ND	ND	ND	380	ND	ND	ND	ND	ND	ND	1,600	ND
	9/12/2019	ND	ND	ND	ND	451	ND	ND	ND	ND	ND	ND	1,770	ND
	10/10/2019	ND	ND	ND	ND	362	ND	ND	ND	ND	ND	ND	1,380	ND
	11/13/2019	ND	ND	ND	ND	598	ND	ND	ND	ND	ND	ND	1,490	ND
	12/12/2019	ND	ND	ND	ND	393	ND	ND	ND	ND	ND	ND	1,200	ND
	1/16/2020	ND	ND	ND	ND	407	ND	ND	ND	ND	ND	ND	1,310	ND
	2/13/2020	ND	ND	ND	ND	458	ND	ND	ND	ND	ND	ND	1,470	ND
	3/12/2020	ND	ND	ND	ND	445	ND	ND	ND	ND	ND	4.7 J	1,370	ND
	4/16/2020	ND	ND	ND	ND	551	ND	ND	ND	ND	ND	ND	1,610	ND
	5/15/2020	ND	ND	ND	ND	456	ND	ND	ND	ND	ND	ND	1,300	ND
	6/10/2020	ND	ND	ND	ND	437	ND	ND	ND	ND	ND	ND	1,430	ND
	7/16/2020	ND	ND	ND	ND	501	ND	ND	ND	ND	ND	ND	1,690	ND
	8/13/2020	ND	ND	ND	ND	469	ND	ND	ND	ND	ND	ND	1,530	ND
	9/17/2020	ND	ND	ND	ND	352	ND	ND	ND	ND	ND	ND	1,340	ND
	10/15/2020	ND	ND	ND	ND	391	ND	ND	ND	ND	ND	ND	1,400	ND
	11/12/2020	ND	ND	ND	ND	553	ND	ND	ND	ND	ND	ND	1,590	ND
	12/16/2020	ND	ND	ND	ND	460	ND	ND	ND	ND	ND	ND	1,370	ND
	1/14/2021	ND	ND	ND	ND	457	ND	ND	ND	ND	ND	ND	1,300	ND
	2/11/2021	ND	ND	ND	ND	517	ND	ND	ND	ND	ND	5.7 J	1,080	ND
	3/11/2021	ND	ND	ND	ND	476	ND	ND	ND	ND	ND	6.0 J	1,260	ND
	4/15/2021	ND	ND	ND	ND	509	ND	ND	ND	ND	ND	ND	1,350	ND
	5/13/2021	ND	ND	ND	ND	503	ND	ND	ND	ND	ND	4.7 J	1,510	ND
	6/14/2021	3.2	ND	ND	ND	468	2.8	ND	ND	1.4 J	ND	4.5	1,300	ND
	7/20/2021	ND	ND	ND	ND	303	ND	ND	ND	ND	ND	6.6 J	1,120	ND
	8/19/2021	ND	ND	ND	ND	441	ND	ND	ND	ND	ND	12.1 J	1,430	ND
	9/16/2021	ND	ND	ND	ND	432	ND	ND	ND	ND	50.0 J	ND	1,540	ND
	10/14/2021	ND	ND	ND	ND	411	ND	ND	ND	ND	ND	ND	1,290	ND
	11/20/2021	ND	ND	ND	ND	418	ND	ND	ND	ND	ND	ND	1,220	ND
	12/16/2021	ND	ND	ND	ND	489	ND	ND	ND	ND	ND	ND	1,600	ND
EW-5	3/12/2020	ND	ND	ND	ND	796	ND	ND	ND	ND	ND	ND	13,800	ND
	4/16/2020	37.5	2.6	ND	10.6	763	1.2	22.3	ND	1.1	ND	47.7	11,100	1.5
	5/14/2020	ND	ND	ND	ND	580	ND	ND	ND	ND	ND	45.7 J	10,000	ND
	6/10/2020	32.7 J	ND	ND	ND	612	ND	ND	ND	ND	ND	47.5 J	10,700	ND
	7/16/2020	ND	ND	ND	ND	559	ND	ND	ND	ND	ND	44.8 J	8,900	ND
	8/13/2020	ND	ND	ND	ND	534	ND	ND	ND	ND	ND	52.8 J	7,200	ND
	9/17/2020	ND	ND	ND	ND	444	ND	ND	ND	ND	ND	47.8 J	7,060	ND
	10/15/2020	ND	ND	ND	ND	490	ND	ND	ND	ND	ND	36.8 J	7,360	ND
	11/12/2020	ND	ND	ND	ND	576	ND	ND	ND	ND	ND	54.1 J	6,640	ND
	12/16/2020	ND	ND	ND	ND	545	ND	ND	ND	ND	ND	ND	6,930	ND
	1/14/2021	ND	ND	ND	ND	589	ND	ND	ND	ND	ND	67.3 J	6,330	ND
	2/11/2021	ND	ND	ND	ND	688	ND	ND	ND	ND	ND	61.2 J	5,680	ND
	3/11/2021	ND	ND	ND	ND	717	ND	ND	ND	ND	ND	60.9 J	6,760	ND
	4/15/2021	ND	ND	ND	ND	761	ND	ND	ND	ND	ND	49.5 J	6,320	ND
	5/13/2021	ND	ND	ND	ND	709	ND	ND	ND	ND	ND	48.8 J	6,870	ND
	6/14/2021	ND	ND	ND	ND	707	16.6 J	ND	ND	ND	ND	56.9	5,520	ND
	7/20/2021	ND	ND	ND	ND	648	ND	ND	ND	ND	ND	52.3	5,130 [b]	ND
	8/19/2021	32.0 [b] J	ND	ND	ND	873	ND	ND	ND	ND	ND	59.5 J	5,900	ND
	9/16/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	249 J	35.2 J	4,290	ND
	10/14/2021	28.0 J	ND	ND	ND	541	ND	ND	ND	ND	ND	ND	3,620	ND
	11/20/2021	ND	ND	ND	ND	685	34.9 J	ND	ND	ND	ND	47.1 J	4,630	ND
	12/16/2021	44.5 J	ND	ND	ND	747	ND	ND	ND	ND	ND	52.1 [c] J	4,050 [c]	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
EW-10	9/18/2009	ND	ND	ND	ND	1,030	ND	ND	ND	ND	ND	ND	7,150	ND
	9/25/2009	ND	ND	ND	ND	831	ND	ND	ND	ND	ND	ND	7,440	ND
	9/30/2009	ND	ND	ND	ND	687	ND	ND	ND	ND	ND	ND	6,180	ND
	10/7/2009	ND	ND	ND	ND	774	ND	ND	ND	ND	ND	ND	5,380	ND
	11/5/2009	ND	ND	ND	ND	915	ND	ND	ND	ND	ND	ND	5,710	ND
	12/3/2009	5.6 J	ND	ND	ND	869	2.8 J	ND	ND	ND	ND	5.1 J	4,650	ND
	12/29/2009	4.6 J	ND	ND	ND	860	ND	ND	ND	ND	ND	4.4 J	6,120	ND
	1/21/2010	ND	ND	ND	ND	1,130	ND	ND	ND	ND	ND	ND	4,210	ND
	2/18/2010	ND	ND	ND	ND	1,080	ND	ND	ND	ND	ND	ND	5,330	ND
	3/30/2010	ND	ND	ND	ND	1,080	5.4 J	ND	ND	ND	ND	5.2 J	6,360	ND
	4/26/2010	ND	ND	ND	ND	1,180	ND	ND	ND	ND	ND	5.5 J	6,660	ND
	5/27/2010	ND	ND	ND	ND	1,290	ND	ND	ND	ND	ND	ND	6,760	ND
	6/22/2010	ND	ND	ND	ND	1,090	9.8 J	ND	ND	ND	ND	ND	6,250	ND
	7/23/2010	ND	ND	ND	ND	1,260	20.1 J	ND	ND	ND	ND	ND	6,370	ND
	8/25/2010	ND	ND	ND	ND	1,360	11.9	ND	ND	ND	ND	5.4 J	7,330	ND
	9/22/2010	ND	ND	ND	ND	1,670	ND	ND	ND	ND	ND	ND	7,820	ND
	10/20/2010	5.9 J	ND	ND	ND	1,550	9.1 J	ND	ND	ND	ND	5.8 J	7,600	ND
	11/2/2010	6.5 J	ND	ND	ND	1,990	5.6 J	ND	ND	ND	ND	6.5 J	9,800	ND
	12/7/2010	8.8 J	ND	ND	ND	2,260	7.8 J	ND	ND	ND	ND	6.6 J	9,350	ND
	1/6/2011	ND	ND	ND	ND	2,180	ND	ND	ND	ND	ND	ND	9,070	ND
	2/10/2011	ND	ND	ND	ND	2,510	7.2 J	ND	ND	ND	ND	ND	9,780	ND
	3/16/2011	ND	ND	ND	ND	2,590	7.7 J	ND	ND	ND	ND	ND	10,600	ND
	4/12/2011	9.2J	ND	ND	ND	2,880	8.9 J	ND	ND	ND	ND	6.1 J	11,200	ND
	5/19/2011	10	ND	ND	ND	3,040	29.1	ND	ND	ND	ND	5.8 J	11,100	ND
	6/16/2011	7.1 J	ND	ND	ND	3,040	ND	ND	ND	ND	8.6 J	ND	11,400	ND
	7/14/2011	8.8 J	ND	ND	ND	3,070	29	ND	ND	ND	ND	ND	10,200	ND
	8/11/2011	12.7	ND	ND	0.91 J	3,370	ND	ND	ND	ND	ND	8.0	12,200	4.3
	9/8/2011	10.7	ND	ND	ND	2,930	11.7	ND	ND	ND	ND	6.7 J	9,460	ND
	10/13/2011	ND	ND	ND	ND	3,610	ND	ND	ND	ND	ND	ND	13,200	ND
	11/10/2011	13.8	ND	ND	ND	4,000	17.1	ND	ND	ND	ND	5.6 J	14,400	4.8 J
	12/8/2011	16.5 J	ND	ND	ND	4,230	17.7 J	ND	ND	ND	ND	ND	15,400	ND
	1/12/2012	ND	ND	ND	ND	4,290	ND	ND	ND	ND	ND	ND	15,100	ND
	2/9/2012	ND	ND	ND	ND	3,520	ND	ND	ND	ND	ND	ND	12,400	ND
	3/15/2012	ND	ND	ND	ND	4,640	ND	ND	ND	ND	ND	ND	14,800[a]	ND
	4/12/2012	12.6J	ND	ND	ND	4,720[a]	13.6 J	ND	ND	ND	ND	ND	15,900[a]	ND
	5/15/2012	ND	ND	ND	ND	4,650	ND	ND	ND	ND	ND	ND	18,000[a]	ND
	6/7/2012	ND	ND	ND	ND	4,070[a]	12.7	ND	ND	ND	ND	5.3 J	15,100[a]	3.3 J
	7/17/2012	ND	ND	ND	ND	4,480	ND	ND	ND	ND	ND	ND	16,600	ND
	8/16/2012	13.9 J	ND	ND	ND	4,920[a]	10.8 J	ND	ND	ND	ND	ND	15,500[a]	ND
	9/13/2012	ND	ND	ND	ND	4,380[a]	ND	ND	ND	ND	ND	ND	17,200	ND
	10/11/2012	ND	ND	ND	ND	4,680	ND	ND	ND	ND	ND	ND	18,000[a]	ND
	11/8/2012	ND	ND	ND	ND	4,380	29.4 J	ND	ND	ND	ND	ND	15,900	ND
	12/6/2012	ND	ND	ND	ND	4,680	ND	ND	ND	ND	ND	ND	16,100	ND
	1/10/2013	ND	ND	ND	ND	4,270	ND	ND	ND	ND	ND	ND	16,700	ND
	2/21/2013	14.7 J	ND	ND	ND	4,560	18.7 J	ND	ND	ND	ND	ND	18,200[a]	ND
	3/14/2013	ND	ND	ND	ND	4,940	ND	ND	ND	ND	ND	ND	17,500	ND
	4/4/2013	ND	ND	ND	ND	4,740	ND	ND	ND	ND	ND	ND	18,800[a]	ND
	5/9/2013	ND	ND	ND	ND	4,580	ND	ND	ND	ND	ND	ND	18,000	ND
	6/13/2013	ND	ND	ND	ND	4,010	ND	ND	ND	ND	ND	ND	15,500	ND
	7/11/2013	ND	ND	ND	ND	4,150	ND	ND	ND	ND	ND	ND	14,600	ND
	8/8/2013	ND	ND	ND	ND	4,310	ND	ND	ND	ND	ND	ND	16,100	ND
	9/12/2013	ND	ND	ND	ND	4,030	ND	ND	ND	ND	ND	ND	13,700	ND
	10/10/2013	ND	ND	ND	ND	3,960	ND	ND	ND	ND	ND	ND	15,300	ND
	11/14/2013	ND	ND	ND	ND	3,770	9.7 J	ND	ND	ND	ND	ND	16,500[a]	ND
	12/12/2013	10.5	ND	ND	ND	2,980	11.2 J	ND	ND	ND	ND	ND	10,400[a]	ND
	1/16/2014	ND	ND	ND	ND	3,450	ND	ND	ND	ND	ND	ND	11,800	ND
	2/17/2014	ND	ND	ND	ND	3,780	ND	ND	ND	ND	ND	ND	13,600[a]	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
EW-10 (continued)	3/6/2014	ND	ND	ND	ND	2,580	ND	ND	ND	ND	ND	ND	13,500[a]	ND
	4/3/2014	ND	ND	ND	ND	2,940	ND	ND	ND	ND	ND	ND	10,500	ND
	5/8/2014	ND	ND	ND	ND	3,050	ND	ND	ND	ND	ND	ND	11,800[a]	ND
	6/12/2014	ND	ND	ND	ND	3,020	ND	ND	ND	ND	ND	ND	11,100[a]	ND
	7/10/2014	ND	ND	ND	ND	2,790	ND	ND	ND	ND	ND	ND	13,300[a]	ND
	8/14/2014	ND	ND	ND	ND	2,720	ND	ND	ND	ND	ND	ND	10,900[a]	ND
	9/11/2014	ND	ND	ND	ND	2,380	ND	ND	ND	ND	ND	ND	9,470[a]	ND
	10/9/2014	ND	ND	ND	ND	2,820	ND	ND	ND	ND	ND	ND	11,500[a]	ND
	11/13/2014	ND	ND	ND	ND	3,390	ND	ND	ND	ND	ND	ND	12,100	ND
	12/11/2014	ND	ND	ND	ND	2,490[a]	ND	ND	ND	ND	ND	ND	9,630[a]	ND
	1/15/2015	ND	ND	ND	ND	2,470	ND	ND	ND	ND	ND	ND	8,870[a]	ND
	2/12/2015	ND	ND	ND	ND	2,440	ND	ND	ND	ND	ND	ND	6,610[a]	ND
	3/19/2015	ND	ND	ND	ND	2,640	ND	ND	ND	ND	ND	ND	8,820[a]	ND
	4/16/2015	ND	ND	ND	ND	2,210	ND	ND	ND	ND	ND	ND	7,850	ND
	5/14/2015	ND	ND	ND	ND	1,890	ND	ND	ND	ND	ND	ND	8,140	ND
	6/11/2015	ND	ND	ND	ND	2,010	ND	ND	ND	ND	ND	ND	7,750	ND
	7/1/2015	ND	ND	ND	ND	1,960	ND	ND	ND	ND	ND	ND	8,160b	ND
	8/13/2015	ND	ND	ND	ND	1,780	ND	ND	ND	ND	ND	ND	7,220	ND
	9/17/2015	ND	ND	ND	ND	1,930	ND	ND	ND	ND	ND	ND	8,080	ND
	10/15/2015	ND	ND	ND	ND	1,830	ND	ND	ND	ND	ND	ND	8,040	ND
	11/12/2015	5.4	ND	ND	ND	2,420b	5.2	ND	ND	ND	ND	3.2	10,000b	1.8
	12/3/2015	ND	ND	ND	ND	1,770	ND	ND	ND	ND	ND	ND	7,490b	ND
	1/14/2016	ND	ND	ND	ND	1,660	ND	ND	NDb	ND	ND	ND	7,160b	ND
	2/11/2016	ND	ND	ND	ND	1,750	ND	ND	NDb	ND	ND	ND	7,520	ND
	3/17/2016	ND	ND	ND	ND	1,600	ND	ND	ND	ND	ND	ND	6,640	ND
	4/14/2016	ND	ND	ND	ND	1,550	ND	ND	ND	ND	ND	ND	5,890b	ND
	5/12/2016	ND	ND	ND	ND	1,580	ND	ND	ND	ND	ND	ND	6,530b	ND
	6/23/2016	ND	ND	ND	ND	1,490	ND	ND	ND	ND	ND	ND	5,920	ND
	7/14/2016	ND	ND	ND	ND	1,540	ND	ND	ND	ND	ND	ND	6,610	ND
	8/11/2016	ND	ND	ND	ND	1,480	ND	ND	ND	ND	ND	ND	6,310b	ND
	9/9/2016	ND	ND	ND	ND	1,360	ND	ND	ND	ND	ND	ND	6,010	ND
	10/13/2016	ND	ND	ND	ND	1,570	ND	ND	ND	ND	ND	ND	7,150	ND
	11/17/2016	ND	ND	ND	ND	1,560	ND	ND	ND	ND	ND	ND	6,210b	ND
	12/7/2016	ND	ND	ND	ND	1,860	ND	ND	ND	ND	ND	ND	7,990	ND
	1/12/2017	ND	ND	ND	ND	1,770	ND	ND	ND	ND	ND	ND	8,310	ND
	2/16/2017	ND	ND	ND	ND	1,550	ND	ND	ND	ND	ND	ND	6,080	ND
	3/12/2017	ND	ND	ND	ND	1,480	ND	ND	ND	ND	ND	ND	7,300	ND
	4/13/2017	ND	ND	ND	ND	1,410	ND	ND	ND	ND	ND	ND	6,840b	ND
	5/11/2017	ND	ND	ND	ND	1,390	ND	ND	ND	ND	ND	ND	6,150b	ND
	6/15/2017	ND	ND	ND	ND	1,350	ND	ND	ND	ND	ND	ND	6,260	ND
	7/25/2017	ND	ND	ND	ND	1,310	ND	ND	ND	ND	ND	ND	5,800	ND
	8/16/2017	ND	ND	ND	ND	1,230	ND	ND	ND	ND	ND	ND	4,810	ND
	9/19/2017	ND	ND	ND	ND	1,280	ND	ND	ND	ND	ND	ND	4,870	ND
	10/12/2017	ND	ND	ND	ND	1,370	ND	ND	ND	ND	ND	ND	5,680	MD
	11/16/2017	ND	ND	ND	ND	1,080	ND	ND	ND	ND	ND	ND	4,800b	MD
	12/14/2017	ND	ND	ND	ND	1,200	ND	ND	ND	ND	ND	ND	5,060	MD
	1/11/2018	ND	ND	ND	ND	1,380	ND	ND	ND	ND	ND	ND	3,250	ND
	2/15/2018	ND	ND	ND	ND	920	ND	ND	ND	ND	ND	ND	3,830	ND
	3/15/2018	ND	ND	ND	ND	973	ND	ND	ND	ND	ND	ND	4,340	ND
	4/12/2018	ND	ND	ND	ND	913	ND	ND	ND	ND	ND	ND	4,130	ND
	5/17/2018	ND	ND	ND	ND	873	ND	ND	ND	ND	ND	ND	3,730	ND
	6/14/2018	ND	ND	ND	ND	850	ND	ND	ND	ND	ND	ND	3,660	ND
	7/19/2018	2.4	ND	ND	ND	707	2	ND	ND	ND	ND	ND	3,240	ND
	8/17/2018	ND	ND	ND	ND	1,230	ND	ND	ND	ND	ND	ND	4,810	ND
	9/13/2018	ND	ND	ND	ND	712	ND	ND	ND	ND	ND	ND	2,910	ND
	10/10/2018	ND	ND	ND	ND	702	ND	ND	ND	ND	ND	ND	3,250	ND
	11/15/2018	1.1	ND	ND	ND	425	1.1	ND	ND	ND	ND	ND	1,620	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
EW-10 (Continued)	12/13/2018	ND	ND	ND	ND	574	ND	ND	ND	ND	ND	ND	2,200	ND
	1/17/2019	ND	ND	ND	ND	676	ND	ND	ND	ND	ND	ND	2,440	ND
	2/17/2019	ND	ND	ND	ND	720	ND	ND	ND	ND	ND	ND	2,440	ND
	3/14/2019	ND	ND	ND	ND	765	ND	ND	ND	ND	ND	ND	2,860	ND
	4/11/2019	ND	ND	ND	ND	741	ND	ND	ND	ND	ND	ND	3,050	ND
	5/16/2019	ND	ND	ND	ND	722	ND	ND	ND	ND	ND	ND	2,840	ND
	6/13/2019	ND	ND	ND	ND	605	ND	ND	ND	ND	ND	ND	2,340	ND
	7/11/2019	ND	ND	ND	ND	615	ND	ND	ND	ND	ND	ND	2,580	ND
	8/15/2019	ND	ND	ND	ND	557	ND	ND	ND	ND	ND	ND	2,570	ND
	9/12/2019	ND	ND	ND	ND	594	ND	ND	ND	ND	ND	ND	2,330	ND
	10/10/2019	ND	ND	ND	ND	514	ND	ND	ND	ND	ND	ND	2,140	ND
	11/13/2019	ND	ND	ND	ND	591	ND	ND	ND	ND	ND	ND	2,250	ND
	12/12/2019	ND	ND	ND	ND	442	ND	ND	ND	ND	ND	ND	1,760	ND
	1/16/2020	ND	ND	ND	ND	361	ND	ND	ND	ND	ND	ND	1,570	ND
	2/13/2020	ND	ND	ND	ND	363	ND	ND	ND	ND	ND	ND	1,540	ND
	3/12/2020	ND	ND	ND	ND	332	ND	ND	ND	ND	ND	ND	1,480	ND
	4/16/2020	ND	ND	ND	ND	557	ND	ND	ND	ND	ND	ND	2,190	ND
	5/15/2020	ND	ND	ND	ND	501	ND	ND	ND	ND	ND	ND	1,540	ND
	6/10/2020	ND	ND	ND	ND	575	ND	ND	ND	ND	ND	ND	2,320	ND
	7/16/2020	ND	ND	ND	ND	403	ND	ND	ND	ND	ND	ND	1,570	ND
	8/13/2020	ND	ND	ND	ND	422	ND	ND	ND	ND	ND	ND	1,940	ND
	9/17/2020	ND	ND	ND	ND	357	ND	ND	ND	ND	ND	ND	1,660	ND
	10/15/2020	ND	ND	ND	ND	406	ND	ND	ND	ND	ND	ND	1,920	ND
	11/12/2020	ND	ND	ND	ND	390	ND	ND	ND	ND	ND	ND	1,690	ND
	12/16/2020	ND	ND	ND	ND	443	ND	ND	ND	ND	ND	ND	1,600	ND
	1/14/2021	ND	ND	ND	ND	394	ND	ND	ND	ND	ND	ND	1,730	ND
	2/11/2021	ND	ND	ND	ND	497	ND	ND	ND	ND	ND	ND	1,880	ND
	3/11/2021	ND	ND	ND	ND	434	ND	ND	ND	ND	ND	ND	1,840	ND
	4/15/2021	ND	ND	ND	ND	407	ND	ND	ND	ND	ND	ND	1,560	ND
	5/13/2021	ND	ND	ND	ND	444	ND	ND	ND	ND	ND	ND	2,130	ND
	6/14/2021	ND	ND	ND	ND	416	ND	ND	ND	ND	ND	ND	1,950	ND
	7/20/2021	ND	ND	ND	ND	382	ND	ND	ND	ND	ND	ND	1,640	ND
	8/19/2021	ND	ND	ND	ND	470	ND	ND	ND	ND	ND	ND	1,980	ND
	9/16/2021	ND	ND	ND	ND	393	ND	ND	ND	ND	62.7 J	ND	1,940	ND
	10/14/2021	ND	ND	ND	ND	347	ND	ND	ND	ND	ND	ND	1,530	ND
	11/20/2021	ND	ND	ND	ND	383	ND	ND	ND	ND	ND	ND	1,510	ND
	12/16/2021	ND	ND	ND	ND	372	ND	ND	ND	ND	ND	ND	1,730	ND
EW-11	9/18/2009	466	ND	75.6 J	ND	14,500	50.2 J	ND	ND	ND	ND	283	19,300	ND
	9/25/2009	679	ND	103	ND	12,900	34.7 J	ND	ND	ND	ND	276	21,400	ND
	9/30/2009	573	ND	101	ND	11,000	30.6 J	ND	ND	ND	ND	223	19,200	ND
	10/7/2009	531	ND	ND	ND	9,570	ND	ND	ND	ND	ND	259	17,600	ND
	11/5/2009	589	ND	118	ND	7,500	35.6 J	ND	ND	ND	ND	183	13,700	ND
	12/3/2009	593	ND	148	ND	6,080	26.8	ND	ND	ND	ND	194	13,300	14.1 J
	12/29/2009	317	ND	94.1	ND	3,240	ND	ND	ND	ND	ND	144	8,950	ND
	1/21/2010	304	ND	75.2	ND	2,880	11.2 J	ND	ND	ND	ND	127	8,030	ND
	2/18/2010	218	ND	79.7	ND	2,710	7.8 J	ND	ND	ND	ND	90.9	6,090	ND
	3/30/2010	205	ND	61.5	ND	2,080	10.8	ND	ND	ND	ND	103	6,340	ND
	4/26/2010	239	ND	60.1	ND	2,160	13.3 J	ND	ND	ND	ND	101	5,990	ND
	5/27/2010	131	ND	ND	ND	1,620	ND	ND	ND	ND	ND	53.9	4,910	ND
	6/22/2010	158	ND	48.3	ND	1,800	17.6 J	ND	ND	ND	ND	73.3	4,930	ND
	7/23/2010	135	ND	56.8	ND	1,830	95.5	ND	ND	ND	ND	67.6	5,690	ND
	8/25/2010	177	ND	48.3	ND	1,820	35	ND	ND	ND	ND	81.6	5,030	ND
	9/22/2010	194	ND	47.7 J	ND	2,030	ND	ND	ND	ND	ND	66.3	5,350	ND
	10/20/2010	154	ND	42.1	ND	1,590	12.6	ND	ND	ND	ND	71.9	4,660	ND
	11/2/2010	168	ND	51.6	ND	1,870	ND	ND	ND	ND	ND	78.3	5,700	ND
	12/7/2010	186	3.7 J	44.4	ND	1,800	11.7	ND	ND	ND	ND	69.6	5,060	ND
	1/6/2011	161	ND	39.3	ND	1,580	6.8 J	ND	ND	ND	ND	58.4	4,450	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
EW-11 (Continued)	2/10/2011	154	ND	34.5	ND	1,390	10.2	ND	ND	ND	ND	62.7	4,330	ND
	3/16/2011	128	2.4 J	25.5	ND	1,460	5	ND	ND	ND	ND	49.7	4,220	3.6
	4/12/2011	132	ND	31.9	ND	1,260	5.4J	ND	ND	ND	ND	63.1	4,110	7.0 J
	5/19/2011	115	2.8 J	29.5	ND	1,430	41.0	ND	ND	ND	ND	55.4	3,980	9.9
	6/16/2011	121	2.5 J	27.8	ND	1,250	17.8	ND	ND	ND	ND	48.3	3,760	9.7 J
	7/14/2011	102	2.1 J	22.8	ND	1,010	17.4	ND	ND	ND	ND	42.8	2,870	6.3
	8/11/2011	152	3.0	30.3	1.3	1,480	6.8	ND	ND	0.63 J	ND	63.9	4,090	9.2
	9/8/2011	108	ND	25.4	ND	1,230	14.8	ND	ND	ND	ND	45.3	3,070	10.1
	10/13/2011	117	3.2 J	28.9	ND	1,420	30.0	ND	ND	ND	ND	50.3	3,890	10.7
	11/10/2011	99	2.4 J	20.2	ND	1,430	20.0	ND	ND	ND	ND	39.8	3,800	10
	12/8/2011**	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	1/12/2012**	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA	NA
	2/9/2012	1.1	2.9J	22.2	ND	1,420	12.2	ND	ND	ND	ND	41.3	3,210[a]	ND
	3/15/2012	110	ND	18.1	ND	1,450	5.9J	ND	ND	ND	ND	45	3,370[a]	23.9
	4/12/2012	94.1	ND	15.9	ND	1,280	18.1	ND	ND	ND	ND	43.7	3,530[a]	27.6
	5/15/2012	102	ND	17.5	ND	1,390	10.9	ND	ND	ND	ND	42.1	3,460[a]	27.9
	6/7/2012	73.9	2.9J	18.5	ND	1,340	15.5	ND	ND	ND	ND	34.7	3,250[a]	24.9
	7/17/2012	78.9	3.1J	17.1	ND	1,160	15.6	ND	ND	ND	ND	38.5	3,620[a]	18.6
	8/16/2012	94.9	ND	15.4	ND	1,380	3.4 J	ND	ND	ND	ND	36.3	3,510[a]	21.4
	9/13/2012	91	ND	15 J	ND	1,110	ND	ND	ND	ND	ND	36.5	3,250	16.9 J
	10/11/2012	97.8	2.4	15.7	0.87 J	1,010[a]	8.6	ND	ND	0.48 J	ND	39.7	2,540[a]	21.4
	11/8/2012	17.8	ND	9.6 J	ND	878	4.3 J	ND	ND	ND	ND	27.4	2,620	18.6
	12/6/2012	74.5	ND	11.2 J	ND	1,130	6.6 J	ND	ND	ND	ND	34.9	2,920	18.4 J
	1/10/2013	57.5	ND	11.4 J	ND	848	5.4 J	ND	ND	ND	ND	32.3	2,660	12.3 J
	2/21/2013	49.8	ND	8.2 J	ND	906	22.1	ND	ND	ND	ND	29.2	2,400[a]	15.9
	3/14/2013	72.7	ND	ND	ND	978	ND	ND	ND	ND	ND	29.2	2,520	21.4
	4/4/2013	65.3	ND	7	ND	919	3.9 J	ND	ND	ND	ND	25.7	2,690[a]	14
	5/9/2013	67.6	ND	9.1 J	ND	934	ND	ND	ND	ND	ND	28.4	2,810	15.7 J
	6/13/2013	65.3	ND	9.2 J	ND	861	ND	ND	ND	ND	ND	28.7	2,530[a]	13.3
	7/11/2013	65.5	1.7 J	6.4	ND	807	2.5 J	ND	ND	ND	ND	28.1	1,790[a]	14
	8/8/2013	43.1	ND	5.5 J	ND	783	ND	ND	ND	ND	7.7	25.7	1,570[a]	10.7
	9/12/2013	52.1	ND	5.3 J	ND	724	3.8 J	ND	ND	ND	ND	23.3	1,940	14.8
	10/10/2013	43.7	ND	ND	ND	653	ND	ND	ND	ND	ND	19.3 J	2,140	ND
	11/14/2013	45.7	ND	4.3 J	ND	670	4.6 J	ND	ND	ND	ND	21.2	1,950[a]	7.9
	12/12/2013	27.9	1.1 J	4	0.43 J	494	2.1	ND	ND	ND	ND	16.1	1,870[a]	4
	1/16/2014	35.3	ND	ND	ND	566	ND	ND	ND	ND	ND	16.8	1,610	ND
	2/17/2014	48.8	ND	ND	ND	611	ND	ND	ND	ND	ND	19.7	4,020	ND
	3/6/2014	34.4	ND	ND	ND	406	ND	ND	ND	ND	ND	19.1	1,690	ND
	4/3/2014	34.6	ND	ND	ND	464	ND	ND	ND	ND	ND	14.8	1,460[a]	ND
	5/8/2014	30.2	ND	ND	ND	435	ND	ND	ND	ND	ND	15.7	1,370[a]	ND
	6/12/2014	32.5	ND	ND	ND	448	ND	ND	ND	ND	ND	15.3	1,560	ND
	7/10/2014	25.5	ND	ND	ND	688	ND	ND	ND	ND	ND	17.9	1,530[a]	ND
	8/14/2014	26.8	ND	ND	ND	434	ND	ND	ND	ND	ND	11.4	1,370[a]	ND
	9/11/2014	23.9	ND	ND	ND	345	ND	ND	ND	ND	ND	13.4	1,360	ND
	10/9/2014	27.2	1.1	2.6	ND	466[a]	1.4	ND	ND	ND	ND	14.2[a]	1,570[a]	2.2
	11/13/2014	27.3	ND	ND	ND	466	ND	ND	ND	ND	ND	10.3	1,550	ND
	12/11/2014	24.8	ND	ND	ND	367	ND	ND	ND	ND	ND	12.6	1,390	ND
	1/15/2015	24.8	ND	ND	ND	352	ND	ND	ND	ND	ND	12.7	1,400[a]	ND
	2/12/2015	22.5	ND	ND	ND	332	ND	ND	ND	ND	ND	9.8	1,400[a]	ND
	3/19/2015	21.8	ND	ND	ND	336	ND	ND	ND	ND	ND	ND	1,190	ND
	4/16/2015	22.2	ND	ND	ND	288	ND	ND	ND	ND	ND	ND	980	ND
	5/14/2015	22.3	ND	ND	ND	263	ND	ND	ND	ND	ND	ND	1,120	ND
	6/11/2015	22.7	ND	ND	ND	267	ND	ND	ND	ND	ND	ND	987	ND
	7/1/2015	21.2	ND	ND	ND	298	ND	ND	ND	ND	ND	9.5	1,170b	ND
	8/13/2015	24.6	ND	ND	ND	305	ND	ND	ND	ND	ND	ND	1,240	ND
	9/17/2015	ND	ND	ND	ND	280	ND	ND	ND	ND	ND	ND	1,110	ND
	10/15/2015	18.5	ND	ND	ND	240	ND	ND	ND	ND	ND	ND	969	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
EW-11 (continued)	11/12/2015	4.9	ND	ND	ND	233b	ND	ND	ND	ND	ND	2.4	1,390b	1.6
	12/3/2015	16.9	ND	ND	ND	224	ND	ND	ND	ND	ND	ND	1,080b	ND
	1/14/2016	ND	ND	ND	ND	185	ND	ND	NDb	ND	ND	ND	997	ND
	2/11/2016	16.3	ND	ND	ND	226	ND	ND	NDb	ND	ND	ND	1,120c	ND
	3/17/2016	14.8	ND	ND	ND	208	ND	ND	ND	ND	ND	ND	914b	ND
	4/14/2016	14.1	ND	ND	ND	210	ND	ND	ND	ND	ND	ND	857	ND
	5/12/2016	ND	ND	ND	ND	204	ND	ND	ND	ND	ND	ND	1,110	ND
	6/23/2016	ND	ND	ND	ND	213	ND	ND	ND	ND	ND	ND	1,060	ND
	7/14/2016	ND	ND	ND	ND	204	ND	ND	ND	ND	ND	ND	1,120	ND
	8/11/2016	ND	ND	ND	ND	204	ND	ND	ND	ND	ND	ND	1,050	ND
	9/9/2016	ND	ND	ND	ND	165	ND	ND	ND	ND	ND	ND	933	ND
	10/13/2016	ND	ND	ND	ND	207	ND	ND	ND	ND	ND	ND	1,070	ND
	11/17/2016	ND	ND	ND	ND	176	ND	ND	ND	ND	ND	ND	1,170	ND
	12/7/2016	ND	ND	ND	ND	189	ND	ND	ND	ND	ND	ND	1,190	ND
	1/12/2017	ND	ND	ND	ND	188	ND	ND	ND	ND	ND	ND	1,120	ND
	2/16/2017	10.9	ND	ND	ND	188	ND	ND	ND	ND	ND	ND	942	ND
	3/12/2017	ND	ND	ND	ND	160	ND	ND	ND	ND	ND	ND	994	ND
	4/13/2017	ND	ND	ND	ND	139	ND	ND	ND	ND	ND	ND	968	ND
	5/11/2017	10.4	ND	ND	ND	165	ND	ND	ND	ND	ND	ND	943	ND
	6/15/2017	ND	ND	ND	ND	175	ND	ND	ND	ND	ND	ND	1,050	ND
	7/25/2017	ND	ND	ND	ND	163	ND	ND	ND	ND	ND	ND	912	ND
	8/17/2017	9.6	ND	ND	ND	169	ND	ND	ND	ND	ND	5.7	786b	ND
	9/19/2017	ND	ND	ND	ND	139	ND	ND	ND	ND	ND	ND	608	ND
	10/12/2017	10.0	ND	ND	ND	164	ND	ND	ND	ND	ND	ND	846	ND
	11/16/2017	10.4	ND	ND	ND	171	ND	ND	ND	ND	ND	ND	785	ND
	12/14/2017	ND	ND	ND	ND	166	ND	ND	ND	ND	ND	ND	879	ND
	1/11/2018	ND	ND	ND	ND	163	ND	ND	ND	ND	ND	ND	851	ND
	2/15/2018	ND	ND	ND	ND	125	ND	ND	ND	ND	ND	ND	589	ND
	3/15/2018	ND	ND	ND	ND	107	ND	ND	ND	ND	ND	ND	529	ND
	4/12/2018	ND	ND	ND	ND	113	ND	ND	ND	ND	ND	ND	565	ND
	5/17/2018	ND	ND	ND	ND	93.7	ND	ND	ND	ND	ND	ND	523	ND
	6/14/2018	ND	ND	ND	ND	117	ND	ND	ND	ND	ND	ND	634	ND
	7/19/2018	5.9	ND	ND	ND	93.7	ND	ND	ND	4.1	ND	3.3	509	ND
	8/17/2018	9.6	ND	ND	ND	169	ND	ND	ND	ND	ND	5.7	786	ND
	9/13/2018	ND	ND	ND	ND	129	ND	ND	ND	ND	ND	ND	605	ND
	10/10/2018	6.5	ND	ND	ND	124	ND	ND	ND	6	ND	ND	635	ND
	11/15/2018	ND	ND	ND	ND	103	ND	ND	ND	ND	ND	ND	480	ND
	12/13/2018	ND	ND	ND	ND	105	ND	ND	ND	ND	ND	ND	506	ND
	1/17/2019	6.0	ND	ND	ND	106	ND	ND	ND	ND	ND	ND	479	ND
	2/17/2019	ND	ND	ND	ND	107	ND	ND	ND	ND	ND	ND	590	ND
	3/14/2019	5.3	ND	ND	ND	104	ND	ND	ND	4.7	ND	2.9	482	ND
	4/11/2019	ND	ND	ND	ND	95.5	ND	ND	ND	ND	ND	ND	556	ND
	5/16/2019	5.6	ND	ND	ND	108	ND	ND	ND	5.3	ND	ND	531	ND
	6/13/2019	ND	ND	ND	ND	80.0	ND	ND	ND	5.2	ND	ND	499	ND
	7/11/2019	ND	ND	ND	ND	94.4	ND	ND	ND	ND	ND	ND	572	ND
	8/15/2019	ND	ND	ND	ND	76.1	ND	ND	ND	ND	ND	ND	504	ND
	9/12/2019	ND	ND	ND	ND	100.0	ND	ND	ND	6.9	ND	ND	557	ND
	10/10/2019	ND	ND	ND	ND	114.0	ND	ND	ND	ND	ND	ND	711	ND
	11/13/2019	ND	ND	ND	ND	94.3	ND	ND	ND	ND	ND	ND	593	ND
	12/12/2019	ND	ND	ND	ND	88.3	ND	ND	ND	5.5	ND	ND	450	ND
	1/16/2020	ND	ND	ND	ND	80.4	ND	ND	ND	5.2	ND	ND	462	ND
	2/13/2020	ND	ND	ND	ND	69.8	ND	ND	ND	ND	ND	ND	390	ND
	3/12/2020	ND	ND	ND	ND	58.5	ND	ND	ND	3.6 J	ND	ND	376	ND
	4/16/2020	3.2	ND	ND	ND	77.8	ND	ND	ND	4.0 J	ND	1.9 J	438	ND
	5/15/2020	3.5 J	ND	ND	ND	76.1	ND	ND	ND	4.5 J	ND	2.2 J	452	ND
	6/10/2020	5.1	ND	ND	ND	88.0	ND	ND	ND	5.8	ND	2.5 J	475	ND
	7/16/2020	2.9 J	ND	ND	ND	67.9	ND	ND	ND	4.3 J	ND	1.9 J	427	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
EW-11 (continued)	8/13/2020	2.9 J	ND	ND	ND	65.8	ND	ND	ND	4.8 J	ND	1.5 J	419	ND
	9/17/2020	4.4 J	ND	ND	ND	68.0	ND	ND	ND	5.5	ND	2.5 J	437	ND
	10/15/2020	3.9 J	ND	ND	ND	89.1	ND	ND	ND	6.7	ND	1.8 J	543	ND
	11/12/2020	4.1 J	ND	ND	ND	86.1	ND	ND	ND	5.6	ND	2.5 J	426	ND
	12/16/2020	4.5 J	ND	ND	ND	93.5	ND	ND	ND	5.6	ND	2.7 J	417	ND
	1/14/2021	4.6 J	ND	ND	ND	81.1	ND	ND	ND	5.6	ND	2.3 J	454	ND
	2/11/2021	4.8 J	ND	ND	ND	94.3	ND	ND	ND	5.5	ND	2.9 J	430	ND
	3/11/2021	4.6 J	ND	ND	ND	92.5	ND	ND	ND	5.5	ND	2.5 J	484	ND
	4/15/2021	3.0 J	ND	ND	ND	70.3	ND	ND	ND	3.6 J	ND	1.9 J	367	ND
	5/13/2021	4.4 J	ND	ND	ND	85.7	ND	ND	ND	6.6 J	ND	ND	494	ND
	6/14/2021	4.0 J	ND	ND	ND	83.8	ND	ND	ND	5.8	ND	2.3 J	428	ND
	7/20/2021	3.3 J	ND	ND	ND	70.5	ND	ND	ND	4.9 J	ND	1.9 J	371	ND
	8/19/2021	3.5 [d] J	ND	ND	ND	83.9	ND	ND	ND	5.2	ND	2.6 J	429	ND
	9/16/2021	3.3 J	ND	ND	ND	72.3	ND	ND	ND	5.3	13.6 J	1.7 J	410	ND
	10/14/2021	3.5 J	ND	ND	ND	66.6	ND	ND	ND	4.1 J	ND	2.4 J	331	ND
	11/20/2021	3.2 J	ND	ND	ND	74.8	ND	ND	ND	4.8 J	ND	1.9 J	355	ND
	12/16/2021	3.9 J	ND	ND	ND	75.0	ND	ND	ND	5.1	ND	ND	388	ND
EW-12	10/16/2014	ND	ND	ND	ND	152	ND	ND	ND	ND	ND	ND	1,240	ND
	3/19/2015	ND	ND	ND	ND	75.2	ND	ND	ND	ND	ND	ND	341[a]	ND
	4/16/2015	ND	ND	ND	ND	70.5	ND	ND	ND	ND	ND	ND	405	ND
	5/14/2015	ND	ND	ND	ND	75.4	ND	ND	ND	ND	ND	ND	270	ND
	6/11/2015	ND	ND	ND	ND	56.6	ND	ND	ND	ND	ND	ND	303	ND
	7/1/2015	ND	ND	ND	ND	73	ND	ND	ND	ND	ND	ND	361b	ND
	8/13/2015	ND	ND	ND	ND	62.4	ND	ND	ND	ND	ND	ND	360	ND
	9/17/2015	ND	ND	ND	ND	61.3	ND	ND	ND	ND	ND	ND	331	ND
	10/15/2015	ND	ND	ND	ND	55.4	ND	ND	ND	ND	ND	ND	296b	ND
	11/12/2015	ND	ND	ND	ND	52.2	ND	ND	ND	ND	ND	ND	252b	ND
	12/3/2015	ND	ND	ND	ND	48	ND	ND	ND	ND	ND	ND	259	ND
	1/14/2016	ND	ND	ND	ND	44.9	ND	ND	NDb	ND	ND	ND	283b	ND
	2/11/2016	ND	ND	ND	ND	113	ND	ND	NDb	ND	ND	ND	809	ND
	3/17/2016	ND	ND	ND	ND	91.9	ND	ND	NDb	ND	ND	ND	482b	ND
	4/14/2016	ND	ND	ND	ND	137	ND	ND	ND	ND	ND	ND	775	ND
	5/12/2016	ND	ND	ND	ND	124	ND	ND	ND	ND	ND	ND	832	ND
	6/23/2016	ND	ND	ND	ND	145	ND	ND	ND	ND	ND	ND	732	ND
	7/14/2016	ND	ND	ND	ND	142	ND	ND	ND	ND	ND	ND	843	ND
	8/11/2016	ND	ND	ND	ND	161	ND	ND	ND	ND	ND	ND	916b	ND
	9/9/2016	ND	ND	ND	ND	167	ND	ND	ND	ND	ND	ND	913b	ND
	10/13/2016	ND	ND	ND	ND	211	ND	ND	ND	ND	ND	ND	961	ND
	11/17/2016	ND	ND	ND	ND	203	ND	ND	ND	ND	ND	ND	1,180	ND
	12/7/2016	ND	ND	ND	ND	290	ND	ND	ND	ND	ND	ND	1,570	ND
	1/12/2017	ND	ND	ND	ND	372	ND	ND	ND	ND	ND	ND	1,950	ND
	2/16/2017	ND	ND	ND	ND	409	ND	ND	ND	ND	ND	ND	1,860	ND
	3/12/2017	ND	ND	ND	ND	405	ND	ND	ND	ND	ND	ND	1,990	ND
	4/13/2017	ND	ND	ND	ND	383	ND	ND	ND	ND	ND	ND	2,320	ND
	5/11/2017	ND	ND	ND	ND	513	ND	ND	ND	ND	ND	ND	2,320	ND
	6/15/2017	ND	ND	ND	ND	524	ND	ND	ND	ND	ND	ND	2,290	ND
	7/25/2017	ND	ND	ND	ND	241	ND	ND	ND	ND	ND	ND	1,140	ND
	8/16/2017	ND	ND	ND	ND	587	ND	ND	ND	ND	ND	ND	2,810	ND
	9/19/2017	ND	ND	ND	ND	813	ND	ND	ND	ND	ND	ND	3,360	ND
	10/12/2017	ND	ND	ND	ND	713	ND	ND	ND	ND	ND	ND	3,100	ND
	11/16/2017	ND	ND	ND	ND	801	ND	ND	ND	ND	ND	ND	3,480	ND
	12/14/2017	ND	ND	ND	ND	843	ND	ND	ND	ND	ND	ND	3,790	ND
	1/11/2018	ND	ND	ND	ND	1,070	ND	ND	ND	ND	ND	ND	4,720	ND
	2/15/2018	ND	ND	ND	ND	909	ND	ND	ND	ND	ND	ND	4,010	ND
	3/15/2018	ND	ND	ND	ND	1,030	ND	ND	ND	ND	ND	ND	4,840	ND
	4/12/2018	ND	ND	ND	ND	1,070	ND	ND	ND	ND	ND	ND	4,960	ND
	5/17/2018	ND	ND	ND	ND	1,040	ND	ND	ND	ND	ND	ND	4,780	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
EW-12 (continued)	6/14/2018	ND	ND	ND	ND	962	ND	ND	ND	ND	ND	ND	4,790	ND
	7/19/2018	5	1.6	ND	ND	859	3.6	ND	ND	ND	ND	1.7	4,700	8.6
	8/17/2018	ND	ND	ND	ND	587	ND	ND	ND	ND	ND	ND	2,810	ND
	9/13/2018	ND	ND	ND	ND	1,100	ND	ND	ND	ND	ND	ND	5,330	ND
	10/10/2018	ND	ND	ND	ND	1,020	ND	ND	ND	ND	ND	ND	5,450	ND
	11/15/2018	ND	ND	ND	ND	820	ND	ND	ND	ND	ND	ND	3,720	ND
	12/13/2018	ND	ND	ND	ND	890	ND	ND	ND	ND	ND	ND	4,050	ND
	1/17/2019	ND	ND	ND	ND	886	ND	ND	ND	ND	ND	ND	3,860	ND
	2/14/2019	ND	ND	ND	ND	660	ND	ND	ND	ND	ND	ND	3,430	ND
	3/14/2019	ND	ND	ND	ND	724	ND	ND	ND	ND	ND	ND	3,600	ND
	4/11/2019	ND	ND	ND	ND	670	ND	ND	ND	ND	ND	ND	3,590	ND
	5/16/2019	ND	ND	ND	ND	647	ND	ND	ND	ND	ND	ND	3,370	ND
	6/13/2019	ND	ND	ND	ND	576	ND	ND	ND	ND	ND	ND	3,350	ND
	7/11/2019	ND	ND	ND	ND	542	ND	ND	ND	ND	ND	ND	2,570	ND
	8/15/2019	ND	ND	ND	ND	586	ND	ND	ND	ND	ND	ND	3,290	ND
	9/12/2019	ND	ND	ND	ND	795	ND	ND	ND	ND	ND	ND	4,420	ND
	10/10/2019	ND	ND	ND	ND	630	ND	ND	ND	ND	ND	ND	3,180	ND
	11/13/2019	ND	ND	ND	ND	725	ND	ND	ND	ND	ND	ND	3,990	ND
	12/12/2019	ND	ND	ND	ND	675	ND	ND	ND	ND	ND	ND	3,400	ND
	1/16/2020	ND	ND	ND	ND	549	ND	ND	ND	ND	ND	ND	2,540	ND
	2/13/2020	ND	ND	ND	ND	645	ND	ND	ND	ND	ND	ND	3,480	ND
	3/12/2020	ND	ND	ND	ND	416	ND	ND	ND	ND	ND	ND	2,600	ND
	4/16/2020	ND	ND	ND	ND	ND	504	ND	ND	ND	ND	ND	2,870	ND
	5/15/2020	ND	ND	ND	ND	ND	393	ND	ND	ND	ND	ND	1,630	ND
	6/10/2020	ND	ND	ND	ND	ND	423	ND	ND	ND	ND	ND	2,380	ND
	7/16/2020	ND	ND	ND	ND	ND	396	ND	ND	ND	ND	ND	2,230	ND
	8/13/2020	ND	ND	ND	ND	ND	369	ND	ND	ND	ND	ND	2,320 [b]	ND
	9/17/2020	ND	ND	ND	ND	ND	385	ND	ND	ND	ND	ND	2,330	ND
	10/15/2020	ND	ND	ND	ND	ND	684	ND	ND	ND	ND	ND	2,630 [c]	ND
	11/12/2020	ND	ND	ND	ND	ND	438	ND	ND	ND	ND	ND	2,710	ND
	12/16/2020	ND	ND	ND	ND	ND	400	ND	ND	ND	ND	ND	2,560	ND
	1/14/2021	ND	ND	ND	ND	ND	443	ND	ND	ND	ND	ND	2,400 b	ND
	2/11/2021	ND	ND	ND	ND	ND	468	ND	ND	ND	ND	ND	2,400	ND
	3/11/2021	ND	ND	ND	ND	403	ND	ND	ND	ND	ND	ND	2,330	ND
	4/28/2021	Not Sampled												
	5/13/2021	ND	ND	ND	ND	296	ND	ND	ND	ND	ND	ND	1,620	ND
	6/14/2021	ND	ND	ND	ND	305	ND	ND	ND	ND	ND	ND	1,840	ND
	7/20/2021	ND	ND	ND	ND	232	ND	ND	ND	ND	ND	ND	1,240	ND
	8/19/2021	ND	ND	ND	ND	343	ND	ND	ND	ND	ND	ND	1,990	ND
	9/16/2021	ND	ND	ND	ND	298	ND	ND	ND	ND	66.3 J	ND	1,860	ND
	10/14/2021	ND	ND	ND	ND	298	ND	ND	ND	ND	ND	ND	1,750	ND
	11/20/2021	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM	NM
	12/16/2021	ND	ND	ND	ND	345	ND	ND	ND	ND	ND	ND	2,190	ND
FASW	10/7/2009	276	9 J	11.7	ND	6,110	37.1	ND	ND	ND	ND	76.7	6,700	8.2 J
	11/5/2009	307	ND	ND	ND	6,900	33.3 J	ND	ND	ND	ND	99.9	7,970	ND
	12/3/2009	175	ND	5 J	ND	3,880	11.2	ND	ND	ND	ND	76.8	4,910	ND
	12/29/2009	170	4.5 J	ND	ND	3,550	9.8 J	ND	ND	ND	ND	82.8	5,310	ND
	1/21/2010	156	ND	ND	ND	3,130	15 J	ND	ND	ND	ND	83.9	3,490	ND
	2/18/2010	99.6	ND	ND	ND	3,150	ND	ND	ND	ND	ND	58.5	4,590	ND
	3/30/2010	114	ND	3.8 J	ND	2,760	17.2	ND	ND	ND	ND	75.4	5,390	ND
	4/26/2010	137	3.8 J	4.1 J	ND	2,950	13.1	ND	ND	ND	ND	76.9	5,450	ND
	5/27/2010	93.1	ND	4.4 J	ND	2,130	5.3 J	ND	ND	ND	ND	54.8	4,580	ND
	6/22/2010	103	ND	ND	ND	2,420	11.6 J	ND	ND	ND	ND	63.7	4,760	ND
	7/23/2010	87.7	ND	ND	ND	2,430	128	ND	ND	ND	ND	59.4	4,950	ND
	8/25/2010	104	ND	3.6 J	ND	2,510	91.8	ND	ND	ND	ND	78	5,300	ND
	9/22/2010	137	ND	ND	ND	3,210	ND	ND	ND	ND	ND	73.5	5,510	ND
	10/20/2010	117	3.1 J	3.5 J	ND	2,730	19.1	ND	ND	ND	ND	72.2	5,590	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
FASW (continued)	11/2/2010	124	ND	4 J	ND	2,900	6 J	ND	ND	ND	ND	80.5	6,640	4.4 J
	12/7/2010	135	4.1 J	4.1 J	1.4 J	3,040	25.3	ND	ND	ND	ND	73.1	5,750	5.3
	1/6/2011	114	ND	ND	ND	2,630	8 J	ND	ND	ND	ND	59.3	5,210	ND
	2/10/2011	123	ND	ND	ND	2,580	ND	ND	ND	ND	ND	67.6	5,330	ND
	3/10/2011	121	ND	3.5 J	ND	2,400	14.5	ND	ND	ND	ND	73	5,660	6.1 J
	4/12/2011	106	ND	3.0J	ND	2,380	5.6 J	ND	ND	ND	ND	73.5	5,310	4.7 J
	5/19/2011	53.4	2.2 J	2.0 J	ND	1,800	141	ND	ND	ND	ND	51.0	4,540	5.4
	6/16/2011	72.7	ND	ND	ND	1,420	24.2	ND	ND	ND	ND	42.1	4,200	3.9 J
	7/14/2011	72.5	ND	ND	ND	1,430	19.4 J	ND	ND	ND	ND	41.4	4,130	ND
	8/11/2011	57.1	ND	ND	ND	1,360	25.6	ND	ND	ND	ND	41.9	3,680	ND
	9/8/2011	64.0	ND	1.9	ND	1,260	14.8	ND	ND	ND	ND	38.3	3,500	4.2
	10/13/2011	69.3	ND	ND	ND	1,280	16.4	ND	ND	ND	ND	39.6	3,830	3.9 J
	11/10/2011	29.4	1.6 J	1.9 J	0.79 J	1,210	76.8	ND	ND	0.55 J	ND	34.2	3,450	3.5
	12/8/2011	72.1	ND	ND	ND	1,350	9 J	ND	ND	ND	ND	38.7	4,070	5.5 J
	1/12/2012	67.5	ND	ND	ND	1,220	ND	ND	ND	ND	ND	31.7	3,520	5.9 J
	2/9/2012	55.9	ND	ND	ND	1,090	8.0 J	ND	ND	ND	ND	31.0	3,350[a]	9.0 J
	3/15/2012	58	ND	ND	ND	1,190	ND	ND	ND	ND	ND	31.8	3,360[a]	8.9
	4/21/2012	55.8	ND	ND	ND	1,080	6.9 J	ND	ND	ND	ND	34.3	3,760[a]	10.6
	5/15/2012	55.5	ND	ND	ND	1,130[a]	12.2	ND	ND	ND	ND	33.7	3,950[a]	9
	6/7/2012	35.6	ND	ND	ND	1,060	9.4 J	ND	ND	ND	ND	27.5	3,590[a]	9.6 J
	7/17/2012	FASW Offline - Pump Failure												
	8/16/2012	67.7	ND	ND	ND	1,300	ND	ND	ND	ND	ND	34.9	4,180[a]	11.8
	9/13/2012	60.4	ND	ND	ND	1,050	ND	ND	ND	ND	ND	32.3	4,070	ND
	10/11/2012	60.9	ND	ND	ND	1,120	2.7 J	ND	ND	ND	ND	3.2	4,130[a]	8.7
	11/8/2012	53.9	ND	ND	ND	949	5.9 J	ND	ND	ND	ND	30.4	3,720	10.3
	12/6/2012	57.5	ND	ND	ND	1,090	ND	ND	ND	ND	ND	29.8	3,610	11.7 J
	1/10/2013	54.7	ND	ND	ND	946	ND	ND	ND	ND	ND	32.4	3,590	12.6
	2/21/2013	51.7	ND	ND	ND	1,050	13.9	ND	ND	ND	ND	31.4	3,630[a]	10.9
	3/14/2013	61.7	ND	ND	ND	1,060	ND	ND	ND	ND	ND	27.3	3,740	10.7 J
	4/4/2013	71.2	ND	ND	ND	1,050	ND	ND	ND	ND	ND	26.8	3,580	ND
	5/9/2013	53.3	ND	ND	ND	963	ND	ND	ND	ND	ND	27.1 J	4,110	9.3 J
	6/13/2013	39.8	ND	ND	ND	784	ND	ND	ND	ND	ND	24.8 J	3,490	ND
	7/11/2013	42.1	ND	ND	ND	772	ND	ND	ND	ND	ND	22.6 J	2,740	ND
	8/8/2013	45.9	ND	ND	ND	1,010	ND	ND	ND	ND	25.6 J	29.9	3,920	ND
	9/12/2013	54.7	ND	ND	ND	961	ND	ND	ND	ND	ND	25.2	3,630[a]	16.8
	10/10/2013	47.3	ND	ND	ND	938	ND	ND	ND	ND	ND	26.4	4,210[a]	10
	11/14/2013	54.2	ND	ND	ND	1,050	2.2 J	ND	ND	ND	ND	28.8	4,180[a]	11.6
	12/12/2013	62.3	ND	ND	ND	1,010	ND	ND	ND	ND	ND	39	3,650[a]	12.5
	1/16/2014	44.4	ND	ND	ND	873	ND	ND	ND	ND	ND	22.9	3,230	ND
	2/17/2014	58.3	ND	ND	ND	957	ND	ND	ND	ND	ND	25.5	4,020	ND
	3/6/2014	43.7	ND	ND	ND	693	ND	ND	ND	ND	ND	266	3,630	ND
	4/3/2014	46.4	ND	ND	ND	828	ND	ND	ND	ND	ND	21.5	3,270	ND
	5/8/2014	38.9	ND	ND	ND	819	ND	ND	ND	ND	ND	21.8	2,800[a]	6.4
	6/12/2014	46.7	ND	ND	ND	896	ND	ND	ND	ND	ND	22.9	3,740[a]	ND
	7/10/2014	17.6	ND	ND	ND	688	ND	ND	ND	ND	ND	17.9	3,000[a]	ND
	8/14/2014	41.2	ND	ND	ND	888	ND	ND	ND	ND	ND	ND	3,430	ND
	9/11/2014	38.4	ND	ND	ND	761	ND	ND	ND	ND	ND	20.5	3,520	ND
	10/9/2014	52.7	ND	ND	ND	1,060	ND	ND	ND	ND	ND	25	4,000[a]	ND
	11/13/2014	39.1	ND	ND	ND	1,010	ND	ND	ND	ND	ND	ND	3,940	ND
	12/11/2014	40.2	ND	ND	ND	824	ND	ND	ND	ND	ND	ND	3,530	ND
	1/15/2015	36.3	ND	ND	ND	721	ND	ND	ND	ND	ND	ND	3,510	ND
	2/12/2015	39.2	ND	ND	ND	811	ND	ND	ND	ND	ND	18.7	3,120[a]	ND
	3/19/2015	44.7	ND	ND	ND	943	ND	ND	ND	ND	ND	23.1	3,520[a]	ND
	4/16/2015	70.1	ND	ND	ND	1,290	ND	ND	ND	ND	ND	31.2	3,040	ND
	5/14/2015	ND	ND	ND	ND	670	ND	ND	ND	ND	ND	ND	3,210	ND
	6/11/2015	ND	ND	ND	ND	729	ND	ND	ND	ND	ND	ND	3,250	ND
	7/1/2015	ND	ND	ND	ND	773	ND	ND	ND	ND	ND	ND	3,470	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
	8/13/2015	50.5	ND	ND	ND	722	ND	ND	ND	ND	ND	ND	3,390	ND
	9/17/2015	ND	ND	ND	ND	752	ND	ND	ND	ND	ND	ND	3,140	ND
	10/15/2015	ND	ND	ND	ND	681	ND	ND	ND	ND	ND	ND	3,140	ND
	11/12/2015	39.1	1.1	ND	ND	698b	1.5	ND	ND	ND	ND	23.6	3,230b	4.6
	12/3/2015	ND	ND	ND	ND	655	ND	ND	ND	ND	ND	ND	2,980	ND
	1/14/2016	ND	ND	ND	ND	567	ND	ND	NDb	ND	ND	ND	2,880	ND
	2/11/2016	ND	ND	ND	ND	664	ND	ND	NDb	ND	ND	ND	3,140	ND
	3/17/2016	36.0	ND	ND	ND	568	ND	ND	ND	ND	ND	ND	2,400	ND
	4/14/2016	33.1	ND	ND	ND	585	ND	ND	ND	ND	ND	ND	2,250	ND
	5/12/2016	ND	ND	ND	ND	625	ND	ND	ND	ND	ND	ND	3,060	ND
	6/23/2016	41.2	ND	ND	ND	716	ND	ND	ND	ND	ND	ND	3,040	ND
	7/14/2016	42.8	ND	ND	ND	718	ND	ND	ND	ND	ND	ND	3,090b	ND
	8/11/2016	ND	ND	ND	ND	705	ND	ND	ND	ND	ND	ND	2,990	ND
	9/9/2016	ND	ND	ND	ND	579	ND	ND	ND	ND	ND	ND	2,580	ND
	10/13/2016	ND	ND	ND	ND	694	ND	ND	ND	ND	ND	ND	2,840	ND
	11/17/2016	ND	ND	ND	ND	579	ND	ND	ND	ND	ND	ND	2,940	ND
	12/7/2016	ND	ND	ND	ND	725	ND	ND	ND	ND	ND	ND	3,440	ND
	1/12/2017	ND	ND	ND	ND	713	ND	ND	ND	ND	ND	ND	3,550	ND
	2/16/2017	ND	ND	ND	ND	636	ND	ND	ND	ND	ND	ND	2,700	ND
	3/12/2017	ND	ND	ND	ND	612	ND	ND	ND	ND	ND	ND	3,230	ND
	4/13/2017	ND	ND	ND	ND	542	ND	ND	ND	ND	ND	ND	3,130	ND
	5/11/2017	31.7	ND	ND	ND	555	ND	ND	ND	ND	ND	ND	2,480	ND
	6/15/2017	42.1	ND	ND	ND	669	ND	ND	ND	ND	ND	ND	2,790	ND
	7/25/2017	ND	ND	ND	ND	621	ND	ND	ND	ND	ND	ND	2,880	ND
	8/16/2017	34.0	ND	ND	ND	628	ND	ND	ND	ND	ND	ND	2,900b	ND
	9/19/2017	31.6	ND	ND	ND	606	ND	ND	ND	ND	ND	ND	2,390	ND
	10/12/2017	ND	ND	ND	ND	664	ND	ND	ND	ND	ND	ND	2,750	ND
	11/16/2017	32.7	ND	ND	ND	584	ND	ND	ND	ND	ND	ND	2,360	ND
	12/14/2017	30.0	ND	ND	ND	582	ND	ND	ND	ND	ND	ND	2,620	ND
	1/11/2018	26.9	ND	ND	ND	555	ND	ND	ND	ND	ND	ND	2,700	ND
	2/15/2018	29.3	ND	ND	ND	483	ND	ND	ND	ND	ND	ND	1,900	ND
	3/15/2018	28.2	ND	ND	ND	553	ND	ND	ND	ND	ND	ND	2,290	ND
	4/12/2018	ND	ND	ND	ND	367	ND	ND	ND	ND	ND	ND	1,320	ND
	5/17/2018	ND	ND	ND	ND	515	ND	ND	ND	ND	ND	ND	2,150	ND
	6/14/2018	ND	ND	ND	ND	538	ND	ND	ND	ND	ND	ND	2,370	ND
	7/19/2018	27.1	ND	ND	ND	483	ND	ND	ND	ND	ND	14.3	2,140	1.3
	8/17/2018	34	ND	ND	ND	628	ND	ND	ND	ND	ND	ND	2,900	ND
	9/13/2018	25.5	ND	ND	ND	548	ND	ND	ND	ND	ND	ND	2,150	ND
	10/10/2018	ND	ND	ND	ND	531	ND	ND	ND	ND	ND	ND	2,450	ND
	11/15/2018	ND	ND	ND	ND	450	ND	ND	ND	ND	ND	ND	1,770	ND
	12/13/2018	ND	ND	ND	ND	473	ND	ND	ND	ND	ND	ND	1,930	ND
	1/17/2019	28.9	ND	ND	ND	527	ND	ND	ND	ND	ND	ND	1,970	ND
	2/14/2019	ND	ND	ND	ND	513	ND	ND	ND	ND	ND	ND	2,230	ND
	3/14/2019	22.3	ND	ND	ND	509	ND	ND	ND	ND	ND	11.1	2,030	ND
	4/11/2019	ND	ND	ND	ND	484	ND	ND	ND	ND	ND	ND	2,090	ND
	5/16/2019	26.5	ND	ND	ND	524	ND	ND	ND	ND	ND	ND	2,170	ND
	6/13/2019	ND	ND	ND	ND	424	ND	ND	ND	ND	ND	ND	2,110	ND
	7/11/2019	23.6	ND	ND	ND	498	ND	ND	ND	ND	ND	ND	2,720	ND
	8/15/2019	ND	ND	ND	ND	456	ND	ND	ND	ND	ND	ND	1,710	ND
	9/12/2019	24.9	ND	ND	ND	535	ND	ND	ND	ND	ND	ND	1,860	ND
	10/10/2019	32.4	ND	ND	ND	672	ND	ND	ND	ND	ND	ND	2,070	ND
	11/13/2019	26.1	ND	ND	ND	612	ND	ND	ND	ND	ND	ND	2,000	ND
	12/12/2019	ND	ND	ND	ND	424	ND	ND	ND	ND	ND	ND	1,620	ND
	1/16/2020	ND	ND	ND	ND	443	ND	ND	ND	ND	ND	ND	1,800	ND
	2/13/2020	ND	ND	ND	ND	395	ND	ND	ND	ND	ND	ND	1,620	ND
	3/12/2020	12.4 J	ND	ND	ND	323	ND	ND	ND	ND	ND	7.1 J	1,390	ND
	4/16/2020	22.1	ND	ND	ND	411	ND	ND	ND	ND	ND	9.2 J	1,770	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
FASW (continued)	5/15/2020	17.5 J	ND	ND	ND	388	ND	ND	ND	ND	ND	9.2 J	1,670	ND
	6/10/2020	14.5 J	ND	ND	ND	346	ND	ND	ND	ND	ND	6.9 J	1,590	ND
	7/16/2020	18.3 J	ND	ND	ND	414	ND	ND	ND	ND	ND	9.2 J	1,790	ND
	8/13/2020	15.5 J	ND	ND	ND	360	ND	ND	ND	ND	ND	5.9 J	1,620	ND
	9/17/2020	18.5 J	ND	ND	ND	409	ND	ND	ND	ND	ND	8.6 J	1,950	ND
	10/15/2020	ND	ND	ND	ND	347	ND	ND	ND	ND	ND	ND	1,790	ND
	11/12/2020	3.8 J	ND	ND	ND	82.6	ND	ND	ND	5.8	11.3	2.1 J	416	ND
	1/14/2021	14.9 J	ND	ND	ND	283	ND	ND	ND	ND	ND	9.1 J	1,260	ND
	2/11/2021	22.1 J	ND	ND	ND	446	ND	ND	ND	ND	ND	8.9 J	1,560	ND
	3/11/2021	ND	ND	ND	ND	403	ND	ND	ND	ND	ND	ND	2,330	ND
	4/15/2021	14.6 J	ND	ND	ND	358	ND	ND	ND	ND	ND	8.1 J	1,440	ND
	5/13/2021	19.4 J	ND	ND	ND	403	ND	ND	ND	ND	ND	7.6 J	1,660	ND
	6/14/2021	ND	ND	ND	ND	342	ND	ND	ND	ND	ND	ND	1,450	ND
	7/20/2021	14.9 J	ND	ND	ND	348	ND	ND	ND	ND	ND	8.1 J	1,290	ND
	8/19/2021	15.3 [d] J	ND	ND	ND	419	ND	ND	ND	ND	ND	10.8 J	1,630	ND
	9/16/2021	16.7 J	ND	ND	ND	381	ND	ND	ND	ND	ND	9.1 J	1,670	ND
	10/14/2021	16.6 J	ND	ND	ND	325	ND	ND	ND	ND	ND	9.3 J	1,220	ND
	11/20/2021	15.6 J	ND	ND	ND	405	ND	ND	ND	ND	ND	6.6 J	1,460	ND
	12/16/2021	18.7 J	ND	ND	ND	386	ND	ND	ND	ND	ND	ND	1,620	ND
Left Toe Drain	9/18/2009	ND	ND	ND	ND	659	ND	ND	ND	ND	ND	ND	4,720	22.9 J
	9/25/2009	ND	ND	ND	ND	651	ND	ND	ND	ND	ND	ND	6,610	18.9 J
	9/30/2009	4.5 J	ND	ND	ND	747	2.2 J	ND	ND	ND	ND	ND	5,420	28.2
	10/7/2009	ND	ND	ND	ND	621	ND	ND	ND	ND	ND	ND	4,120	31.8
	11/5/2009	ND	ND	ND	ND	781	ND	ND	ND	ND	ND	ND	5,170	22.4 J
	12/29/2009	ND	ND	ND	ND	583	ND	ND	ND	ND	ND	ND	4,840	13.3
	2/18/2010	ND	ND	ND	ND	306	ND	ND	ND	ND	ND	ND	2,330	5.2 J
	3/30/2010	ND	ND	ND	ND	284	ND	ND	ND	ND	ND	ND	2,430	ND
	4/26/2010	4.9 J	ND	ND	ND	280	2.1 J	ND	ND	ND	ND	ND	2,280	5.8
	5/27/2010	ND	ND	ND	ND	340	ND	ND	ND	ND	ND	ND	3,100	8.6
	6/22/2010	ND	ND	ND	ND	413	ND	ND	ND	ND	ND	ND	3,170	13.9 J
	7/23/2010	ND	ND	ND	ND	594	15.1 J	ND	ND	ND	ND	ND	4,520	15.3 J
	8/25/2010	ND	ND	ND	ND	642	ND	ND	ND	ND	ND	ND	4,760	17
	9/22/2010	ND	ND	ND	ND	715	ND	ND	ND	ND	ND	ND	4,620	21.3 J
	10/20/2010	4.7 J	ND	ND	ND	735	ND	ND	ND	ND	ND	ND	5,520	20.5
	11/2/2010	5.2 J	ND	ND	ND	605	ND	ND	ND	ND	ND	ND	4,220	20.2
	12/7/2010	4.2 J	ND	ND	ND	659	ND	ND	ND	ND	ND	ND	5,210	20.1
	1/6/2011	6.3 J	ND	ND	ND	808	ND	ND	ND	ND	ND	ND	6,200	26.2
	2/10/2011	6.8 J	ND	ND	ND	836	ND	ND	ND	ND	ND	ND	6,360	25.7
	3/16/2011	ND	ND	ND	NA	664	2.8 J	NA	NA	ND	NA	ND	5,700	25.6
	4/12/2011	5.3J	ND	ND	ND	599	2.6 J	ND	ND	ND	ND	ND	4,210	18.2
	5/19/2011	3.8 J	ND	ND	ND	613	3.7 J	ND	ND	ND	ND	ND	3,490	19.3
	6/16/2011	3.2 J	ND	ND	NA	515	2.2 J	NA	NA	ND	NA	ND	3,330[a]	18
	7/14/2011	4.0 J	ND	ND	ND	595	2.2 J	ND	ND	ND	ND	ND	3,540	17.6
	8/11/2011	ND	ND	ND	ND	732	ND	ND	ND	ND	ND	ND	4,080	22
	9/8/2011	5.8	ND	ND	ND	716	3.2 J	ND	ND	ND	ND	ND	4,070	34
	10/13/2011	ND	ND	ND	ND	820	ND	ND	ND	ND	ND	ND	5,550	38.1
	11/10/2011	8.4	ND	ND	ND	851	5.2	ND	ND	ND	ND	ND	5,370	38.5
	12/8/2011	9.5 J	ND	ND	ND	1,000	5.7 J	ND	ND	ND	ND	ND	7,510	53.5
	1/12/2012	6.4 J	ND	ND	ND	899	ND	ND	ND	ND	ND	ND	6,710	42.1
	2/9/2012	7.5	0.35 J	ND	ND	879[a]	4.1	ND	ND	0.77 J	ND	ND	5,930[a]	51.3
	3/15/2012	ND	ND	ND	ND	926	ND	ND	ND	ND	ND	ND	5,510	38.0 J
	4/12/2012	4.3 J	ND	ND	ND	826	ND	ND	ND	ND	ND	ND	5,100[a]	38.6
	5/15/2012	ND	ND	ND	ND	792	ND	ND	ND	ND	ND	ND	4,570[a]	30.9
	6/7/2012	ND	ND	ND	ND	738	ND	ND	ND	ND	ND	ND	4,240[a]	30.4
	7/17/2012	ND	ND	ND	ND	773	ND	ND	ND	ND	ND	ND	3,900[a]	31.4
	8/16/2012	4.2 J	ND	ND	ND	757	ND	ND	ND	ND	ND	ND	4,100[a]	26
	9/13/2012	ND	ND	ND	ND	670	ND	ND	ND	ND	ND	ND	4,180	26.7

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
Left Toe Drain (continued)	10/11/2012	5.6 J	ND	ND	ND	662	ND	ND	ND	ND	ND	ND	4,170[a]	24.1
	11/8/2012	ND	ND	ND	ND	429	4.7 J	ND	ND	ND	ND	ND	1,980	13.9
	12/6/2012	4.9 J	ND	ND	ND	645	ND	ND	ND	ND	ND	ND	4,030	22.2
	1/10/2013	ND	ND	ND	ND	723	ND	ND	ND	ND	ND	ND	4,850	30.3
	2/21/2013	6.5 J	ND	ND	ND	887	6.8 J	ND	ND	ND	ND	ND	6,290[a]	32.3
	3/14/2013	5.9 J	ND	ND	ND	871	2.8 J	ND	ND	ND	ND	ND	4,690[a]	38.6
	4/4/2013	ND	ND	ND	ND	772	ND	ND	ND	ND	ND	ND	4,560[a]	22.8
	5/9/2013	ND	ND	ND	ND	516	ND	ND	ND	ND	ND	ND	3,160	19.6 J
	6/13/2013	ND	ND	ND	ND	444	ND	ND	ND	ND	ND	ND	2,800[a]	15.6
	7/11/2013	ND	ND	ND	ND	319	ND	ND	ND	ND	ND	ND	1,750[a]	9.6
	8/8/2013	ND	ND	ND	ND	371	ND	ND	ND	ND	ND	ND	1,860[a]	12.3
	9/12/2013	1.9 J	ND	ND	ND	352	ND	ND	ND	ND	ND	ND	1,960[a]	13.2
	10/10/2013	ND	ND	ND	ND	395	ND	ND	ND	ND	ND	ND	2,280	12.6 J
	11/14/2013	4.1 J	ND	ND	ND	557	ND	ND	ND	ND	ND	ND	3,440[a]	21.7
	12/12/2013	4.5 J	ND	ND	ND	436	ND	ND	ND	ND	ND	ND	3,560[a]	19.8
	1/16/2014	ND	ND	ND	ND	548	ND	ND	ND	ND	ND	ND	3,060	ND
	2/17/2014	ND	ND	ND	ND	438	ND	ND	ND	ND	ND	ND	2,750[a]	16.3
	3/6/2014	ND	ND	ND	ND	249	ND	ND	ND	ND	ND	ND	2,120[a]	12.3
	4/3/2014	ND	ND	ND	ND	207	ND	ND	ND	ND	ND	ND	1,200	ND
	5/8/2014	ND	ND	ND	ND	191	ND	ND	ND	ND	ND	ND	1,190	ND
	6/12/2014	ND	ND	ND	ND	242	ND	ND	ND	ND	ND	ND	1,410	ND
	7/10/2014	ND	ND	ND	ND	250	ND	ND	ND	ND	ND	ND	1,630[a]	8.5
	8/14/2014	ND	ND	ND	ND	410	ND	ND	ND	ND	ND	ND	2,330[a]	13.7
	9/11/2014	ND	ND	ND	ND	355	ND	ND	ND	ND	ND	ND	2,170[a]	13.5
	10/9/2014	ND	ND	ND	ND	586	ND	ND	ND	ND	ND	ND	2,910[a]	23.4
	11/13/2014	ND	ND	ND	ND	616	ND	ND	ND	ND	ND	ND	3,230	ND
	12/11/2014	4.3	ND	ND	ND	548[a]	2.4	ND	ND	ND	ND	ND	3,040	26.8
	1/15/2015	ND	ND	ND	ND	519	ND	ND	ND	ND	ND	ND	3,900	ND
	2/12/2015	3.1	ND	ND	ND	420[a]	1.7	ND	ND	ND	ND	ND	2,470[a]	16.9
	3/19/2015	ND	ND	ND	ND	388	ND	ND	ND	ND	ND	ND	2,380	ND
	4/16/2015	ND	ND	ND	ND	344	ND	ND	ND	ND	ND	ND	1,960	ND
	5/14/2015	ND	ND	ND	ND	273	ND	ND	ND	ND	ND	ND	1,690	15.8
	6/11/2015	ND	ND	ND	ND	300	ND	ND	ND	ND	ND	ND	1,680	ND
	7/1/2015	ND	ND	ND	ND	346	ND	ND	ND	ND	ND	ND	2,250b	13.5
	8/13/2015	ND	ND	ND	ND	351	ND	ND	ND	ND	ND	ND	2,200	ND
	9/17/2015	ND	ND	ND	ND	494	ND	ND	ND	ND	ND	ND	2,360b	ND
	10/15/2015	ND	ND	ND	ND	377	ND	ND	ND	ND	ND	ND	2,730	ND
	11/12/2015	3.6	ND	ND	ND	373	2.0	ND	ND	ND	ND	ND	2,660	18.6
	12/4/2015	ND	ND	ND	ND	386	ND	ND	ND	ND	ND	ND	2,910	ND
	1/14/2016	ND	ND	ND	ND	265	ND	ND	NDb	ND	ND	ND	1,950	ND
	2/11/2016	ND	ND	ND	ND	257	ND	ND	ND	ND	ND	ND	1,670	ND
	3/17/2016	ND	ND	ND	ND	235	ND	ND	ND	ND	ND	ND	1,460	ND
	4/14/2016	ND	ND	ND	ND	250	ND	ND	ND	ND	ND	ND	1,410	ND
	5/12/2016	ND	ND	ND	ND	216	ND	ND	ND	ND	ND	ND	1,530	ND
	6/16/2016	ND	ND	ND	ND	231	ND	ND	ND	ND	ND	ND	1,470	ND
	7/14/2016	ND	ND	ND	ND	259	ND	ND	ND	ND	ND	ND	1,620	ND
	8/11/2016	ND	ND	ND	ND	234	ND	ND	ND	ND	ND	ND	1,430	ND
	9/9/2016	ND	ND	ND	ND	198	ND	ND	ND	ND	ND	ND	1,140b	10.7
	10/13/2016	ND	ND	ND	ND	210	ND	ND	ND	ND	ND	ND	1,350	ND
	11/17/2016	ND	ND	ND	ND	177	ND	ND	ND	ND	ND	ND	1,150b	ND
	12/7/2016	ND	ND	ND	ND	197	ND	ND	ND	ND	ND	ND	1,480	ND
	1/12/2017	ND	ND	ND	ND	247	ND	ND	ND	ND	ND	ND	2,020	ND
	2/16/2017	ND	ND	ND	ND	217	ND	ND	ND	ND	ND	ND	1,600	ND
	3/12/2017	ND	ND	ND	ND	171	ND	ND	ND	ND	ND	ND	1,430	ND
	4/13/2017	ND	ND	ND	ND	138	ND	ND	ND	ND	ND	ND	1,220	ND
	5/11/2017	ND	ND	ND	ND	140	ND	ND	ND	ND	ND	ND	937b	ND
	6/15/2017	ND	ND	ND	ND	113	ND	ND	ND	ND	ND	ND	784	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
Left Toe Drain (continued)	7/25/2017	ND	ND	ND	ND	127	ND	ND	ND	ND	ND	ND	736	ND
	8/17/2017	ND	ND	ND	ND	115	ND	ND	ND	ND	ND	ND	649	ND
	9/19/2017	ND	ND	ND	ND	120	ND	ND	ND	ND	ND	ND	616	ND
	10/12/2017	ND	ND	ND	ND	117	ND	ND	ND	ND	ND	ND	660	ND
	11/16/2017	ND	ND	ND	ND	100	ND	ND	ND	ND	ND	ND	522	ND
	12/14/2017	ND	ND	ND	ND	109	ND	ND	ND	ND	ND	ND	687	ND
	1/11/2018	ND	ND	ND	ND	120	ND	ND	ND	ND	ND	ND	669	ND
	2/15/2018	ND	ND	ND	ND	92.9	ND	ND	ND	ND	ND	ND	585	ND
	3/15/2018	ND	ND	ND	ND	72.9	ND	ND	ND	ND	ND	ND	441	ND
	4/12/2018	ND	ND	ND	ND	81.5	ND	ND	ND	ND	ND	ND	463	ND
	5/17/2018	ND	ND	ND	ND	58.8	ND	ND	ND	ND	ND	ND	341	ND
	6/14/2018	ND	ND	ND	ND	42.3	ND	ND	ND	ND	ND	ND	224	ND
	7/19/2018	ND	ND	ND	ND	48.1	ND	ND	ND	ND	ND	ND	194	1.4
	8/17/2018	ND	ND	ND	ND	115	ND	ND	ND	ND	ND	ND	649	ND
	9/13/2018	ND	ND	ND	ND	37.6	ND	ND	ND	ND	ND	ND	154	ND
	10/10/2018	ND	ND	ND	ND	38.1	ND	ND	ND	ND	ND	ND	158	1.6
	11/15/2018	ND	ND	ND	ND	37.5	ND	ND	ND	ND	ND	ND	154	1.4
	12/13/2018	ND	ND	ND	ND	37.1	ND	ND	ND	ND	ND	ND	219	ND
	1/17/2019	ND	ND	ND	ND	43.8	ND	ND	ND	ND	ND	ND	228	1.1
	2/14/2019	ND	ND	ND	ND	32.8	ND	ND	ND	ND	ND	ND	205	ND
	3/14/2019	ND	ND	ND	ND	41.8	ND	ND	ND	ND	ND	ND	202	1.0
	4/11/2019	ND	ND	ND	ND	29.8	ND	ND	ND	ND	ND	ND	182	ND
	5/16/2019	ND	ND	ND	ND	26.9	ND	ND	ND	ND	ND	ND	139	ND
	6/16/2019	ND	ND	ND	ND	19.5	ND	ND	ND	ND	ND	ND	108	ND
	7/11/2019	ND	ND	ND	ND	23.3	ND	ND	ND	ND	ND	ND	108	ND
	8/15/2019	ND	ND	ND	ND	23.9	ND	ND	ND	ND	ND	ND	114	ND
	9/15/2019	ND	ND	ND	ND	22.0	ND	ND	ND	ND	ND	ND	98	ND
	10/10/2019	ND	ND	ND	ND	30.3	ND	ND	ND	ND	ND	ND	121	2.2
	11/13/2019	ND	ND	ND	ND	38.3	ND	ND	50.8	ND	ND	ND	146	3.4
	12/12/2019	ND	ND	ND	ND	31.2	ND	ND	ND	ND	ND	ND	117	2.6
	1/16/2020	ND	ND	ND	ND	36.9	ND	ND	ND	ND	ND	ND	149	ND
	2/13/2020	ND	ND	ND	ND	42.6	ND	ND	ND	ND	ND	ND	168	2.5
	3/12/2020	ND	ND	ND	ND	33.1	ND	ND	ND	ND	ND	ND	126	2.2 J
	4/16/2020	ND	ND	ND	ND	50.4	ND	ND	ND	ND	ND	ND	202	3.7 J
	5/15/2020	ND	ND	ND	ND	34.0	ND	ND	ND	ND	ND	ND	132	3.2
	6/10/2020	0.90 J	ND	ND	ND	36.9	ND	ND	ND	ND	ND	ND	113	3.4
	7/16/2020	0.81 J	ND	ND	ND	33.1 [d]	0.33 J	ND	ND	ND	ND	ND	74	1.8 [d] J
	8/13/2020	0.69 J	ND	ND	ND	41.1	ND	ND	ND	ND	ND	ND	81	3.9
	9/17/2020	0.74 J	ND	ND	ND	39.0	0.25 J	ND	ND	ND	ND	ND	83	5.4
	10/15/2020	0.58 J	ND	ND	ND	39.7	ND	ND	ND	ND	ND	ND	80	4.9 [c]
	11/12/2020	0.75 J	ND	ND	ND	45.7	0.23 J	ND	ND	ND	ND	ND	99	5.6
	12/16/2020	ND	ND	ND	ND	43.6	ND	ND	ND	ND	ND	ND	119	6.4
	1/14/2021	1.2 J	ND	ND	ND	47.8	ND	ND	ND	ND	ND	ND	159	5.7
	2/11/2021	1.5 J	ND	ND	ND	63.2	ND	ND	ND	ND	ND	ND	172	5.3
	3/11/2021	1.7 J	ND	ND	ND	57.9	ND	ND	ND	ND	ND	ND	184	5.2
	4/15/2021	1.3 J	ND	ND	ND	58.8	ND	ND	ND	ND	ND	ND	182	4.8
	5/13/2021	1.4 J	ND	ND	ND	56.6	ND	ND	ND	ND	ND	ND	188	4.6
	6/14/2021	ND	ND	ND	ND	57.9	ND	ND	ND	ND	ND	ND	156	4.4
	7/20/2021	0.75 J	ND	ND	ND	46.5	ND	ND	ND	ND	ND	ND	104	4.5
	8/19/2021	0.75 [d] J	ND	ND	ND	54.9	ND	ND	ND	ND	4.0 J	ND	116	7.2
	9/16/2021	0.92 J	ND	ND	ND	60.7	ND	ND	ND	ND	ND	ND	96.1 [b]	9
	10/14/2021	0.54 J	ND	ND	ND	48.7	ND	ND	ND	ND	ND	ND	83	4.3
	11/20/2021	0.52 J	ND	ND	ND	53.8	ND	ND	ND	ND	ND	ND	98	5.3
	12/16/2021	ND	ND	ND	ND	57.3	ND	ND	ND	ND	ND	ND	150 E	5.8
Right Toe Drain	9/18/2009	ND	ND	ND	ND	17.8	ND	ND	ND	ND	ND	ND	171	2
	12/29/2009	ND	ND	ND	ND	4.1	ND	ND	ND	ND	ND	ND	5	1.9
	2/18/2010	ND	ND	ND	ND	3.5	ND	ND	ND	ND	ND	ND	3	1.8

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
Right Toe Drain (continued)	3/30/2010	ND	ND	ND	ND	6.8	ND	ND	ND	ND	ND	ND	27	1.9
	4/26/2010	ND	ND	ND	ND	5.5	ND	ND	5.7 J	ND	ND	ND	12	1.9
	5/27/2010	ND	ND	ND	ND	7.9	ND	ND	3.6 J	ND	ND	ND	45	2.2
	6/22/2010	ND	ND	ND	ND	7.3	ND	ND	ND	ND	ND	ND	52	4
	7/23/2010	ND	ND	ND	ND	17.3	ND	ND	ND	ND	ND	ND	113	2.8
	8/25/2010	ND	ND	ND	ND	18.9	ND	ND	ND	ND	ND	ND	99	3.9
	9/22/2010	ND	ND	ND	ND	11.1	ND	ND	ND	ND	ND	ND	80	2.6
	10/20/2010	ND	ND	ND	ND	1.6	ND	ND	ND	ND	ND	ND	ND	2.3
	11/2/2010	ND	ND	ND	ND	1.1	ND	ND	ND	ND	ND	ND	0.34 J	1.9
	12/7/2010	ND	ND	ND	ND	2.5	ND	ND	ND	ND	ND	ND	3	2.6
	1/6/2011	ND	ND	ND	ND	3.8	ND	ND	ND	ND	ND	ND	16	2.1
	2/10/2011	ND	ND	ND	ND	5.9	ND	ND	ND	ND	ND	ND	28	2.1
	3/16/2011	ND	ND	ND	NA	4.9	ND	NA	NA	ND	NA	ND	4	2.6
	4/12/2011	ND	ND	ND	ND	6.1	ND	ND	ND	ND	ND	ND	19	2.5
	5/19/2011	ND	ND	ND	ND	3.2	ND	ND	15.5	ND	ND	ND	5	0.97 J
	6/16/2011	ND	ND	ND	NA	5.5	ND	NA	NA	ND	NA	ND	74	1.7
	7/14/2011	ND	ND	ND	ND	2.5 J	ND	ND	ND	ND	ND	ND	11	ND
	8/11/2011	ND	ND	ND	ND	4.1	ND	ND	18.4	ND	ND	ND	22	0.72 J
	9/8/2011	ND	ND	ND	ND	1.1	ND	ND	11.5	ND	ND	ND	0.38 J	ND
	10/13/2011	ND	ND	ND	ND	0.63 J	ND	ND	9.0 J	ND	ND	ND	0.42 J	0.79 J
	11/10/2011	ND	ND	ND	ND	14.4	ND	ND	8.7 J	ND	ND	ND	103	1.3
	12/8/2011	ND	ND	ND	ND	6.1	ND	ND	18	ND	ND	ND	38	2.3
	1/12/2012	ND	ND	ND	ND	7.2	ND	ND	ND	ND	ND	ND	21	2.5
	2/9/2012	ND	ND	ND	ND	4.4	ND	ND	10.8	ND	ND	ND	13	2.6
	3/15/2012	ND	ND	ND	ND	6.2	ND	ND	18.4	ND	ND	ND	14	4.5
	4/12/2012	ND	ND	ND	ND	6.2	ND	ND	ND	ND	ND	ND	32	3.3
	5/15/2012	ND	ND	ND	ND	6.1	ND	ND	ND	ND	ND	ND	30	2.4
	6/7/2012	ND	ND	ND	ND	6.9	ND	ND	25.5	ND	ND	ND	35	2.2
	7/17/2012	ND	ND	ND	ND	12.7	ND	ND	19.6	ND	ND	ND	79	0.81 J
	8/16/2012	ND	ND	ND	ND	2.8	ND	ND	25.3	ND	ND	ND	8	1.9
	9/13/2012	ND	ND	ND	ND	5.7	ND	ND	ND	ND	ND	ND	29	1.4
	10/11/2012	ND	ND	ND	ND	0.75 J	ND	ND	5.0 J	ND	ND	ND	7	0.52 J
	11/8/2012	ND	ND	ND	ND	4.8	ND	ND	4.6 J	ND	0.27 J	ND	27	0.66 J
	12/6/2012	ND	ND	ND	ND	5.1	ND	ND	ND	ND	ND	ND	31	1.1
	1/10/2013	0.28 J	ND	ND	ND	3.5	ND	ND	ND	ND	ND	ND	4	3.2
	2/21/2013	0.38 J	ND	ND	ND	7.3	ND	ND	ND	ND	ND	ND	18	2.8
	3/14/2013	0.52 J	ND	ND	ND	9.4	ND	ND	7.2 J	ND	ND	ND	18	4
	4/4/2013	ND	ND	ND	ND	7.4	ND	ND	ND	ND	ND	ND	10	2.1
	5/9/2013	ND	ND	ND	ND	8.9	ND	ND	ND	ND	ND	ND	42	2.1
	6/13/2013	ND	ND	ND	ND	8.2	ND	ND	ND	ND	ND	ND	31	1.7
	7/11/2013	0.25 J	ND	ND	ND	10.3	ND	ND	ND	ND	ND	ND	47	2.4
	8/8/2013	ND	ND	ND	ND	8.5	ND	ND	34.8	ND	ND	ND	35	3.3
	9/12/2013	ND	ND	ND	ND	6.4	ND	ND	6.6 J	ND	ND	ND	17	3.4
	10/10/2013	ND	ND	ND	ND	1.7	ND	ND	17.9	ND	ND	ND	8	2.4
	11/14/2013	ND	ND	ND	ND	2.2	ND	ND	13.8	ND	ND	ND	9	4.1
	12/12/2013	0.47 J	ND	ND	ND	4.9	ND	ND	ND	ND	ND	ND	10	3.6
	1/16/2014	ND	ND	ND	ND	5.0	ND	ND	ND	ND	ND	ND	11	2.2
	2/17/2014	ND	ND	ND	ND	5.9	ND	ND	ND	ND	ND	ND	16	1.9
	3/6/2014	ND	ND	ND	ND	3.4	ND	ND	ND	ND	ND	ND	8	2.9
	4/3/2014	ND	ND	ND	ND	5.0	ND	ND	ND	ND	ND	ND	11	2.3
	5/8/2014	ND	ND	ND	ND	3.5	ND	ND	ND	ND	ND	ND	5	1.4
	6/12/2014	ND	ND	ND	ND	3.4	ND	ND	ND	ND	ND	ND	3	2.2
	7/10/2014	ND	ND	ND	ND	1.7	ND	ND	121	ND	ND	ND	2	1.5
	8/14/2014	ND	ND	ND	ND	2.2	ND	ND	ND	ND	ND	ND	10	2.8
	9/11/2014	ND	ND	ND	ND	2.3	ND	ND	ND	ND	ND	ND	34	1.4
	10/9/2014	ND	ND	ND	ND	2.1	ND	ND	ND	ND	ND	ND	16	3.4
	11/13/2014	ND	ND	ND	ND	2.1	ND	ND	ND	ND	ND	ND	12	3.8

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
	12/11/2014	ND	ND	ND	ND	3	ND	ND	ND	ND	ND	ND	5	4.3
	1/15/2015	ND	ND	ND	ND	3.5	ND	ND	ND	ND	ND	ND	9	1.6
	2/12/2015	ND	ND	ND	ND	7.6	ND	ND	ND	ND	ND	ND	92	1.9
	3/19/2015	ND	ND	ND	ND	4.7	ND	ND	ND	ND	ND	ND	20	2.6
	4/16/2015	ND	ND	ND	ND	4.2	ND	ND	ND	ND	ND	ND	35	1.8
	5/14/2015	ND	ND	ND	ND	3.1	ND	ND	ND	ND	ND	ND	12	2
	6/11/2015	ND	ND	ND	ND	4.3	ND	ND	ND	ND	ND	ND	51	1.4
	7/1/2015	ND	ND	ND	ND	4.9	ND	ND	ND	ND	ND	ND	72	ND
	8/13/2015	ND	ND	ND	ND	2.8	ND	ND	ND	ND	ND	ND	39	ND
	9/17/2015	ND	ND	ND	ND	1.8	ND	ND	ND	ND	ND	ND	14	ND
	10/15/2015	ND	ND	ND	ND	3.2	ND	ND	ND	ND	ND	ND	11	1.6
	11/12/2015	ND	ND	ND	ND	4.9	ND	ND	ND	ND	ND	ND	50	ND
	12/4/2015	ND	ND	ND	ND	5.8	ND	ND	ND	ND	ND	ND	70	2.7
	1/14/2016	ND	ND	ND	ND	4.3	ND	ND	NDb	ND	ND	ND	53	1.6
	2/11/2016	ND	ND	ND	ND	4.6	ND	ND	ND	ND	ND	ND	45	1.6
	3/17/2016	ND	ND	ND	ND	4.9	ND	ND	ND	ND	ND	ND	27	2.2
	4/14/2016	ND	ND	ND	ND	5.6	ND	ND	ND	ND	ND	ND	31	2.0
	5/12/2016	ND	ND	ND	ND	4.4	ND	ND	ND	ND	ND	ND	29	2.8
	6/16/2016	ND	ND	ND	ND	3.2	ND	ND	ND	ND	ND	ND	32	1.4
	7/14/2016	ND	ND	ND	ND	1.1	ND	ND	ND	ND	ND	ND	5	ND
	8/11/2016	ND	ND	ND	ND	3.3	ND	ND	ND	ND	ND	ND	50	1.5
	9/9/2016	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2	ND
	10/13/2016	ND	ND	ND	ND	3.1	ND	ND	ND	ND	ND	ND	15	1.1
	11/17/2016	ND	ND	ND	ND	4.1	ND	ND	ND	ND	ND	ND	17	ND
	12/7/2016	ND	ND	ND	ND	1.2	ND	ND	ND	ND	ND	ND	4	1.6
	1/12/2017	ND	ND	ND	ND	6.5	ND	ND	ND	ND	ND	ND	25	ND
	2/16/2017	ND	ND	ND	ND	6.8	ND	ND	ND	ND	ND	ND	12	1.7
	3/12/2017	ND	ND	ND	ND	10.3	ND	ND	ND	ND	ND	ND	14	2.3
	4/13/2017	ND	ND	ND	ND	5.9	ND	ND	ND	ND	ND	ND	14	2.0
	5/11/2017	ND	ND	ND	ND	4.9	ND	ND	ND	ND	ND	ND	19	ND
	6/15/2017	ND	ND	ND	ND	2.3	ND	ND	ND	ND	ND	ND	11	ND
	7/25/2017	ND	ND	ND	ND	4.0	ND	ND	ND	ND	ND	ND	25	ND
	8/16/2017	ND	ND	ND	ND	2.4	ND	ND	ND	ND	ND	ND	14	ND
	9/19/2017	ND	ND	ND	ND	2.8	ND	ND	ND	ND	ND	ND	14	ND
	10/12/2017	ND	ND	ND	ND	3.4	ND	ND	ND	ND	ND	ND	21	ND
	11/16/2017	ND	ND	ND	ND	2.4	ND	ND	ND	ND	ND	ND	11	ND
	12/14/2017	ND	ND	ND	ND	2.1	ND	ND	ND	ND	ND	ND	4	ND
	1/11/2018	ND	ND	ND	ND	3.2	ND	ND	ND	ND	ND	ND	7	ND
	2/15/2018	ND	ND	ND	ND	6.2	ND	ND	ND	ND	ND	ND	24	ND
	3/15/2018	ND	ND	ND	ND	2.7	ND	ND	ND	ND	ND	ND	4	ND
	4/12/2018	ND	ND	ND	ND	3	ND	ND	ND	ND	ND	ND	18	ND
	5/17/2018	ND	ND	ND	ND	3.6	ND	ND	ND	ND	ND	ND	12	ND
	6/14/2018	ND	ND	ND	ND	1.2	ND	ND	ND	ND	ND	ND	5	ND
	7/19/2018	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	4	ND
	8/17/2018	ND	ND	ND	ND	2.4	ND	ND	ND	ND	ND	ND	14	ND
	9/13/2018	ND	ND	ND	ND	1.8	ND	ND	ND	ND	ND	ND	10	ND
	10/10/2018	ND	ND	ND	ND	1.1	ND	ND	ND	ND	ND	ND	4	ND
	11/15/2018	ND	ND	ND	ND	1.6	ND	ND	ND	ND	ND	ND	ND	ND
	12/13/2018	ND	ND	ND	ND	1.6	ND	ND	ND	ND	ND	ND	ND	ND
	1/17/2019	ND	ND	ND	ND	1.3	ND	ND	ND	ND	ND	ND	ND	1.1
	2/14/2019	ND	ND	ND	ND	1.2	ND	ND	ND	ND	ND	ND	1	ND
	3/14/2019	ND	ND	ND	ND	2.1	ND	ND	ND	ND	ND	ND	2	1.2
	4/11/2019	ND	ND	ND	ND	1.8	ND	ND	ND	ND	ND	ND	2	1.3
	5/16/2019	ND	ND	ND	ND	1.2	ND	ND	ND	ND	ND	ND	4	ND
	6/16/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2	ND
	7/11/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	1	ND
	8/15/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2	ND

Appendix A Table 2
Groundwater Treatment Analytical Data
FPE Groundwater Treatment System
Edgefield, South Carolina

Location	Date	Volatile Organic Compounds												
		1,1-DCE (µg/L)	*1,1-DCA (µg/L)*	*1,1,1-TCA (µg/L)*	*1,1,2-TCA (µg/L)*	*cis-1,2-DCE (µg/L)*	*trans-1,2-DCE (µg/L)*	*MEK (µg/L)*	*Acetone (µg/L)*	*Chloroform (µg/L)*	*Methylene Chloride (µg/L)*	*PCE (µg/L)*	*TCE (µg/L)*	*VC (µg/L)*
Right Toe Drain (continued)	9/12/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	10/10/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	11/13/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	12/12/2019	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND
	1/16/2020	ND	ND	ND	ND	1.6	ND	ND	ND	ND	ND	ND	ND	ND
	2/13/2020	ND	ND	ND	ND	2.5	ND	ND	ND	ND	ND	ND	4	ND
	3/14/2020	ND	ND	ND	ND	1.7	ND	ND	ND	ND	ND	ND	3	0.79 J
	4/16/2020	ND	ND	ND	ND	1.6 J	ND	ND	ND	ND	ND	ND	3	0.73 J
	5/15/2020	ND	ND	ND	ND	0.63 J	ND	ND	ND	ND	ND	ND	1	ND
	6/10/2020	ND	ND	ND	ND	1.0	ND	ND	ND	ND	ND	ND	1	0.64 J
	7/16/2020	ND	ND	ND	ND	1.4 J	ND	ND	ND	ND	ND	ND	2	0.96 J
	8/13/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	2	ND
	9/17/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.53 J
	10/15/2020	ND	ND	ND	ND	0.41 J	ND	ND	ND	ND	ND	ND	1	ND
	11/12/2020	ND	ND	ND	ND	1.4 J	ND	ND	ND	ND	ND	ND	2	ND
	12/16/2020	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.68 J
	1/14/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.65 J
	2/11/2021	ND	ND	ND	ND	2.2	ND	ND	ND	ND	ND	ND	4	1.0
	3/11/2021	ND	ND	ND	ND	0.69 J	ND	ND	ND	ND	ND	ND	0.37 J	0.89 J
	4/15/2021	ND	ND	ND	ND	1.7	ND	ND	ND	ND	ND	ND	3	1.3
	5/13/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.42 J
	6/14/2021	ND	ND	ND	ND	1.3	ND	ND	14.6 J	ND	ND	ND	4	ND
	7/20/2021	ND	ND	ND	ND	1.6	ND	ND	ND	ND	ND	ND	3	0.69 J
	8/19/2021	ND	ND	ND	ND	3.2	ND	ND	ND	ND	ND	ND	6	1.2
	9/16/2021	ND	ND	ND	ND	2.7	ND	ND	ND	ND	ND	ND	7	ND
	10/14/2021	ND	ND	ND	ND	1.7	ND	ND	ND	ND	ND	ND	3	0.48 J
	11/20/2021	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	ND	0.38 J	ND
	12/16/2021	ND	ND	ND	ND	1.2	ND	ND	11.5 J	ND	ND	ND	2.0	ND

Notes

J - Estimated Value

NA - Not Analyzed

ND - Not Detected

DCA - Dichloroethane

DCE - Dichloroethene

MEK - Methyl Ethyl Ketone (2-butanone)

PCE - Tetrachloroethene

TCA - Trichloroethane

TCE - Trichloroethene

VC - Vinyl Chloride

b- Indicates analyte found in associated method blank

[a] Run #2

* Suspect result, believed to be erroneous

** Recovery well EW-11 not sampled due to pump/motor/piping failure

[1] It is believed that sample labels for EW-2 and EW-4 were inadvertently switched for samples collected on 7/23/10. Data have been corrected in this table.

[2] It is believed that sample labels for EW-2 and EW-4 were inadvertently switched for samples collected on 8/25/10. Data have been corrected in this table.

All constituent units are micrograms/liter (µg/L).

Only those compounds that were detected in at least one sample above the practical quantitation limit are shown.

Bold values for effluent sampling results indicate those above South Carolina Maximum Contaminant Levels (SC R.61-58.5). Suspect results are not bolded.

[p] (pH=3) Sample pH did not satisfy field preservation criteria

APPENDIX B

Surface Water and Groundwater Quality Data Reports – September 2021

The results set forth herein are provided by SGS North America Inc.

e-Hardcopy 2.0
Automated Report

Technical Report for

ARCADIS Geraghty & Miller

FPE; Edgefield, SC

30067293.2.2

SGS Job Number: FA88882

Sampling Date: 09/13/21

Report to:

ARCADIS Geraghty & Miller
1450 Greene St Suite 220
Augusta, GA 30901
jeff.beckner@arcadis-us.com

ATTN: Jeff Beckner

Total number of pages in report: 50

Test results contained within this data package meet the requirements of the National Environmental Laboratory Accreditation Program and/or state specific certification programs as applicable.

Norm Farmer
Technical Director

Client Service contact: Evita Martinez 407-425-6700

Certifications: FL(E83510), LA(03051), KS(E-10327), NC(573), NJ(FL002), NY(12022), SC(96038001) DoD ELAP(ANAB L2229), AZ(AZ0806), CA(2937), TX(T104704404), PA(68-03573), VA(460177), AL, AK, AR, CT, IA, KY, MA, MI. MS, ND, NH, NV, OK, OR, UT, VT, WA, WV

Test results relate only to samples analyzed.

September 29, 2021

Jeff Beckner
Arcadis Geraghty & Miller
1450 Greene St
Augusta, FL 30901

RE: SGS North America Inc. - Orlando job FA88882 Reissue

Dear Mr. Beckner,

The final report for job number FA88882 has been edited to reflect requested corrections. These edits have been incorporated into the revised report.

Matrix sample and Matrix sample Duplicate for FA88882-1 through FA88882-7 have been re-processed.

SGS North America Inc. - Orlando apologies for any inconvenience this may have caused. Please feel free to contact us if we can be of further assistance

Sincerely,

SGS North America Inc. - Orlando

Sections: 1 2 3 4 5

Table of Contents

SGS North America Inc.

Sample Summary

ARCADIS Geraghty & Miller

Job No: FA88882

FPE; Edgefield, SC
Project No: 30067293.2.2

Sample Number	Collected Date	Time	By	Received	Matrix Code	Type	Client Sample ID
This report contains results reported as ND = Not detected. The following applies:							
Organics ND	= Not detected above the MDL						
FA88882-1	09/13/21	12:15	RR	09/14/21	AQ	Ground Water	STAR RD
FA88882-2	09/13/21	12:30	RR	09/14/21	AQ	Ground Water	MIDPOINT
FA88882-3	09/13/21	12:40	RR	09/14/21	AQ	Ground Water	DDPD10
FA88882-4	09/13/21	12:45	RR	09/14/21	AQ	Ground Water	DDPC
FA88882-5	09/13/21	13:15	RR	09/14/21	AQ	Ground Water	STA-3
FA88882-6	09/13/21	13:20	RR	09/14/21	AQ	Ground Water	STA-5
FA88882-7	09/13/21	13:25	RR	09/14/21	AQ	Ground Water	STA-7
FA88882-8	09/13/21	13:30	RR	09/14/21	AQ	Ground Water	STA-8
FA88882-9	09/13/21	13:40	RR	09/14/21	AQ	Ground Water	STA-13
FA88882-10	09/13/21	00:00	RR	09/14/21	AQ	Ground Water	DUP-4
FA88882-11	09/13/21	00:00	RR	09/14/21	AQ	Trip Blank Water	TB

Summary of Hits

Job Number: FA88882
Account: ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC
Collected: 09/13/21

Lab Sample ID / Analyte	Client Sample ID	Result/ Qual	RL	MDL	Units	Method
FA88882-1	**STAR RD**					
No hits reported in this sample.						
FA88882-2	**MIDPOINT**					
No hits reported in this sample.						
FA88882-3	**DDPD10**					
No hits reported in this sample.						
FA88882-4	**DDPC**					
No hits reported in this sample.						
FA88882-5	**STA-3**					
No hits reported in this sample.						
FA88882-6	**STA-5**					
No hits reported in this sample.						
FA88882-7	**STA-7**					
No hits reported in this sample.						
FA88882-8	**STA-8**					
No hits reported in this sample.						
FA88882-9	**STA-13**					
No hits reported in this sample.						
FA88882-10	**DUP-4**					
No hits reported in this sample.						
FA88882-11	**TB**					
Toluene		0.75 J	1.0	0.30	ug/l	SW846 8260D

Sample Results

Report of Analysis

Report of Analysis

Client Sample ID:	STAR RD		
Lab Sample ID:	FA88882-1	**Date Sampled:**	09/13/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	1P81500.D	1	09/24/21 17:23	CV	n/a	n/a	V1P3302
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	STAR RD		
Lab Sample ID:	FA88882-1	**Date Sampled:**	09/13/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane [b]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride [b]	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	106%		83-118%
17060-07-0	1,2-Dichloroethane-D4	116%		79-125%
2037-26-5	Toluene-D8	95%		85-112%
460-00-4	4-Bromofluorobenzene	106%		83-118%

(a) Associated CCV and BS recovery outside control limits high, sample was ND.
(b) Associated CCV outside of control limits high, sample was ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MIDPOINT		
Lab Sample ID:	FA88882-2	**Date Sampled:**	09/13/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	1P81502.D	1	09/24/21 17:56	CV	n/a	n/a	V1P3302
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MIDPOINT		
Lab Sample ID:	FA88882-2	**Date Sampled:**	09/13/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane [b]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride [b]	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	95%		83-118%
17060-07-0	1,2-Dichloroethane-D4	94%		79-125%
2037-26-5	Toluene-D8	95%		85-112%
460-00-4	4-Bromofluorobenzene	103%		83-118%

(a) Associated CCV and BS recovery outside control limits high, sample was ND.
(b) Associated CCV outside of control limits high, sample was ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	DDPD10		
Lab Sample ID:	FA88882-3	**Date Sampled:**	09/13/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	1P81504.D	1	09/24/21 18:29	CV	n/a	n/a	V1P3302
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	DDPD10		
Lab Sample ID:	FA88882-3	**Date Sampled:**	09/13/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane [b]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride [b]	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	107%		83-118%
17060-07-0	1,2-Dichloroethane-D4	120%		79-125%
2037-26-5	Toluene-D8	93%		85-112%
460-00-4	4-Bromofluorobenzene	103%		83-118%

(a) Associated CCV and BS recovery outside control limits high, sample was ND.
(b) Associated CCV outside of control limits high, sample was ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	DDPC		
Lab Sample ID:	FA88882-4	**Date Sampled:**	09/13/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	1P81506.D	1	09/24/21 19:02	CV	n/a	n/a	V1P3302
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	DDPC		
Lab Sample ID:	FA88882-4	**Date Sampled:**	09/13/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane [b]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride [b]	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	108%		83-118%
17060-07-0	1,2-Dichloroethane-D4	122%		79-125%
2037-26-5	Toluene-D8	95%		85-112%
460-00-4	4-Bromofluorobenzene	102%		83-118%

(a) Associated CCV and BS recovery outside control limits high, sample was ND.
(b) Associated CCV outside of control limits high, sample was ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	STA-3		
Lab Sample ID:	FA88882-5	**Date Sampled:**	09/13/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	1P81508.D	1	09/24/21 19:34	CV	n/a	n/a	V1P3302
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	STA-3		
Lab Sample ID:	FA88882-5	**Date Sampled:**	09/13/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane [b]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride [b]	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	108%		83-118%
17060-07-0	1,2-Dichloroethane-D4	124%		79-125%
2037-26-5	Toluene-D8	95%		85-112%
460-00-4	4-Bromofluorobenzene	101%		83-118%

(a) Associated CCV and BS recovery outside control limits high, sample was ND.
(b) Associated CCV outside of control limits high, sample was ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	STA-5		
Lab Sample ID:	FA88882-6	**Date Sampled:**	09/13/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	1P81510.D	1	09/24/21 20:07	CV	n/a	n/a	V1P3302
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	STA-5		
Lab Sample ID:	FA88882-6	**Date Sampled:**	09/13/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane [b]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride [b]	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	111%		83-118%
17060-07-0	1,2-Dichloroethane-D4	128% [c]		79-125%
2037-26-5	Toluene-D8	95%		85-112%
460-00-4	4-Bromofluorobenzene	104%		83-118%

(a) Associated CCV and BS recovery outside control limits high, sample was ND.
(b) Associated CCV outside of control limits high, sample was ND.
(c) Outside control limits; however, sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	STA-7		
Lab Sample ID:	FA88882-7	**Date Sampled:**	09/13/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	1P81512.D	1	09/24/21 20:40	CV	n/a	n/a	V1P3302
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	STA-7		
Lab Sample ID:	FA88882-7	**Date Sampled:**	09/13/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane [b]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride [b]	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	109%		83-118%
17060-07-0	1,2-Dichloroethane-D4	124%		79-125%
2037-26-5	Toluene-D8	94%		85-112%
460-00-4	4-Bromofluorobenzene	104%		83-118%

(a) Associated CCV and BS recovery outside control limits high, sample was ND.
(b) Associated CCV outside of control limits high, sample was ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	STA-8		
Lab Sample ID:	FA88882-8	**Date Sampled:**	09/13/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	1A38035.D	1	09/27/21 13:37	CV	n/a	n/a	V1A1596
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane [a]	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	STA-8		
Lab Sample ID:	FA88882-8	**Date Sampled:**	09/13/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [b]	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	99%		83-118%
17060-07-0	1,2-Dichloroethane-D4	99%		79-125%
2037-26-5	Toluene-D8	95%		85-112%
460-00-4	4-Bromofluorobenzene	99%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.
(b) Associated CCV outside control limits low.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	STA-13		
Lab Sample ID:	FA88882-9	**Date Sampled:**	09/13/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	2P81483.D	1	09/24/21 12:42	CV	n/a	n/a	V2P3303
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	STA-13		
Lab Sample ID:	FA88882-9	**Date Sampled:**	09/13/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride [a]	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	104%		83-118%
17060-07-0	1,2-Dichloroethane-D4	108%		79-125%
2037-26-5	Toluene-D8	96%		85-112%
460-00-4	4-Bromofluorobenzene	102%		83-118%

(a) Associated CCV outside of control limits high, sample was ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	DUP-4		
Lab Sample ID:	FA88882-10	**Date Sampled:**	09/13/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	2P81485.D	1	09/24/21 13:15	CV	n/a	n/a	V2P3303
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	DUP-4		
Lab Sample ID:	FA88882-10	**Date Sampled:**	09/13/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride [a]	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	104%		83-118%
17060-07-0	1,2-Dichloroethane-D4	110%		79-125%
2037-26-5	Toluene-D8	94%		85-112%
460-00-4	4-Bromofluorobenzene	100%		83-118%

(a) Associated CCV outside of control limits high, sample was ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	TB		
Lab Sample ID:	FA88882-11	**Date Sampled:**	09/13/21
Matrix:	AQ - Trip Blank Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	2P81481.D	1	09/24/21 12:09	CV	n/a	n/a	V2P3303
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	TB		
Lab Sample ID:	FA88882-11	**Date Sampled:**	09/13/21
Matrix:	AQ - Trip Blank Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	0.75	1.0	0.30	ug/l	J
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride [a]	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	102%		83-118%
17060-07-0	1,2-Dichloroethane-D4	108%		79-125%
2037-26-5	Toluene-D8	96%		85-112%
460-00-4	4-Bromofluorobenzene	103%		83-118%

(a) Associated CCV outside of control limits high, sample was ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Misc. Forms

Custody Documents and Other Forms

Includes the following where applicable:

- Chain of Custody

ARCADIS | ID#: | **CHAIN OF CUSTODY & LABORATORY ANALYSIS REQUEST FORM** | Page ___ of ___ | Lab Work Order # FA88882

Send Results to:
Contact & Company Name: Jeff Beckner/ARCADIS | Telephone:
Address: 1450 Greene St. Ste220 | Fax:
City: Augusta | State: GA | Zip: 30901 | E-mail Address:
Project Name/Location (City, State): FPE / Edgefield, SC | Project #:
Sampler's Printed Name: Reggie Ricard | Sampler's Signature: Reggie Ricard

	Sample ID	Collection Date	Collection Time	Type (✓) Comp	Type (✓) Grab	Matrix	Preservative	Filtered (✓)	# of Containers	Container Information	1,4 Dioxane 8260 TCL 20	REMARKS
							B		3	1	PARAMETER ANALYSIS & METHOD	
1	Star Rd	9-13-21	1215		X	W					X	
2	Midpoint	9-13	1230		X	W					X	
3	DDPD10	9-13	1240		X	W					X	
4	DDPC	9-13	1245		X	W					X	
5	Stg-3	9-13	1315		X	W					X	
6	Stg-5	9-13	1320		X	W					X	
7	Stg-7	9-13	1325		X	W					X	
8	Stg-8	9-13	1330		X	W					X	
9	Stg-13	9-13	1340		X	W					X	
10	Dup-4	9-13	—		X	W					X	
11	TB										2	

Keys

Preservation Key:
A. H_2SO_4
B. HCL
C. HNO_3
D. NaOH
E. None
F. Other: _____
G. Other: _____
H. Other: _____

Container Information Key:
1. 40 ml Vial
2. 1 L Amber
3. 250 ml Plastic
4. 500 ml Plastic
5. Encore
6. 2 oz. Glass
7. 4 oz. Glass
8. 8 oz. Glass
9. Other: _____
10. Other: _____

Matrix Key:
SO - Soil | SE - Sediment | NL - NAPL/Oil
W - Water | SL - Sludge | SW - Sample Wipe
T - Tissue | A - Air | Other: _____

INITIAL ASSESSMENT DD

LABEL VERIFICATION

Special Instructions/Comments: 1,4 Dm

☐ Special QA/QC Instructions(✓):

Laboratory Information and Receipt		Relinquished By	Received By	Relinquished By	Laboratory Received By
Lab Name: SGS	Cooler Custody Seal (✓)	Printed Name: Reggie Ricard	Printed Name: FX	Printed Name: FX	Printed Name: Peter H
☒ Cooler packed with ice (✓)	☐ Intact ☐ Not Intact	Signature: Reggie Ricard	Signature:	Signature:	Signature: Peter H
Specify Turnaround Requirements:	Sample Receipt:	Firm: ARCADIS	Firm/Courier:	Firm/Courier:	Firm: SGS
Shipping Tracking #:	Condition/Cooler Temp: _____	Date/Time: 9-13-21 1600	Date/Time:	Date/Time:	Date/Time: 9/14/21 0906

20730826 CofC AR Form 08.27.2015 | **Distribution:** | WHITE – Laboratory returns with results | YELLOW – Lab copy | PINK – Retained by Arcadis

FA88882: Chain of Custody
Page 1 of 2

SGS Sample Receipt Summary

Job Number: FA88882 **Client:** ARCADIS **Project:** FPE/EDGEFIELD

Date / Time Received: 9/14/2021 10:00:00 AM **Delivery Method:** FX **Airbill #'s:** 5061 4510 5369

Therm ID: IR 1; **Therm CF:** 0.2; **# of Coolers:** 1

Cooler Temps (Raw Measured) °C: Cooler 1: (1.2);

Cooler Temps (Corrected) °C: Cooler 1: (1.4);

Cooler Information	Y	or	N
1. Custody Seals Present	☑		☐
2. Custody Seals Intact	☑		☐
3. Temp criteria achieved	☑		☐
4. Cooler temp verification	IR Gun		
5. Cooler media	Ice (Bag)		

Trip Blank Information	Y	or	N	N/A
1. Trip Blank present / cooler	☑		☐	☐
2. Trip Blank listed on COC	☑		☐	☐

	W	or	S	N/A
3. Type Of TB Received	☑		☐	☐

Sample Information	Y	or	N	N/A
1. Sample labels present on bottles	☑		☐	
2. Samples preserved properly	☑		☐	
3. Sufficient volume/containers recvd for analysis:	☑		☐	
4. Condition of sample	Intact			
5. Sample recvd within HT	☑		☐	
6. Dates/Times/IDs on COC match Sample Label	☑		☐	
7. VOCs have headspace	☐		☑	☐
8. Bottles received for unspecified tests	☐		☑	
9. Compositing instructions clear	☐		☐	☑
10. Voa Soil Kits/Jars received past 48hrs?	☐		☐	☑
11. % Solids Jar received?	☐		☐	☑
12. Residual Chlorine Present?	☐		☐	☑

Misc. Information

Number of Encores: 25-Gram _____ 5-Gram _____ Number of 5035 Field Kits: _____ Number of Lab Filtered Metals: _____

Test Strip Lot #s: pH 0-3 230315 pH 10-12 219813A Other: (Specify) _____ _____

Residual Chlorine Test Strip Lot #: _____

Comments

SM001
Rev. Date 05/24/17

Technician: PETERH Date: 9/14/2021 10:00:00 A Reviewer: _____ Date: _____

FA88882: Chain of Custody
Page 2 of 2

MS Volatiles

QC Data Summaries

Includes the following where applicable:

- Method Blank Summaries
- Blank Spike Summaries
- Matrix Spike and Duplicate Summaries

Method Blank Summary

Job Number: FA88882
Account: ARCGMSCA ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC

Sample	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
V1P3302-MB	1P81478.D	1	09/24/21	CV	n/a	n/a	V1P3302

The QC reported here applies to the following samples: **Method:** SW846 8260D

FA88882-1, FA88882-2, FA88882-3, FA88882-4, FA88882-5, FA88882-6, FA88882-7

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	

Method Blank Summary

Job Number: FA88882
Account: ARCGMSCA ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC

Sample	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
V1P3302-MB	1P81478.D	1	09/24/21	CV	n/a	n/a	V1P3302

The QC reported here applies to the following samples: **Method:** SW846 8260D

FA88882-1, FA88882-2, FA88882-3, FA88882-4, FA88882-5, FA88882-6, FA88882-7

CAS No.	Compound	Result	RL	MDL	Units	Q
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries		Limits
1868-53-7	Dibromofluoromethane	104%	83-118%
17060-07-0	1,2-Dichloroethane-D4	108%	79-125%
2037-26-5	Toluene-D8	96%	85-112%
460-00-4	4-Bromofluorobenzene	101%	83-118%

Method Blank Summary

Job Number: FA88882
Account: ARCGMSCA ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC

Sample	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
V2P3303-MB	2P81479.D	1	09/24/21	CV	n/a	n/a	V2P3303

The QC reported here applies to the following samples: **Method:** SW846 8260D

FA88882-9, FA88882-10, FA88882-11

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	

Method Blank Summary

Job Number: FA88882
Account: ARCGMSCA ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC

Sample	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
V2P3303-MB	2P81479.D	1	09/24/21	CV	n/a	n/a	V2P3303

The QC reported here applies to the following samples: **Method:** SW846 8260D

FA88882-9, FA88882-10, FA88882-11

CAS No.	Compound	Result	RL	MDL	Units	Q
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries		Limits
1868-53-7	Dibromofluoromethane	104%	83-118%
17060-07-0	1,2-Dichloroethane-D4	109%	79-125%
2037-26-5	Toluene-D8	96%	85-112%
460-00-4	4-Bromofluorobenzene	101%	83-118%

Method Blank Summary

Job Number: FA88882
Account: ARCGMSCA ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC

Sample	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
V1A1596-MB	1A38029.D	1	09/27/21	CV	n/a	n/a	V1A1596

The QC reported here applies to the following samples: **Method:** SW846 8260D

FA88882-8

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	

Method Blank Summary

Job Number: FA88882
Account: ARCGMSCA ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC

Sample	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
V1A1596-MB	1A38029.D	1	09/27/21	CV	n/a	n/a	V1A1596

The QC reported here applies to the following samples: **Method:** SW846 8260D

FA88882-8

CAS No.	Compound	Result	RL	MDL	Units	Q
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries		Limits
1868-53-7	Dibromofluoromethane	99%	83-118%
17060-07-0	1,2-Dichloroethane-D4	98%	79-125%
2037-26-5	Toluene-D8	97%	85-112%
460-00-4	4-Bromofluorobenzene	98%	83-118%

Blank Spike Summary

Job Number: FA88882
Account: ARCGMSCA ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC

Sample	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
V1P3302-BS	1P81474.D	1	09/24/21	CV	n/a	n/a	V1P3302

The QC reported here applies to the following samples: **Method:** SW846 8260D

FA88882-1, FA88882-2, FA88882-3, FA88882-4, FA88882-5, FA88882-6, FA88882-7

CAS No.	Compound	Spike ug/l	BSP ug/l	BSP %	Limits
67-64-1	Acetone	125	106	85	50-147
71-43-2	Benzene	25	27.1	108	81-122
74-97-5	Bromochloromethane	25	21.3	85	76-123
75-27-4	Bromodichloromethane	25	28.5	114	79-123
75-25-2	Bromoform	25	26.2	105	66-123
78-93-3	2-Butanone (MEK)	125	120	96	56-143
75-15-0	Carbon Disulfide	25	23.7	95	66-148
56-23-5	Carbon Tetrachloride	25	32.3	129	76-136
108-90-7	Chlorobenzene	25	25.6	102	82-124
75-00-3	Chloroethane	25	30.3	121	62-144
67-66-3	Chloroform	25	27.6	110	80-124
110-82-7	Cyclohexane	25	25.6	102	73-138
124-48-1	Dibromochloromethane	25	25.8	103	78-122
96-12-8	1,2-Dibromo-3-chloropropane	25	24.5	98	64-123
106-93-4	1,2-Dibromoethane	25	24.5	98	75-120
75-71-8	Dichlorodifluoromethane	25	22.4	90	42-167
95-50-1	1,2-Dichlorobenzene	25	25.2	101	82-124
541-73-1	1,3-Dichlorobenzene	25	25.1	100	84-125
106-46-7	1,4-Dichlorobenzene	25	24.9	100	78-120
75-34-3	1,1-Dichloroethane	25	27.9	112	81-122
107-06-2	1,2-Dichloroethane	25	27.1	108	75-125
75-35-4	1,1-Dichloroethylene	25	28.7	115	78-137
156-59-2	cis-1,2-Dichloroethylene	25	26.7	107	78-120
156-60-5	trans-1,2-Dichloroethylene	25	27.8	111	76-127
78-87-5	1,2-Dichloropropane	25	25.1	100	76-124
10061-01-5	cis-1,3-Dichloropropene	25	27.1	108	75-118
10061-02-6	trans-1,3-Dichloropropene	25	27.6	110	80-120
100-41-4	Ethylbenzene	25	26.4	106	81-121
76-13-1	Freon 113	25	27.6	110	72-134
591-78-6	2-Hexanone	125	121	97	61-129
98-82-8	Isopropylbenzene	25	27.6	110	83-132
79-20-9	Methyl Acetate	125	121	97	65-126
74-83-9	Methyl Bromide	25	36.8	147*	59-143
74-87-3	Methyl Chloride	25	24.1	96	50-159
108-87-2	Methylcyclohexane	25	27.4	110	76-129
75-09-2	Methylene Chloride	25	22.6	90	69-135

* = Outside of Control Limits.

Blank Spike Summary

Job Number: FA88882
Account: ARCGMSCA ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC

Sample	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
V1P3302-BS	1P81474.D	1	09/24/21	CV	n/a	n/a	V1P3302

The QC reported here applies to the following samples: **Method:** SW846 8260D

FA88882-1, FA88882-2, FA88882-3, FA88882-4, FA88882-5, FA88882-6, FA88882-7

CAS No.	Compound	Spike ug/l	BSP ug/l	BSP %	Limits
108-10-1	4-Methyl-2-pentanone (MIBK)	125	124	99	66-122
1634-04-4	Methyl Tert Butyl Ether	25	24.7	99	72-117
100-42-5	Styrene	25	25.5	102	78-119
79-34-5	1,1,2,2-Tetrachloroethane	25	22.2	89	72-120
127-18-4	Tetrachloroethylene	25	25.7	103	76-135
108-88-3	Toluene	25	25.1	100	80-120
87-61-6	1,2,3-Trichlorobenzene	25	24.7	99	68-131
120-82-1	1,2,4-Trichlorobenzene	25	25.6	102	73-129
71-55-6	1,1,1-Trichloroethane	25	30.2	121	75-130
79-00-5	1,1,2-Trichloroethane	25	23.4	94	76-119
79-01-6	Trichloroethylene	25	27.2	109	81-126
75-69-4	Trichlorofluoromethane	25	37.4	150	71-156
75-01-4	Vinyl Chloride	25	34.4	138	69-159
	m,p-Xylene	50	53.3	107	79-126
95-47-6	o-Xylene	25	26.7	107	80-127

CAS No.	Surrogate Recoveries	BSP	Limits
1868-53-7	Dibromofluoromethane	104%	83-118%
17060-07-0	1,2-Dichloroethane-D4	108%	79-125%
2037-26-5	Toluene-D8	97%	85-112%
460-00-4	4-Bromofluorobenzene	102%	83-118%

* = Outside of Control Limits.

Blank Spike Summary

Job Number: FA88882
Account: ARCGMSCA ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC

Sample	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
V2P3303-BS	2P81475.D	1	09/24/21	CV	n/a	n/a	V2P3303

The QC reported here applies to the following samples: **Method:** SW846 8260D

FA88882-9, FA88882-10, FA88882-11

CAS No.	Compound	Spike ug/l	BSP ug/l	BSP %	Limits
67-64-1	Acetone	125	104	83	50-147
71-43-2	Benzene	25	26.2	105	81-122
74-97-5	Bromochloromethane	25	24.2	97	76-123
75-27-4	Bromodichloromethane	25	27.7	111	79-123
75-25-2	Bromoform	25	26.5	106	66-123
78-93-3	2-Butanone (MEK)	125	115	92	56-143
75-15-0	Carbon Disulfide	25	24.8	99	66-148
56-23-5	Carbon Tetrachloride	25	30.5	122	76-136
108-90-7	Chlorobenzene	25	25.1	100	82-124
75-00-3	Chloroethane	25	28.5	114	62-144
67-66-3	Chloroform	25	26.5	106	80-124
110-82-7	Cyclohexane	25	24.8	99	73-138
124-48-1	Dibromochloromethane	25	25.2	101	78-122
96-12-8	1,2-Dibromo-3-chloropropane	25	24.2	97	64-123
106-93-4	1,2-Dibromoethane	25	23.1	92	75-120
75-71-8	Dichlorodifluoromethane	25	23.7	95	42-167
95-50-1	1,2-Dichlorobenzene	25	24.9	100	82-124
541-73-1	1,3-Dichlorobenzene	25	25.0	100	84-125
106-46-7	1,4-Dichlorobenzene	25	24.8	99	78-120
75-34-3	1,1-Dichloroethane	25	27.6	110	81-122
107-06-2	1,2-Dichloroethane	25	26.7	107	75-125
75-35-4	1,1-Dichloroethylene	25	27.8	111	78-137
156-59-2	cis-1,2-Dichloroethylene	25	25.8	103	78-120
156-60-5	trans-1,2-Dichloroethylene	25	26.3	105	76-127
78-87-5	1,2-Dichloropropane	25	24.4	98	76-124
10061-01-5	cis-1,3-Dichloropropene	25	25.8	103	75-118
10061-02-6	trans-1,3-Dichloropropene	25	26.2	105	80-120
100-41-4	Ethylbenzene	25	25.5	102	81-121
76-13-1	Freon 113	25	26.3	105	72-134
591-78-6	2-Hexanone	125	115	92	61-129
98-82-8	Isopropylbenzene	25	27.5	110	83-132
79-20-9	Methyl Acetate	125	115	92	65-126
74-83-9	Methyl Bromide	25	33.2	133	59-143
74-87-3	Methyl Chloride	25	29.3	117	50-159
108-87-2	Methylcyclohexane	25	27.3	109	76-129
75-09-2	Methylene Chloride	25	20.4	82	69-135

* = Outside of Control Limits.

Blank Spike Summary

Job Number: FA88882
Account: ARCGMSCA ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC

Sample	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
V2P3303-BS	2P81475.D	1	09/24/21	CV	n/a	n/a	V2P3303

The QC reported here applies to the following samples: **Method:** SW846 8260D

FA88882-9, FA88882-10, FA88882-11

CAS No.	Compound	Spike ug/l	BSP ug/l	BSP %	Limits
108-10-1	4-Methyl-2-pentanone (MIBK)	125	121	97	66-122
1634-04-4	Methyl Tert Butyl Ether	25	24.2	97	72-117
100-42-5	Styrene	25	25.3	101	78-119
79-34-5	1,1,2,2-Tetrachloroethane	25	22.0	88	72-120
127-18-4	Tetrachloroethylene	25	25.0	100	76-135
108-88-3	Toluene	25	24.7	99	80-120
87-61-6	1,2,3-Trichlorobenzene	25	24.7	99	68-131
120-82-1	1,2,4-Trichlorobenzene	25	24.6	98	73-129
71-55-6	1,1,1-Trichloroethane	25	29.1	116	75-130
79-00-5	1,1,2-Trichloroethane	25	23.8	95	76-119
79-01-6	Trichloroethylene	25	26.1	104	81-126
75-69-4	Trichlorofluoromethane	25	36.4	146	71-156
75-01-4	Vinyl Chloride	25	36.6	146	69-159
	m,p-Xylene	50	51.9	104	79-126
95-47-6	o-Xylene	25	25.9	104	80-127

CAS No.	Surrogate Recoveries	BSP	Limits
1868-53-7	Dibromofluoromethane	104%	83-118%
17060-07-0	1,2-Dichloroethane-D4	105%	79-125%
2037-26-5	Toluene-D8	98%	85-112%
460-00-4	4-Bromofluorobenzene	100%	83-118%

* = Outside of Control Limits.

Blank Spike Summary

Job Number: FA88882
Account: ARCGMSCA ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC

Sample	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
V1A1596-BS	1A38025.D	1	09/27/21	CV	n/a	n/a	V1A1596

The QC reported here applies to the following samples: **Method:** SW846 8260D

FA88882-8

CAS No.	Compound	Spike ug/l	BSP ug/l	BSP %	Limits
67-64-1	Acetone	125	103	82	50-147
71-43-2	Benzene	25	27.4	110	81-122
74-97-5	Bromochloromethane	25	26.3	105	76-123
75-27-4	Bromodichloromethane	25	25.8	103	79-123
75-25-2	Bromoform	25	23.7	95	66-123
78-93-3	2-Butanone (MEK)	125	115	92	56-143
75-15-0	Carbon Disulfide	25	23.4	94	66-148
56-23-5	Carbon Tetrachloride	25	26.8	107	76-136
108-90-7	Chlorobenzene	25	25.5	102	82-124
75-00-3	Chloroethane	25	26.5	106	62-144
67-66-3	Chloroform	25	26.4	106	80-124
110-82-7	Cyclohexane	25	26.4	106	73-138
124-48-1	Dibromochloromethane	25	23.9	96	78-122
96-12-8	1,2-Dibromo-3-chloropropane	25	21.6	86	64-123
106-93-4	1,2-Dibromoethane	25	24.2	97	75-120
75-71-8	Dichlorodifluoromethane	25	20.0	80	42-167
95-50-1	1,2-Dichlorobenzene	25	25.0	100	82-124
541-73-1	1,3-Dichlorobenzene	25	26.0	104	84-125
106-46-7	1,4-Dichlorobenzene	25	24.8	99	78-120
75-34-3	1,1-Dichloroethane	25	28.2	113	81-122
107-06-2	1,2-Dichloroethane	25	24.9	100	75-125
75-35-4	1,1-Dichloroethylene	25	27.8	111	78-137
156-59-2	cis-1,2-Dichloroethylene	25	27.1	108	78-120
156-60-5	trans-1,2-Dichloroethylene	25	27.0	108	76-127
78-87-5	1,2-Dichloropropane	25	26.4	106	76-124
10061-01-5	cis-1,3-Dichloropropene	25	26.0	104	75-118
10061-02-6	trans-1,3-Dichloropropene	25	25.4	102	80-120
100-41-4	Ethylbenzene	25	25.5	102	81-121
76-13-1	Freon 113	25	26.6	106	72-134
591-78-6	2-Hexanone	125	116	93	61-129
98-82-8	Isopropylbenzene	25	26.7	107	83-132
79-20-9	Methyl Acetate	125	124	99	65-126
74-83-9	Methyl Bromide	25	19.2	77	59-143
74-87-3	Methyl Chloride	25	20.8	83	50-159
108-87-2	Methylcyclohexane	25	27.5	110	76-129
75-09-2	Methylene Chloride	25	23.7	95	69-135

* = Outside of Control Limits.

Blank Spike Summary

Job Number: FA88882
Account: ARCGMSCA ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC

Sample	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
V1A1596-BS	1A38025.D	1	09/27/21	CV	n/a	n/a	V1A1596

The QC reported here applies to the following samples: **Method:** SW846 8260D

FA88882-8

CAS No.	Compound	Spike ug/l	BSP ug/l	BSP %	Limits
108-10-1	4-Methyl-2-pentanone (MIBK)	125	121	97	66-122
1634-04-4	Methyl Tert Butyl Ether	25	24.0	96	72-117
100-42-5	Styrene	25	25.7	103	78-119
79-34-5	1,1,2,2-Tetrachloroethane	25	24.2	97	72-120
127-18-4	Tetrachloroethylene	25	24.9	100	76-135
108-88-3	Toluene	25	25.0	100	80-120
87-61-6	1,2,3-Trichlorobenzene	25	24.0	96	68-131
120-82-1	1,2,4-Trichlorobenzene	25	24.2	97	73-129
71-55-6	1,1,1-Trichloroethane	25	26.9	108	75-130
79-00-5	1,1,2-Trichloroethane	25	24.5	98	76-119
79-01-6	Trichloroethylene	25	27.0	108	81-126
75-69-4	Trichlorofluoromethane	25	27.7	111	71-156
75-01-4	Vinyl Chloride	25	25.0	100	69-159
	m,p-Xylene	50	50.7	101	79-126
95-47-6	o-Xylene	25	25.8	103	80-127

CAS No.	Surrogate Recoveries	BSP	Limits
1868-53-7	Dibromofluoromethane	102%	83-118%
17060-07-0	1,2-Dichloroethane-D4	95%	79-125%
2037-26-5	Toluene-D8	97%	85-112%
460-00-4	4-Bromofluorobenzene	104%	83-118%

* = Outside of Control Limits.

Matrix Spike/Matrix Spike Duplicate Summary

Job Number: FA88882
Account: ARCGMSCA ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC

Sample	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
FA89134-1MS	2P81517.D	5	09/24/21	CV	n/a	n/a	V2P3303
FA89134-1MSD	2P81519.D	5	09/24/21	CV	n/a	n/a	V2P3303
FA89134-1	2P81487.D	1	09/24/21	CV	n/a	n/a	V2P3303

The QC reported here applies to the following samples: **Method:** SW846 8260D

FA88882-9, FA88882-10, FA88882-11

CAS No.	Compound	FA89134-1 ug/l	Q	Spike ug/l	MS ug/l	MS %	Spike ug/l	MSD ug/l	MSD %	RPD	Limits Rec/RPD
67-64-1	Acetone	ND		625	836	134	625	534	85	44*	50-147/21
71-43-2	Benzene	ND		125	134	107	125	131	105	2	81-122/14
74-97-5	Bromochloromethane	ND		125	125	100	125	127	102	2	76-123/14
75-27-4	Bromodichloromethane	ND		125	147	118	125	143	114	3	79-123/19
75-25-2	Bromoform	ND		125	136	109	125	129	103	5	66-123/21
78-93-3	2-Butanone (MEK)	ND		625	589	94	625	587	94	0	56-143/18
75-15-0	Carbon Disulfide	ND		125	202	162*	125	122	98	49*	66-148/23
56-23-5	Carbon Tetrachloride	ND		125	175	140*	125	173	138*	1	76-136/23
108-90-7	Chlorobenzene	ND		125	123	98	125	124	99	1	82-124/14
75-00-3	Chloroethane	ND		125	180	144	125	187	150*	4	62-144/20
67-66-3	Chloroform	ND		125	145	116	125	144	115	1	80-124/15
110-82-7	Cyclohexane	ND		125	125	100	125	127	102	2	73-138/18
124-48-1	Dibromochloromethane	ND		125	126	101	125	128	102	2	78-122/19
96-12-8	1,2-Dibromo-3-chloropropane	ND		125	126	101	125	130	104	3	64-123/18
106-93-4	1,2-Dibromoethane	ND		125	116	93	125	114	91	2	75-120/13
75-71-8	Dichlorodifluoromethane	ND		125	171	137	125	154	123	10	42-167/19
95-50-1	1,2-Dichlorobenzene	ND		125	124	99	125	127	102	2	82-124/14
541-73-1	1,3-Dichlorobenzene	ND		125	127	102	125	128	102	1	84-125/14
106-46-7	1,4-Dichlorobenzene	ND		125	122	98	125	125	100	2	78-120/15
75-34-3	1,1-Dichloroethane	0.52	J	125	141	112	125	143	114	1	81-122/15
107-06-2	1,2-Dichloroethane	ND		125	151	121	125	146	117	3	75-125/14
75-35-4	1,1-Dichloroethylene	ND		125	222	178*	125	152	122	37*	78-137/18
156-59-2	cis-1,2-Dichloroethylene	ND		125	125	100	125	126	101	1	78-120/15
156-60-5	trans-1,2-Dichloroethylene	ND		125	176	141*	125	136	109	26*	76-127/17
78-87-5	1,2-Dichloropropane	ND		125	116	93	125	119	95	3	76-124/14
10061-01-5	cis-1,3-Dichloropropene	ND		125	125	100	125	127	102	2	75-118/23
10061-02-6	trans-1,3-Dichloropropene	ND		125	128	102	125	128	102	0	80-120/22
100-41-4	Ethylbenzene	ND		125	133	106	125	126	101	5	81-121/14
76-13-1	Freon 113	ND		125	219	175*	125	140	112	44*	72-134/20
591-78-6	2-Hexanone	ND		625	628	100	625	642	103	2	61-129/18
98-82-8	Isopropylbenzene	ND		125	139	111	125	134	107	4	83-132/15
79-20-9	Methyl Acetate	ND		625	827	132*	625	569	91	37*	65-126/18
74-83-9	Methyl Bromide	ND		125	200	160*	125	186	149*	7	59-143/19
74-87-3	Methyl Chloride	ND		125	199	159	125	185	148	7	50-159/19
108-87-2	Methylcyclohexane	ND		125	128	102	125	133	106	4	76-129/17
75-09-2	Methylene Chloride	ND		125	199	159*	125	119	95	50*	69-135/16

* = Outside of Control Limits.

Matrix Spike/Matrix Spike Duplicate Summary

Job Number: FA88882
Account: ARCGMSCA ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC

Sample	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
FA89134-1MS	2P81517.D	5	09/24/21	CV	n/a	n/a	V2P3303
FA89134-1MSD	2P81519.D	5	09/24/21	CV	n/a	n/a	V2P3303
FA89134-1	2P81487.D	1	09/24/21	CV	n/a	n/a	V2P3303

The QC reported here applies to the following samples: **Method:** SW846 8260D

FA88882-9, FA88882-10, FA88882-11

CAS No.	Compound	FA89134-1 ug/l	Q	Spike ug/l	MS ug/l	MS %	Spike ug/l	MSD ug/l	MSD %	RPD	Limits Rec/RPD
108-10-1	4-Methyl-2-pentanone (MIBK)	ND		625	599	96	625	604	97	1	66-122/16
1634-04-4	Methyl Tert Butyl Ether	ND		125	138	110	125	125	100	10	72-117/14
100-42-5	Styrene	ND		125	138	110	125	123	98	11	78-119/23
79-34-5	1,1,2,2-Tetrachloroethane	ND		125	112	90	125	108	86	4	72-120/14
127-18-4	Tetrachloroethylene	ND		125	120	96	125	121	97	1	76-135/16
108-88-3	Toluene	ND		125	118	94	125	119	95	1	80-120/14
87-61-6	1,2,3-Trichlorobenzene	ND		125	123	98	125	123	98	0	68-131/25
120-82-1	1,2,4-Trichlorobenzene	ND		125	119	95	125	121	97	2	73-129/20
71-55-6	1,1,1-Trichloroethane	ND		125	168	134*	125	159	127	6	75-130/16
79-00-5	1,1,2-Trichloroethane	ND		125	108	86	125	112	90	4	76-119/14
79-01-6	Trichloroethylene	ND		125	137	110	125	136	109	1	81-126/15
75-69-4	Trichlorofluoromethane	ND		125	282	226*	125	256	205*	10	71-156/21
75-01-4	Vinyl Chloride	ND		125	233	186*	125	216	173*	8	69-159/18
	m,p-Xylene	ND		250	264	106	250	274	110	4	79-126/15
95-47-6	o-Xylene	ND		125	143	114	125	129	103	10	80-127/14

CAS No.	Surrogate Recoveries	MS	MSD	FA89134-1	Limits
1868-53-7	Dibromofluoromethane	110%	111%	103%	83-118%
17060-07-0	1,2-Dichloroethane-D4	120%	116%	106%	79-125%
2037-26-5	Toluene-D8	98%	96%	97%	85-112%
460-00-4	4-Bromofluorobenzene	102%	104%	103%	83-118%

* = Outside of Control Limits.

Matrix Spike/Matrix Spike Duplicate Summary

Job Number: FA88882
Account: ARCGMSCA ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC

Sample	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
FA88958-3MS	1A38067.D	1	09/27/21	CV	n/a	n/a	V1A1596
FA88958-3MSD	1A38069.D	1	09/27/21	CV	n/a	n/a	V1A1596
FA88958-3	1A38043.D	1	09/27/21	CV	n/a	n/a	V1A1596

The QC reported here applies to the following samples: **Method:** SW846 8260D

FA88882-8

CAS No.	Compound	FA88958-3 ug/l	Q	Spike ug/l	MS ug/l	MS %	Spike ug/l	MSD ug/l	MSD %	RPD	Limits Rec/RPD
67-64-1	Acetone	25	U	125	89.1	71	125	88.1	70	1	50-147/21
71-43-2	Benzene	1.0	U	25	27.4	110	25	27.5	110	0	81-122/14
74-97-5	Bromochloromethane	1.0	U	25	26.2	105	25	26.5	106	1	76-123/14
75-27-4	Bromodichloromethane	1.0	U	25	25.4	102	25	25.8	103	2	79-123/19
75-25-2	Bromoform	1.0	U	25	21.5	86	25	21.5	86	0	66-123/21
78-93-3	2-Butanone (MEK)	5.0	U	125	112	90	125	112	90	0	56-143/18
75-15-0	Carbon Disulfide	2.0	U	25	21.8	87	25	22.2	89	2	66-148/23
56-23-5	Carbon Tetrachloride	1.0	U	25	25.9	104	25	25.6	102	1	76-136/23
108-90-7	Chlorobenzene	1.0	U	25	25.0	100	25	24.5	98	2	82-124/14
75-00-3	Chloroethane	2.0	U	25	28.0	112	25	35.1	140	23*	62-144/20
67-66-3	Chloroform	1.0	U	25	26.4	106	25	26.3	105	0	80-124/15
110-82-7	Cyclohexane	1.0	U	25	25.5	102	25	25.6	102	0	73-138/18
124-48-1	Dibromochloromethane	1.0	U	25	22.5	90	25	22.2	89	1	78-122/19
96-12-8	1,2-Dibromo-3-chloropropane	5.0	U	25	20.5	82	25	19.7	79	4	64-123/18
106-93-4	1,2-Dibromoethane	2.0	U	25	23.7	95	25	23.6	94	0	75-120/13
75-71-8	Dichlorodifluoromethane	2.0	U	25	19.9	80	25	19.5	78	2	42-167/19
95-50-1	1,2-Dichlorobenzene	1.0	U	25	24.3	97	25	23.8	95	2	82-124/14
541-73-1	1,3-Dichlorobenzene	1.0	U	25	24.9	100	25	24.5	98	2	84-125/14
106-46-7	1,4-Dichlorobenzene	1.0	U	25	24.2	97	25	23.6	94	3	78-120/15
75-34-3	1,1-Dichloroethane	1.0	U	25	28.2	113	25	28.2	113	0	81-122/15
107-06-2	1,2-Dichloroethane	1.0	U	25	24.5	98	25	24.9	100	2	75-125/14
75-35-4	1,1-Dichloroethylene	1.0	U	25	26.7	107	25	27.2	109	2	78-137/18
156-59-2	cis-1,2-Dichloroethylene	1.0	U	25	27.4	110	25	27.4	110	0	78-120/15
156-60-5	trans-1,2-Dichloroethylene	1.0	U	25	26.6	106	25	26.6	106	0	76-127/17
78-87-5	1,2-Dichloropropane	1.0	U	25	26.7	107	25	27.1	108	1	76-124/14
10061-01-5	cis-1,3-Dichloropropene	1.0	U	25	23.8	95	25	24.1	96	1	75-118/23
10061-02-6	trans-1,3-Dichloropropene	1.0	U	25	23.4	94	25	23.7	95	1	80-120/22
100-41-4	Ethylbenzene	1.0	U	25	24.9	100	25	24.4	98	2	81-121/14
76-13-1	Freon 113	1.0	U	25	25.6	102	25	26.4	106	3	72-134/20
591-78-6	2-Hexanone	10	U	125	114	91	125	108	86	5	61-129/18
98-82-8	Isopropylbenzene	1.0	U	25	25.6	102	25	24.9	100	3	83-132/15
79-20-9	Methyl Acetate	20	U	125	115	92	125	115	92	0	65-126/18
74-83-9	Methyl Bromide	5.0	U	25	17.6	70	25	18.8	75	7	59-143/19
74-87-3	Methyl Chloride	2.0	U	25	20.6	82	25	20.4	82	1	50-159/19
108-87-2	Methylcyclohexane	1.0	U	25	26.4	106	25	27.0	108	2	76-129/17
75-09-2	Methylene Chloride	5.0	U	25	22.6	90	25	23.2	93	3	69-135/16

* = Outside of Control Limits.

Matrix Spike/Matrix Spike Duplicate Summary

Job Number: FA88882
Account: ARCGMSCA ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC

Sample	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
FA88958-3MS	1A38067.D	1	09/27/21	CV	n/a	n/a	V1A1596
FA88958-3MSD	1A38069.D	1	09/27/21	CV	n/a	n/a	V1A1596
FA88958-3	1A38043.D	1	09/27/21	CV	n/a	n/a	V1A1596

The QC reported here applies to the following samples: **Method:** SW846 8260D

FA88882-8

CAS No.	Compound	FA88958-3 ug/l	Q	Spike ug/l	MS ug/l	MS %	Spike ug/l	MSD ug/l	MSD %	RPD	Limits Rec/RPD
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0	U	125	120	96	125	117	94	3	66-122/16
1634-04-4	Methyl Tert Butyl Ether	1.0	U	25	23.2	93	25	23.8	95	3	72-117/14
100-42-5	Styrene	1.0	U	25	24.7	99	25	24.2	97	2	78-119/23
79-34-5	1,1,2,2-Tetrachloroethane	1.0	U	25	24.2	97	25	23.8	95	2	72-120/14
127-18-4	Tetrachloroethylene	1.0	U	25	22.9	92	25	22.5	90	2	76-135/16
108-88-3	Toluene	1.0	U	25	24.5	98	25	24.0	96	2	80-120/14
87-61-6	1,2,3-Trichlorobenzene	2.0	U	25	22.9	92	25	23.0	92	0	68-131/25
120-82-1	1,2,4-Trichlorobenzene	2.0	U	25	22.6	90	25	22.4	90	1	73-129/20
71-55-6	1,1,1-Trichloroethane	1.0	U	25	26.6	106	25	26.5	106	0	75-130/16
79-00-5	1,1,2-Trichloroethane	1.0	U	25	24.1	96	25	24.4	98	1	76-119/14
79-01-6	Trichloroethylene	1.0	U	25	26.1	104	25	26.1	104	0	81-126/15
75-69-4	Trichlorofluoromethane	2.0	U	25	27.2	109	25	27.1	108	0	71-156/21
75-01-4	Vinyl Chloride	1.0	U	25	24.4	98	25	24.0	96	2	69-159/18
	m,p-Xylene	2.0	U	50	48.9	98	50	48.2	96	1	79-126/15
95-47-6	o-Xylene	1.0	U	25	24.9	100	25	24.4	98	2	80-127/14

CAS No.	Surrogate Recoveries	MS	MSD	FA88958-3	Limits
1868-53-7	Dibromofluoromethane	100%	103%	99%	83-118%
17060-07-0	1,2-Dichloroethane-D4	93%	99%	99%	79-125%
2037-26-5	Toluene-D8	95%	94%	95%	85-112%
460-00-4	4-Bromofluorobenzene	102%	104%	101%	83-118%

* = Outside of Control Limits.

Matrix Spike/Matrix Spike Duplicate Summary

Job Number: FA88882
Account: ARCGMSCA ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC

Sample	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
FA88882-1MS	1P81594.D	5	09/28/21	CV	n/a	n/a	V1P3302
FA88882-1MSD	1P81596.D	5	09/28/21	CV	n/a	n/a	V1P3302
FA88882-1	1P81500.D	1	09/24/21	CV	n/a	n/a	V1P3302

The QC reported here applies to the following samples: **Method:** SW846 8260D

FA88882-1, FA88882-2, FA88882-3, FA88882-4, FA88882-5, FA88882-6, FA88882-7

CAS No.	Compound	FA88882-1 ug/l	Q	Spike ug/l	MS ug/l	MS %	Spike ug/l	MSD ug/l	MSD %	RPD	Limits Rec/RPD
67-64-1	Acetone	ND		625	634	101	625	645	103	2	50-147/21
71-43-2	Benzene	ND		125	122	98	125	123	98	1	81-122/14
74-97-5	Bromochloromethane	ND		125	116	93	125	121	97	4	76-123/14
75-27-4	Bromodichloromethane	ND		125	137	110	125	138	110	1	79-123/19
75-25-2	Bromoform	ND		125	122	98	125	123	98	1	66-123/21
78-93-3	2-Butanone (MEK)	ND		625	590	94	625	607	97	3	56-143/18
75-15-0	Carbon Disulfide	ND		125	92.1	74	125	94.7	76	3	66-148/23
56-23-5	Carbon Tetrachloride	ND		125	145	116	125	146	117	1	76-136/23
108-90-7	Chlorobenzene	ND		125	121	97	125	123	98	2	82-124/14
75-00-3	Chloroethane	ND		125	140	112	125	130	104	7	62-144/20
67-66-3	Chloroform	ND		125	134	107	125	132	106	2	80-124/15
110-82-7	Cyclohexane	ND		125	116	93	125	117	94	1	73-138/18
124-48-1	Dibromochloromethane	ND		125	125	100	125	127	102	2	78-122/19
96-12-8	1,2-Dibromo-3-chloropropane	ND		125	119	95	125	119	95	0	64-123/18
106-93-4	1,2-Dibromoethane	ND		125	124	99	125	125	100	1	75-120/13
75-71-8	Dichlorodifluoromethane	ND		125	151	121	125	142	114	6	42-167/19
95-50-1	1,2-Dichlorobenzene	ND		125	123	98	125	118	94	4	82-124/14
541-73-1	1,3-Dichlorobenzene	ND		125	120	96	125	121	97	1	84-125/14
106-46-7	1,4-Dichlorobenzene	ND		125	121	97	125	121	97	0	78-120/15
75-34-3	1,1-Dichloroethane	ND		125	134	107	125	133	106	1	81-122/15
107-06-2	1,2-Dichloroethane	ND		125	137	110	125	137	110	0	75-125/14
75-35-4	1,1-Dichloroethylene	ND		125	121	97	125	118	94	3	78-137/18
156-59-2	cis-1,2-Dichloroethylene	ND		125	128	102	125	128	102	0	78-120/15
156-60-5	trans-1,2-Dichloroethylene	ND		125	132	106	125	131	105	1	76-127/17
78-87-5	1,2-Dichloropropane	ND		125	123	98	125	124	99	1	76-124/14
10061-01-5	cis-1,3-Dichloropropene	ND		125	123	98	125	123	98	0	75-118/23
10061-02-6	trans-1,3-Dichloropropene	ND		125	130	104	125	129	103	1	80-120/22
100-41-4	Ethylbenzene	ND		125	123	98	125	120	96	2	81-121/14
76-13-1	Freon 113	ND		125	119	95	125	117	94	2	72-134/20
591-78-6	2-Hexanone	ND		625	571	91	625	618	99	8	61-129/18
98-82-8	Isopropylbenzene	ND		125	131	105	125	132	106	1	83-132/15
79-20-9	Methyl Acetate	ND		625	571	91	625	587	94	3	65-126/18
74-83-9	Methyl Bromide	ND		125	143	114	125	131	105	9	59-143/19
74-87-3	Methyl Chloride	ND		125	143	114	125	141	113	1	50-159/19
108-87-2	Methylcyclohexane	ND		125	121	97	125	120	96	1	76-129/17
75-09-2	Methylene Chloride	ND		125	136	109	125	138	110	1	69-135/16

* = Outside of Control Limits.

Matrix Spike/Matrix Spike Duplicate Summary

Job Number: FA88882
Account: ARCGMSCA ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC

Sample	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
FA88882-1MS	1P81594.D	5	09/28/21	CV	n/a	n/a	V1P3302
FA88882-1MSD	1P81596.D	5	09/28/21	CV	n/a	n/a	V1P3302
FA88882-1	1P81500.D	1	09/24/21	CV	n/a	n/a	V1P3302

The QC reported here applies to the following samples: **Method:** SW846 8260D

FA88882-1, FA88882-2, FA88882-3, FA88882-4, FA88882-5, FA88882-6, FA88882-7

CAS No.	Compound	FA88882-1 ug/l	Q	Spike ug/l	MS ug/l	MS %	Spike ug/l	MSD ug/l	MSD %	RPD	Limits Rec/RPD
108-10-1	4-Methyl-2-pentanone (MIBK)	ND		625	609	97	625	604	97	1	66-122/16
1634-04-4	Methyl Tert Butyl Ether	ND		125	118	94	125	117	94	1	72-117/14
100-42-5	Styrene	ND		125	127	102	125	127	102	0	78-119/23
79-34-5	1,1,2,2-Tetrachloroethane	ND		125	116	93	125	114	91	2	72-120/14
127-18-4	Tetrachloroethylene	ND		125	119	95	125	118	94	1	76-135/16
108-88-3	Toluene	ND		125	119	95	125	120	96	1	80-120/14
87-61-6	1,2,3-Trichlorobenzene	ND		125	113	90	125	110	88	3	68-131/25
120-82-1	1,2,4-Trichlorobenzene	ND		125	116	93	125	114	91	2	73-129/20
71-55-6	1,1,1-Trichloroethane	ND		125	135	108	125	138	110	2	75-130/16
79-00-5	1,1,2-Trichloroethane	ND		125	123	98	125	122	98	1	76-119/14
79-01-6	Trichloroethylene	ND		125	122	98	125	125	100	2	81-126/15
75-69-4	Trichlorofluoromethane	ND		125	158	126	125	154	123	3	71-156/21
75-01-4	Vinyl Chloride	ND		125	149	119	125	145	116	3	69-159/18
	m,p-Xylene	ND		250	247	99	250	247	99	0	79-126/15
95-47-6	o-Xylene	ND		125	129	103	125	130	104	1	80-127/14

CAS No.	Surrogate Recoveries	MS	MSD	FA88882-1	Limits
1868-53-7	Dibromofluoromethane	106%	108%	106%	83-118%
17060-07-0	1,2-Dichloroethane-D4	114%	112%	116%	79-125%
2037-26-5	Toluene-D8	100%	101%	95%	85-112%
460-00-4	4-Bromofluorobenzene	100%	99%	106%	83-118%

* = Outside of Control Limits.

The results set forth herein are provided by SGS North America Inc.

e-Hardcopy 2.0
Automated Report

Technical Report for

ARCADIS Geraghty & Miller

FPE; Edgefield, SC

30067293.2.2

SGS Job Number: FA88901

Sampling Dates: 09/07/21 - 09/10/21

Report to:

ARCADIS Geraghty & Miller

jbeckner@arcadis-us.com

ATTN: Jeff Beckner

Total number of pages in report: **68**

Test results contained within this data package meet the requirements of the National Environmental Laboratory Accreditation Program and/or state specific certification programs as applicable.

Norm Farmer
Technical Director

Client Service contact: Evita Martinez 407-425-6700

Certifications: FL(E83510), LA(03051), KS(E-10327), NC(573), NJ(FL002), NY(12022), SC(96038001) DoD ELAP(ANAB L2229), AZ(AZ0806), CA(2937), TX(T104704404), PA(68-03573), VA(460177), AL, AK, AR, CT, IA, KY, MA, MI. MS, ND, NH, NV, OK, OR, UT, VT, WA, WV

Sections: 1 2 3 4

Table of Contents

Sample Summary

ARCADIS Geraghty & Miller

Job No: FA88901

FPE; Edgefield, SC
Project No: 30067293.2.2

Sample Number	Collected Date	Time	By	Received	Matrix Code	Type	Client Sample ID
FA88901-1	09/07/21	09:39	JO	09/14/21	AQ	Ground Water	SMMW-1
FA88901-2	09/07/21	10:43	JO	09/14/21	AQ	Ground Water	RNMW-2
FA88901-3	09/07/21	12:30	JO	09/14/21	AQ	Ground Water	RNMW-1
FA88901-4	09/07/21	13:24	JO	09/14/21	AQ	Ground Water	SMMW-13
FA88901-5	09/07/21	14:21	JO	09/14/21	AQ	Ground Water	SMMW-11
FA88901-6	09/07/21	14:54	JO	09/14/21	AQ	Ground Water	SMMW-10
FA88901-7	09/08/21	08:22	JO	09/14/21	AQ	Ground Water	SMMW-3
FA88901-8	09/08/21	09:00	JO	09/14/21	AQ	Ground Water	SMMW-9
FA88901-9	09/08/21	09:58	JO	09/14/21	AQ	Ground Water	SMMW-7
FA88901-10	09/08/21	10:49	JO	09/14/21	AQ	Ground Water	SMMW-12
FA88901-11	09/08/21	11:59	JO	09/14/21	AQ	Ground Water	SMMW-2
FA88901-12	09/08/21	12:50	JO	09/14/21	AQ	Ground Water	SFMW-1A

This report contains results reported as ND = Not detected. The following applies:
Organics ND = Not detected above the MDL

Sample Summary
(continued)

ARCADIS Geraghty & Miller

Job No: FA88901

FPE; Edgefield, SC
Project No: 30067293.2.2

Sample Number	Collected Date	Time	By	Received	Matrix Code	Type	Client Sample ID
FA88901-13	09/08/21	13:45	JO	09/14/21	AQ	Ground Water	SMMW-5
FA88901-14	09/09/21	08:50	JO	09/14/21	AQ	Ground Water	SMMW-4
FA88901-15	09/09/21	00:00	JO	09/14/21	AQ	Ground Water	DUP-2
FA88901-16	09/09/21	09:48	JO	09/14/21	AQ	Ground Water	SMMW-6
FA88901-17	09/09/21	10:36	JO	09/14/21	AQ	Ground Water	SMMW-8
FA88901-18	09/09/21	12:30	JO	09/14/21	AQ	Ground Water	B2SF
FA88901-19	09/09/21	13:20	JO	09/14/21	AQ	Ground Water	B1SF
FA88901-20	09/09/21	14:10	JO	09/14/21	AQ	Ground Water	B4SF
FA88901-21	09/10/21	08:20	JO	09/14/21	AQ	Ground Water	B3SF
FA88901-22	09/10/21	09:05	JO	09/14/21	AQ	Ground Water	B5SF
FA88901-23	09/10/21	10:46	JO	09/14/21	AQ	Ground Water	TMW-1
FA88901-24	09/10/21	12:03	JO	09/14/21	AQ	Ground Water	TMW-2
FA88901-25	09/10/21	12:57	JO	09/14/21	AQ	Ground Water	RTB-3

Sample Summary
(continued)

ARCADIS Geraghty & Miller

Job No: FA88901

FPE; Edgefield, SC
Project No: 30067293.2.2

Sample Number	Collected Date	Time	By	Received	Matrix Code	Type	Client Sample ID
FA88901-26	09/10/21	13:33	JO	09/14/21	AQ	Ground Water	RTB-4
FA88901-27	09/07/21	00:00	JO	09/14/21	AQ	Trip Blank Water	TB

Summary of Hits

Job Number: FA88901
Account: ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC
Collected: 09/07/21 thru 09/10/21

Lab Sample ID / Analyte	Client Sample ID	Result/ Qual	RL	MDL	Units	Method
FA88901-1	**SMMW-1**					
Chloroform		1.1	1.0	0.30	ug/l	SW846 8260D
Trichloroethylene		0.94 J	1.0	0.35	ug/l	SW846 8260D
FA88901-2	**RNMW-2**					
Trichloroethylene		2.2	1.0	0.35	ug/l	SW846 8260D
FA88901-3	**RNMW-1**					
Trichloroethylene		2.0	1.0	0.35	ug/l	SW846 8260D
FA88901-4	**SMMW-13**					
1,1-Dichloroethane		0.55 J	1.0	0.34	ug/l	SW846 8260D
cis-1,2-Dichloroethylene		26.6	1.0	0.28	ug/l	SW846 8260D
Trichloroethylene		1.3	1.0	0.35	ug/l	SW846 8260D
FA88901-5	**SMMW-11**					
cis-1,2-Dichloroethylene		20.0	1.0	0.28	ug/l	SW846 8260D
Trichloroethylene		7.3	1.0	0.35	ug/l	SW846 8260D
FA88901-6	**SMMW-10**					
Chloroform		0.47 J	1.0	0.30	ug/l	SW846 8260D
cis-1,2-Dichloroethylene		4.0	1.0	0.28	ug/l	SW846 8260D
Trichloroethylene		1.2	1.0	0.35	ug/l	SW846 8260D
FA88901-7	**SMMW-3**					
1,1-Dichloroethylene		2.0 J	5.0	1.6	ug/l	SW846 8260D
cis-1,2-Dichloroethylene		53.5	5.0	1.4	ug/l	SW846 8260D
Trichloroethylene		276	5.0	1.7	ug/l	SW846 8260D
FA88901-8	**SMMW-9**					
cis-1,2-Dichloroethylene		2060	200	55	ug/l	SW846 8260D
Methylene Chloride		456 J	1000	400	ug/l	SW846 8260D
Trichloroethylene		13800	200	69	ug/l	SW846 8260D
FA88901-9	**SMMW-7**					
cis-1,2-Dichloroethylene		2180	200	55	ug/l	SW846 8260D

Summary of Hits

Job Number: FA88901
Account: ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC
Collected: 09/07/21 thru 09/10/21

Lab Sample ID / Analyte	Client Sample ID	Result/ Qual	RL	MDL	Units	Method
Trichloroethylene		10100	200	69	ug/l	SW846 8260D
FA88901-10	**SMMW-12**					
cis-1,2-Dichloroethylene		216	25	6.9	ug/l	SW846 8260D
Trichloroethylene		2240	25	8.6	ug/l	SW846 8260D
FA88901-11	**SMMW-2**					
cis-1,2-Dichloroethylene		28.2	10	2.8	ug/l	SW846 8260D
Trichloroethylene		629	10	3.5	ug/l	SW846 8260D
FA88901-12	**SFMW-1A**					
cis-1,2-Dichloroethylene		20.3	10	2.8	ug/l	SW846 8260D
Trichloroethylene		474	10	3.5	ug/l	SW846 8260D
FA88901-13	**SMMW-5**					
cis-1,2-Dichloroethylene		60.9	2.5	0.69	ug/l	SW846 8260D
Trichloroethylene		187	2.5	0.86	ug/l	SW846 8260D
FA88901-14	**SMMW-4**					
cis-1,2-Dichloroethylene		442	50	14	ug/l	SW846 8260D
Trichloroethylene		3700	50	17	ug/l	SW846 8260D
FA88901-15	**DUP-2**					
cis-1,2-Dichloroethylene		488	50	14	ug/l	SW846 8260D
Trichloroethylene		3940	50	17	ug/l	SW846 8260D
FA88901-16	**SMMW-6**					
cis-1,2-Dichloroethylene		69.0	25	6.9	ug/l	SW846 8260D
Methylene Chloride		61.9 J	130	50	ug/l	SW846 8260D
Trichloroethylene		1470	25	8.6	ug/l	SW846 8260D
FA88901-17	**SMMW-8**					
Chloroform		5.6	2.0	0.60	ug/l	SW846 8260D
cis-1,2-Dichloroethylene		9.3	2.0	0.55	ug/l	SW846 8260D
Methylene Chloride		4.8 J	10	4.0	ug/l	SW846 8260D
Tetrachloroethylene		0.44 J	2.0	0.43	ug/l	SW846 8260D
Trichloroethylene		122	2.0	0.69	ug/l	SW846 8260D

Summary of Hits

Job Number: FA88901
Account: ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC
Collected: 09/07/21 thru 09/10/21

Lab Sample ID / Analyte	Client Sample ID	Result/ Qual	RL	MDL	Units	Method
FA88901-18	**B2SF**					
Chloroform		8.7	2.5	0.75	ug/l	SW846 8260D
1,1-Dichloroethylene		1.9 J	2.5	0.81	ug/l	SW846 8260D
cis-1,2-Dichloroethylene		21.2	2.5	0.69	ug/l	SW846 8260D
Methylene Chloride		22.4	13	5.0	ug/l	SW846 8260D
Tetrachloroethylene		0.80 J	2.5	0.54	ug/l	SW846 8260D
Trichloroethylene		192	2.5	0.86	ug/l	SW846 8260D
FA88901-19	**B1SF**					
cis-1,2-Dichloroethylene		773	100	28	ug/l	SW846 8260D
Methylene Chloride		209 J	500	200	ug/l	SW846 8260D
Trichloroethylene		5710	100	35	ug/l	SW846 8260D
FA88901-20	**B4SF**					
cis-1,2-Dichloroethylene		93.6	20	5.5	ug/l	SW846 8260D
Trichloroethylene		1580	20	6.9	ug/l	SW846 8260D
FA88901-21	**B3SF**					
cis-1,2-Dichloroethylene		126	10	2.8	ug/l	SW846 8260D
Trichloroethylene		871	10	3.5	ug/l	SW846 8260D
FA88901-22	**B5SF**					
2-Butanone (MEK)		96.8	50	20	ug/l	SW846 8260D
cis-1,2-Dichloroethylene		66.9	10	2.8	ug/l	SW846 8260D
Trichloroethylene		838	10	3.5	ug/l	SW846 8260D
FA88901-23	**TMW-1**					
Bromodichloromethane		0.26 J	1.0	0.24	ug/l	SW846 8260D
Chloroform		0.57 J	1.0	0.30	ug/l	SW846 8260D
FA88901-24	**TMW-2**					
Chloroform		0.61 J	1.0	0.30	ug/l	SW846 8260D
FA88901-25	**RTB-3**					
cis-1,2-Dichloroethylene		469	25	6.9	ug/l	SW846 8260D
Trichloroethylene		2030	25	8.6	ug/l	SW846 8260D

Summary of Hits

Job Number: FA88901
Account: ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC
Collected: 09/07/21 thru 09/10/21

Lab Sample ID / Analyte	Client Sample ID	Result/ Qual	RL	MDL	Units	Method
FA88901-26	**RTB-4**					
cis-1,2-Dichloroethylene		10.6	1.0	0.28	ug/l	SW846 8260D
Tetrachloroethylene		0.43 J	1.0	0.22	ug/l	SW846 8260D
Trichloroethylene		88.5	2.0	0.69	ug/l	SW846 8260D
FA88901-27	**TB**					
Toluene		0.36 J	1.0	0.30	ug/l	SW846 8260D

Sample Results

Report of Analysis

Report of Analysis

Client Sample ID:	SMMW-1		
Lab Sample ID:	FA88901-1	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	2A37777.D	1	09/20/21 13:48	CV	n/a	n/a	V2A1591
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane [a]	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	1.1	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-1		
Lab Sample ID:	FA88901-1	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	0.94	1.0	0.35	ug/l	J
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	100%		83-118%
17060-07-0	1,2-Dichloroethane-D4	101%		79-125%
2037-26-5	Toluene-D8	100%		85-112%
460-00-4	4-Bromofluorobenzene	100%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	RNMW-2		
Lab Sample ID:	FA88901-2	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	2A37779.D	1	09/20/21 14:18	CV	n/a	n/a	V2A1591
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane [a]	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	RNMW-2		
Lab Sample ID:	FA88901-2	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	2.2	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	98%		83-118%
17060-07-0	1,2-Dichloroethane-D4	99%		79-125%
2037-26-5	Toluene-D8	101%		85-112%
460-00-4	4-Bromofluorobenzene	98%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	RNMW-1		
Lab Sample ID:	FA88901-3	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	2A37781.D	1	09/20/21 14:47	CV	n/a	n/a	V2A1591
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane [a]	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	RNMW-1		
Lab Sample ID:	FA88901-3	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	2.0	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	100%		83-118%
17060-07-0	1,2-Dichloroethane-D4	97%		79-125%
2037-26-5	Toluene-D8	101%		85-112%
460-00-4	4-Bromofluorobenzene	99%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-13		
Lab Sample ID:	FA88901-4	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	2A37783.D	1	09/20/21 15:17	CV	n/a	n/a	V2A1591
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane [a]	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	0.55	1.0	0.34	ug/l	J
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	26.6	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-13		
Lab Sample ID:	FA88901-4	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	1.3	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	100%		83-118%
17060-07-0	1,2-Dichloroethane-D4	100%		79-125%
2037-26-5	Toluene-D8	99%		85-112%
460-00-4	4-Bromofluorobenzene	99%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-11		
Lab Sample ID:	FA88901-5	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	2A37785.D	1	09/20/21 15:47	CV	n/a	n/a	V2A1591
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane [a]	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	20.0	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-11		
Lab Sample ID:	FA88901-5	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	7.3	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	99%		83-118%
17060-07-0	1,2-Dichloroethane-D4	98%		79-125%
2037-26-5	Toluene-D8	101%		85-112%
460-00-4	4-Bromofluorobenzene	98%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-10		
Lab Sample ID:	FA88901-6	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	2A37787.D	1	09/20/21 16:17	CV	n/a	n/a	V2A1591
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane [a]	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	0.47	1.0	0.30	ug/l	J
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	4.0	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-10		
Lab Sample ID:	FA88901-6	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	1.2	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	100%		83-118%
17060-07-0	1,2-Dichloroethane-D4	101%		79-125%
2037-26-5	Toluene-D8	100%		85-112%
460-00-4	4-Bromofluorobenzene	99%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-3		
Lab Sample ID:	FA88901-7	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I70989.D	5	09/21/21 20:28	SO	n/a	n/a	VI2313
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	130	50	ug/l	
71-43-2	Benzene	ND	5.0	1.6	ug/l	
74-97-5	Bromochloromethane	ND	5.0	2.3	ug/l	
75-27-4	Bromodichloromethane	ND	5.0	1.2	ug/l	
75-25-2	Bromoform	ND	5.0	2.0	ug/l	
78-93-3	2-Butanone (MEK)	ND	25	10	ug/l	
75-15-0	Carbon Disulfide [a]	ND	10	2.7	ug/l	
56-23-5	Carbon Tetrachloride	ND	5.0	1.8	ug/l	
108-90-7	Chlorobenzene	ND	5.0	1.0	ug/l	
75-00-3	Chloroethane	ND	10	3.3	ug/l	
67-66-3	Chloroform	ND	5.0	1.5	ug/l	
110-82-7	Cyclohexane	ND	5.0	2.0	ug/l	
124-48-1	Dibromochloromethane	ND	5.0	1.4	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	25	5.2	ug/l	
106-93-4	1,2-Dibromoethane	ND	10	1.4	ug/l	
75-71-8	Dichlorodifluoromethane	ND	10	2.5	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	5.0	1.6	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	5.0	1.1	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	5.0	1.3	ug/l	
75-34-3	1,1-Dichloroethane	ND	5.0	1.7	ug/l	
107-06-2	1,2-Dichloroethane	ND	5.0	1.6	ug/l	
75-35-4	1,1-Dichloroethylene	2.0	5.0	1.6	ug/l	J
156-59-2	cis-1,2-Dichloroethylene	53.5	5.0	1.4	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	5.0	1.1	ug/l	
78-87-5	1,2-Dichloropropane	ND	5.0	2.1	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	5.0	1.5	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	5.0	1.1	ug/l	
100-41-4	Ethylbenzene	ND	5.0	1.8	ug/l	
76-13-1	Freon 113	ND	5.0	2.4	ug/l	
591-78-6	2-Hexanone	ND	50	10	ug/l	
98-82-8	Isopropylbenzene	ND	5.0	1.1	ug/l	
79-20-9	Methyl Acetate	ND	100	25	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-3		
Lab Sample ID:	FA88901-7	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	25	10	ug/l	
74-87-3	Methyl Chloride	ND	10	2.5	ug/l	
108-87-2	Methylcyclohexane	ND	5.0	2.2	ug/l	
75-09-2	Methylene Chloride	ND	25	10	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	25	5.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	5.0	1.1	ug/l	
100-42-5	Styrene	ND	5.0	1.1	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	5.0	1.5	ug/l	
127-18-4	Tetrachloroethylene [b]	ND	5.0	1.1	ug/l	
108-88-3	Toluene	ND	5.0	1.5	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	10	3.1	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	10	2.5	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	5.0	1.2	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	5.0	2.3	ug/l	
79-01-6	Trichloroethylene	276	5.0	1.7	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	10	2.5	ug/l	
75-01-4	Vinyl Chloride	ND	5.0	2.0	ug/l	
	m,p-Xylene	ND	10	2.3	ug/l	
95-47-6	o-Xylene	ND	5.0	1.3	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	92%		83-118%
17060-07-0	1,2-Dichloroethane-D4	97%		79-125%
2037-26-5	Toluene-D8	92%		85-112%
460-00-4	4-Bromofluorobenzene	93%		83-118%

(a) Associated CCV outside of control limits low.
(b) Associated CCV outside of control limits high, sample was ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-9		
Lab Sample ID:	FA88901-8	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I70990.D	200	09/21/21 20:52	SO	n/a	n/a	VI2313
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	5000	2000	ug/l	
71-43-2	Benzene	ND	200	62	ug/l	
74-97-5	Bromochloromethane	ND	200	90	ug/l	
75-27-4	Bromodichloromethane	ND	200	48	ug/l	
75-25-2	Bromoform	ND	200	81	ug/l	
78-93-3	2-Butanone (MEK)	ND	1000	400	ug/l	
75-15-0	Carbon Disulfide [a]	ND	400	110	ug/l	
56-23-5	Carbon Tetrachloride	ND	200	71	ug/l	
108-90-7	Chlorobenzene	ND	200	40	ug/l	
75-00-3	Chloroethane	ND	400	130	ug/l	
67-66-3	Chloroform	ND	200	60	ug/l	
110-82-7	Cyclohexane	ND	200	78	ug/l	
124-48-1	Dibromochloromethane	ND	200	55	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	1000	210	ug/l	
106-93-4	1,2-Dibromoethane	ND	400	55	ug/l	
75-71-8	Dichlorodifluoromethane	ND	400	100	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	200	65	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	200	43	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	200	51	ug/l	
75-34-3	1,1-Dichloroethane	ND	200	68	ug/l	
107-06-2	1,2-Dichloroethane	ND	200	62	ug/l	
75-35-4	1,1-Dichloroethylene	ND	200	64	ug/l	
156-59-2	cis-1,2-Dichloroethylene	2060	200	55	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	200	44	ug/l	
78-87-5	1,2-Dichloropropane	ND	200	85	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	200	58	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	200	43	ug/l	
100-41-4	Ethylbenzene	ND	200	71	ug/l	
76-13-1	Freon 113	ND	200	96	ug/l	
591-78-6	2-Hexanone	ND	2000	400	ug/l	
98-82-8	Isopropylbenzene	ND	200	44	ug/l	
79-20-9	Methyl Acetate	ND	4000	1000	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-9		
Lab Sample ID:	FA88901-8	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	1000	400	ug/l	
74-87-3	Methyl Chloride	ND	400	100	ug/l	
108-87-2	Methylcyclohexane	ND	200	87	ug/l	
75-09-2	Methylene Chloride	456	1000	400	ug/l	J
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	1000	200	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	200	46	ug/l	
100-42-5	Styrene	ND	200	44	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	200	60	ug/l	
127-18-4	Tetrachloroethylene [b]	ND	200	43	ug/l	
108-88-3	Toluene	ND	200	60	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	400	120	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	400	100	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	200	50	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	200	93	ug/l	
79-01-6	Trichloroethylene	13800	200	69	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	400	100	ug/l	
75-01-4	Vinyl Chloride	ND	200	82	ug/l	
	m,p-Xylene	ND	400	93	ug/l	
95-47-6	o-Xylene	ND	200	51	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	91%		83-118%
17060-07-0	1,2-Dichloroethane-D4	96%		79-125%
2037-26-5	Toluene-D8	91%		85-112%
460-00-4	4-Bromofluorobenzene	94%		83-118%

(a) Associated CCV outside of control limits low.
(b) Associated CCV outside of control limits high, sample was ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-7		
Lab Sample ID:	FA88901-9	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I70991.D	200	09/21/21 21:16	SO	n/a	n/a	VI2313
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	5000	2000	ug/l	
71-43-2	Benzene	ND	200	62	ug/l	
74-97-5	Bromochloromethane	ND	200	90	ug/l	
75-27-4	Bromodichloromethane	ND	200	48	ug/l	
75-25-2	Bromoform	ND	200	81	ug/l	
78-93-3	2-Butanone (MEK)	ND	1000	400	ug/l	
75-15-0	Carbon Disulfide [a]	ND	400	110	ug/l	
56-23-5	Carbon Tetrachloride	ND	200	71	ug/l	
108-90-7	Chlorobenzene	ND	200	40	ug/l	
75-00-3	Chloroethane	ND	400	130	ug/l	
67-66-3	Chloroform	ND	200	60	ug/l	
110-82-7	Cyclohexane	ND	200	78	ug/l	
124-48-1	Dibromochloromethane	ND	200	55	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	1000	210	ug/l	
106-93-4	1,2-Dibromoethane	ND	400	55	ug/l	
75-71-8	Dichlorodifluoromethane	ND	400	100	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	200	65	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	200	43	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	200	51	ug/l	
75-34-3	1,1-Dichloroethane	ND	200	68	ug/l	
107-06-2	1,2-Dichloroethane	ND	200	62	ug/l	
75-35-4	1,1-Dichloroethylene	ND	200	64	ug/l	
156-59-2	cis-1,2-Dichloroethylene	2180	200	55	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	200	44	ug/l	
78-87-5	1,2-Dichloropropane	ND	200	85	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	200	58	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	200	43	ug/l	
100-41-4	Ethylbenzene	ND	200	71	ug/l	
76-13-1	Freon 113	ND	200	96	ug/l	
591-78-6	2-Hexanone	ND	2000	400	ug/l	
98-82-8	Isopropylbenzene	ND	200	44	ug/l	
79-20-9	Methyl Acetate	ND	4000	1000	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-7		
Lab Sample ID:	FA88901-9	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	1000	400	ug/l	
74-87-3	Methyl Chloride	ND	400	100	ug/l	
108-87-2	Methylcyclohexane	ND	200	87	ug/l	
75-09-2	Methylene Chloride	ND	1000	400	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	1000	200	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	200	46	ug/l	
100-42-5	Styrene	ND	200	44	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	200	60	ug/l	
127-18-4	Tetrachloroethylene [b]	ND	200	43	ug/l	
108-88-3	Toluene	ND	200	60	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	400	120	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	400	100	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	200	50	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	200	93	ug/l	
79-01-6	Trichloroethylene	10100	200	69	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	400	100	ug/l	
75-01-4	Vinyl Chloride	ND	200	82	ug/l	
	m,p-Xylene	ND	400	93	ug/l	
95-47-6	o-Xylene	ND	200	51	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	92%		83-118%
17060-07-0	1,2-Dichloroethane-D4	98%		79-125%
2037-26-5	Toluene-D8	92%		85-112%
460-00-4	4-Bromofluorobenzene	94%		83-118%

(a) Associated CCV outside of control limits low.
(b) Associated CCV outside of control limits high, sample was ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-12		
Lab Sample ID:	FA88901-10	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I70992.D	25	09/21/21 21:40	SO	n/a	n/a	VI2313
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	630	250	ug/l	
71-43-2	Benzene	ND	25	7.8	ug/l	
74-97-5	Bromochloromethane	ND	25	11	ug/l	
75-27-4	Bromodichloromethane	ND	25	6.1	ug/l	
75-25-2	Bromoform	ND	25	10	ug/l	
78-93-3	2-Butanone (MEK)	ND	130	50	ug/l	
75-15-0	Carbon Disulfide [a]	ND	50	13	ug/l	
56-23-5	Carbon Tetrachloride	ND	25	8.9	ug/l	
108-90-7	Chlorobenzene	ND	25	5.0	ug/l	
75-00-3	Chloroethane	ND	50	17	ug/l	
67-66-3	Chloroform	ND	25	7.5	ug/l	
110-82-7	Cyclohexane	ND	25	9.8	ug/l	
124-48-1	Dibromochloromethane	ND	25	6.9	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	130	26	ug/l	
106-93-4	1,2-Dibromoethane	ND	50	6.9	ug/l	
75-71-8	Dichlorodifluoromethane	ND	50	13	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	25	8.1	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	25	5.4	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	25	6.4	ug/l	
75-34-3	1,1-Dichloroethane	ND	25	8.5	ug/l	
107-06-2	1,2-Dichloroethane	ND	25	7.8	ug/l	
75-35-4	1,1-Dichloroethylene	ND	25	8.1	ug/l	
156-59-2	cis-1,2-Dichloroethylene	216	25	6.9	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	25	5.5	ug/l	
78-87-5	1,2-Dichloropropane	ND	25	11	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	25	7.3	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	25	5.4	ug/l	
100-41-4	Ethylbenzene	ND	25	8.9	ug/l	
76-13-1	Freon 113	ND	25	12	ug/l	
591-78-6	2-Hexanone	ND	250	50	ug/l	
98-82-8	Isopropylbenzene	ND	25	5.5	ug/l	
79-20-9	Methyl Acetate	ND	500	130	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-12		
Lab Sample ID:	FA88901-10	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	130	50	ug/l	
74-87-3	Methyl Chloride	ND	50	13	ug/l	
108-87-2	Methylcyclohexane	ND	25	11	ug/l	
75-09-2	Methylene Chloride	ND	130	50	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	130	25	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	25	5.7	ug/l	
100-42-5	Styrene	ND	25	5.6	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	25	7.5	ug/l	
127-18-4	Tetrachloroethylene [b]	ND	25	5.4	ug/l	
108-88-3	Toluene	ND	25	7.5	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	50	15	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	50	13	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	25	6.2	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	25	12	ug/l	
79-01-6	Trichloroethylene	2240	25	8.6	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	50	13	ug/l	
75-01-4	Vinyl Chloride	ND	25	10	ug/l	
	m,p-Xylene	ND	50	12	ug/l	
95-47-6	o-Xylene	ND	25	6.4	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	92%		83-118%
17060-07-0	1,2-Dichloroethane-D4	97%		79-125%
2037-26-5	Toluene-D8	93%		85-112%
460-00-4	4-Bromofluorobenzene	93%		83-118%

(a) Associated CCV outside of control limits low.
(b) Associated CCV outside of control limits high, sample was ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-2		
Lab Sample ID:	FA88901-11	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I70993.D	10	09/21/21 22:04	SO	n/a	n/a	VI2313
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	250	100	ug/l	
71-43-2	Benzene	ND	10	3.1	ug/l	
74-97-5	Bromochloromethane	ND	10	4.5	ug/l	
75-27-4	Bromodichloromethane	ND	10	2.4	ug/l	
75-25-2	Bromoform	ND	10	4.1	ug/l	
78-93-3	2-Butanone (MEK)	ND	50	20	ug/l	
75-15-0	Carbon Disulfide [a]	ND	20	5.3	ug/l	
56-23-5	Carbon Tetrachloride	ND	10	3.6	ug/l	
108-90-7	Chlorobenzene	ND	10	2.0	ug/l	
75-00-3	Chloroethane	ND	20	6.7	ug/l	
67-66-3	Chloroform	ND	10	3.0	ug/l	
110-82-7	Cyclohexane	ND	10	3.9	ug/l	
124-48-1	Dibromochloromethane	ND	10	2.8	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	50	10	ug/l	
106-93-4	1,2-Dibromoethane	ND	20	2.8	ug/l	
75-71-8	Dichlorodifluoromethane	ND	20	5.0	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	10	3.2	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	10	2.2	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	10	2.6	ug/l	
75-34-3	1,1-Dichloroethane	ND	10	3.4	ug/l	
107-06-2	1,2-Dichloroethane	ND	10	3.1	ug/l	
75-35-4	1,1-Dichloroethylene	ND	10	3.2	ug/l	
156-59-2	cis-1,2-Dichloroethylene	28.2	10	2.8	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	10	2.2	ug/l	
78-87-5	1,2-Dichloropropane	ND	10	4.3	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	10	2.9	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	10	2.1	ug/l	
100-41-4	Ethylbenzene	ND	10	3.6	ug/l	
76-13-1	Freon 113	ND	10	4.8	ug/l	
591-78-6	2-Hexanone	ND	100	20	ug/l	
98-82-8	Isopropylbenzene	ND	10	2.2	ug/l	
79-20-9	Methyl Acetate	ND	200	50	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-2		
Lab Sample ID:	FA88901-11	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	50	20	ug/l	
74-87-3	Methyl Chloride	ND	20	5.0	ug/l	
108-87-2	Methylcyclohexane	ND	10	4.4	ug/l	
75-09-2	Methylene Chloride	ND	50	20	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	50	10	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	10	2.3	ug/l	
100-42-5	Styrene	ND	10	2.2	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	10	3.0	ug/l	
127-18-4	Tetrachloroethylene [b]	ND	10	2.2	ug/l	
108-88-3	Toluene	ND	10	3.0	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	20	6.1	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	20	5.0	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	10	2.5	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	10	4.7	ug/l	
79-01-6	Trichloroethylene	629	10	3.5	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	20	5.0	ug/l	
75-01-4	Vinyl Chloride	ND	10	4.1	ug/l	
	m,p-Xylene	ND	20	4.7	ug/l	
95-47-6	o-Xylene	ND	10	2.6	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	92%		83-118%
17060-07-0	1,2-Dichloroethane-D4	97%		79-125%
2037-26-5	Toluene-D8	92%		85-112%
460-00-4	4-Bromofluorobenzene	92%		83-118%

(a) Associated CCV outside of control limits low.
(b) Associated CCV outside of control limits high, sample was ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SFMW-1A		
Lab Sample ID:	FA88901-12	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I70994.D	10	09/21/21 22:29	SO	n/a	n/a	VI2313
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	250	100	ug/l	
71-43-2	Benzene	ND	10	3.1	ug/l	
74-97-5	Bromochloromethane	ND	10	4.5	ug/l	
75-27-4	Bromodichloromethane	ND	10	2.4	ug/l	
75-25-2	Bromoform	ND	10	4.1	ug/l	
78-93-3	2-Butanone (MEK)	ND	50	20	ug/l	
75-15-0	Carbon Disulfide [a]	ND	20	5.3	ug/l	
56-23-5	Carbon Tetrachloride	ND	10	3.6	ug/l	
108-90-7	Chlorobenzene	ND	10	2.0	ug/l	
75-00-3	Chloroethane	ND	20	6.7	ug/l	
67-66-3	Chloroform	ND	10	3.0	ug/l	
110-82-7	Cyclohexane	ND	10	3.9	ug/l	
124-48-1	Dibromochloromethane	ND	10	2.8	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	50	10	ug/l	
106-93-4	1,2-Dibromoethane	ND	20	2.8	ug/l	
75-71-8	Dichlorodifluoromethane	ND	20	5.0	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	10	3.2	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	10	2.2	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	10	2.6	ug/l	
75-34-3	1,1-Dichloroethane	ND	10	3.4	ug/l	
107-06-2	1,2-Dichloroethane	ND	10	3.1	ug/l	
75-35-4	1,1-Dichloroethylene	ND	10	3.2	ug/l	
156-59-2	cis-1,2-Dichloroethylene	20.3	10	2.8	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	10	2.2	ug/l	
78-87-5	1,2-Dichloropropane	ND	10	4.3	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	10	2.9	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	10	2.1	ug/l	
100-41-4	Ethylbenzene	ND	10	3.6	ug/l	
76-13-1	Freon 113	ND	10	4.8	ug/l	
591-78-6	2-Hexanone	ND	100	20	ug/l	
98-82-8	Isopropylbenzene	ND	10	2.2	ug/l	
79-20-9	Methyl Acetate	ND	200	50	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SFMW-1A		
Lab Sample ID:	FA88901-12	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	50	20	ug/l	
74-87-3	Methyl Chloride	ND	20	5.0	ug/l	
108-87-2	Methylcyclohexane	ND	10	4.4	ug/l	
75-09-2	Methylene Chloride	ND	50	20	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	50	10	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	10	2.3	ug/l	
100-42-5	Styrene	ND	10	2.2	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	10	3.0	ug/l	
127-18-4	Tetrachloroethylene [b]	ND	10	2.2	ug/l	
108-88-3	Toluene	ND	10	3.0	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	20	6.1	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	20	5.0	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	10	2.5	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	10	4.7	ug/l	
79-01-6	Trichloroethylene	474	10	3.5	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	20	5.0	ug/l	
75-01-4	Vinyl Chloride	ND	10	4.1	ug/l	
	m,p-Xylene	ND	20	4.7	ug/l	
95-47-6	o-Xylene	ND	10	2.6	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	93%		83-118%
17060-07-0	1,2-Dichloroethane-D4	96%		79-125%
2037-26-5	Toluene-D8	92%		85-112%
460-00-4	4-Bromofluorobenzene	93%		83-118%

(a) Associated CCV outside of control limits low.
(b) Associated CCV outside of control limits high, sample was ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-5		
Lab Sample ID:	FA88901-13	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I70995.D	2.5	09/21/21 22:53	SO	n/a	n/a	VI2313
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	63	25	ug/l	
71-43-2	Benzene	ND	2.5	0.78	ug/l	
74-97-5	Bromochloromethane	ND	2.5	1.1	ug/l	
75-27-4	Bromodichloromethane	ND	2.5	0.61	ug/l	
75-25-2	Bromoform	ND	2.5	1.0	ug/l	
78-93-3	2-Butanone (MEK)	ND	13	5.0	ug/l	
75-15-0	Carbon Disulfide [a]	ND	5.0	1.3	ug/l	
56-23-5	Carbon Tetrachloride	ND	2.5	0.89	ug/l	
108-90-7	Chlorobenzene	ND	2.5	0.50	ug/l	
75-00-3	Chloroethane	ND	5.0	1.7	ug/l	
67-66-3	Chloroform	ND	2.5	0.75	ug/l	
110-82-7	Cyclohexane	ND	2.5	0.98	ug/l	
124-48-1	Dibromochloromethane	ND	2.5	0.69	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	13	2.6	ug/l	
106-93-4	1,2-Dibromoethane	ND	5.0	0.69	ug/l	
75-71-8	Dichlorodifluoromethane	ND	5.0	1.3	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	2.5	0.81	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	2.5	0.54	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	2.5	0.64	ug/l	
75-34-3	1,1-Dichloroethane	ND	2.5	0.85	ug/l	
107-06-2	1,2-Dichloroethane	ND	2.5	0.78	ug/l	
75-35-4	1,1-Dichloroethylene	ND	2.5	0.81	ug/l	
156-59-2	cis-1,2-Dichloroethylene	60.9	2.5	0.69	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	2.5	0.55	ug/l	
78-87-5	1,2-Dichloropropane	ND	2.5	1.1	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	2.5	0.73	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	2.5	0.54	ug/l	
100-41-4	Ethylbenzene	ND	2.5	0.89	ug/l	
76-13-1	Freon 113	ND	2.5	1.2	ug/l	
591-78-6	2-Hexanone	ND	25	5.0	ug/l	
98-82-8	Isopropylbenzene	ND	2.5	0.55	ug/l	
79-20-9	Methyl Acetate	ND	50	13	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-5		
Lab Sample ID:	FA88901-13	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	13	5.0	ug/l	
74-87-3	Methyl Chloride	ND	5.0	1.3	ug/l	
108-87-2	Methylcyclohexane	ND	2.5	1.1	ug/l	
75-09-2	Methylene Chloride	ND	13	5.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	13	2.5	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	2.5	0.57	ug/l	
100-42-5	Styrene	ND	2.5	0.56	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	2.5	0.75	ug/l	
127-18-4	Tetrachloroethylene [b]	ND	2.5	0.54	ug/l	
108-88-3	Toluene	ND	2.5	0.75	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	5.0	1.5	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	5.0	1.3	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	2.5	0.62	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	2.5	1.2	ug/l	
79-01-6	Trichloroethylene	187	2.5	0.86	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	5.0	1.3	ug/l	
75-01-4	Vinyl Chloride	ND	2.5	1.0	ug/l	
	m,p-Xylene	ND	5.0	1.2	ug/l	
95-47-6	o-Xylene	ND	2.5	0.64	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	93%		83-118%
17060-07-0	1,2-Dichloroethane-D4	97%		79-125%
2037-26-5	Toluene-D8	91%		85-112%
460-00-4	4-Bromofluorobenzene	94%		83-118%

(a) Associated CCV outside of control limits low.
(b) Associated CCV outside of control limits high, sample was ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-4		
Lab Sample ID:	FA88901-14	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I71016.D	50	09/22/21 12:07	SO	n/a	n/a	VI2314
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	1300	500	ug/l	
71-43-2	Benzene	ND	50	16	ug/l	
74-97-5	Bromochloromethane	ND	50	23	ug/l	
75-27-4	Bromodichloromethane	ND	50	12	ug/l	
75-25-2	Bromoform	ND	50	20	ug/l	
78-93-3	2-Butanone (MEK)	ND	250	100	ug/l	
75-15-0	Carbon Disulfide	ND	100	27	ug/l	
56-23-5	Carbon Tetrachloride	ND	50	18	ug/l	
108-90-7	Chlorobenzene	ND	50	10	ug/l	
75-00-3	Chloroethane	ND	100	33	ug/l	
67-66-3	Chloroform	ND	50	15	ug/l	
110-82-7	Cyclohexane	ND	50	20	ug/l	
124-48-1	Dibromochloromethane	ND	50	14	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	250	52	ug/l	
106-93-4	1,2-Dibromoethane	ND	100	14	ug/l	
75-71-8	Dichlorodifluoromethane	ND	100	25	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	50	16	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	50	11	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	50	13	ug/l	
75-34-3	1,1-Dichloroethane	ND	50	17	ug/l	
107-06-2	1,2-Dichloroethane	ND	50	16	ug/l	
75-35-4	1,1-Dichloroethylene	ND	50	16	ug/l	
156-59-2	cis-1,2-Dichloroethylene	442	50	14	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	50	11	ug/l	
78-87-5	1,2-Dichloropropane	ND	50	21	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	50	15	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	50	11	ug/l	
100-41-4	Ethylbenzene	ND	50	18	ug/l	
76-13-1	Freon 113	ND	50	24	ug/l	
591-78-6	2-Hexanone	ND	500	100	ug/l	
98-82-8	Isopropylbenzene	ND	50	11	ug/l	
79-20-9	Methyl Acetate	ND	1000	250	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-4		
Lab Sample ID:	FA88901-14	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	250	100	ug/l	
74-87-3	Methyl Chloride	ND	100	25	ug/l	
108-87-2	Methylcyclohexane	ND	50	22	ug/l	
75-09-2	Methylene Chloride	ND	250	100	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	250	50	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	50	11	ug/l	
100-42-5	Styrene	ND	50	11	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	50	15	ug/l	
127-18-4	Tetrachloroethylene	ND	50	11	ug/l	
108-88-3	Toluene	ND	50	15	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	100	31	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	100	25	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	50	12	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	50	23	ug/l	
79-01-6	Trichloroethylene	3700	50	17	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	100	25	ug/l	
75-01-4	Vinyl Chloride	ND	50	20	ug/l	
	m,p-Xylene	ND	100	23	ug/l	
95-47-6	o-Xylene	ND	50	13	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	91%		83-118%
17060-07-0	1,2-Dichloroethane-D4	98%		79-125%
2037-26-5	Toluene-D8	92%		85-112%
460-00-4	4-Bromofluorobenzene	93%		83-118%

(a) Associated CCV outside of control limits low.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	DUP-2		
Lab Sample ID:	FA88901-15	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I71039.D	50	09/23/21 10:07	SO	n/a	n/a	VI2316
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	1300	500	ug/l	
71-43-2	Benzene	ND	50	16	ug/l	
74-97-5	Bromochloromethane	ND	50	23	ug/l	
75-27-4	Bromodichloromethane	ND	50	12	ug/l	
75-25-2	Bromoform	ND	50	20	ug/l	
78-93-3	2-Butanone (MEK)	ND	250	100	ug/l	
75-15-0	Carbon Disulfide	ND	100	27	ug/l	
56-23-5	Carbon Tetrachloride	ND	50	18	ug/l	
108-90-7	Chlorobenzene	ND	50	10	ug/l	
75-00-3	Chloroethane	ND	100	33	ug/l	
67-66-3	Chloroform	ND	50	15	ug/l	
110-82-7	Cyclohexane	ND	50	20	ug/l	
124-48-1	Dibromochloromethane	ND	50	14	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	250	52	ug/l	
106-93-4	1,2-Dibromoethane	ND	100	14	ug/l	
75-71-8	Dichlorodifluoromethane [a]	ND	100	25	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	50	16	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	50	11	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	50	13	ug/l	
75-34-3	1,1-Dichloroethane	ND	50	17	ug/l	
107-06-2	1,2-Dichloroethane	ND	50	16	ug/l	
75-35-4	1,1-Dichloroethylene	ND	50	16	ug/l	
156-59-2	cis-1,2-Dichloroethylene	488	50	14	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	50	11	ug/l	
78-87-5	1,2-Dichloropropane	ND	50	21	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	50	15	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	50	11	ug/l	
100-41-4	Ethylbenzene	ND	50	18	ug/l	
76-13-1	Freon 113	ND	50	24	ug/l	
591-78-6	2-Hexanone	ND	500	100	ug/l	
98-82-8	Isopropylbenzene	ND	50	11	ug/l	
79-20-9	Methyl Acetate	ND	1000	250	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	DUP-2		
Lab Sample ID:	FA88901-15	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	250	100	ug/l	
74-87-3	Methyl Chloride	ND	100	25	ug/l	
108-87-2	Methylcyclohexane	ND	50	22	ug/l	
75-09-2	Methylene Chloride	ND	250	100	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	250	50	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	50	11	ug/l	
100-42-5	Styrene	ND	50	11	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	50	15	ug/l	
127-18-4	Tetrachloroethylene	ND	50	11	ug/l	
108-88-3	Toluene	ND	50	15	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	100	31	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	100	25	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	50	12	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	50	23	ug/l	
79-01-6	Trichloroethylene	3940	50	17	ug/l	
75-69-4	Trichlorofluoromethane [b]	ND	100	25	ug/l	
75-01-4	Vinyl Chloride	ND	50	20	ug/l	
	m,p-Xylene	ND	100	23	ug/l	
95-47-6	o-Xylene	ND	50	13	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	92%		83-118%
17060-07-0	1,2-Dichloroethane-D4	97%		79-125%
2037-26-5	Toluene-D8	91%		85-112%
460-00-4	4-Bromofluorobenzene	93%		83-118%

(a) Associated CCV outside of control limits low.
(b) Associated CCV and ECC outside DOD QSM control limits high.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-6		
Lab Sample ID:	FA88901-16	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I71018.D	25	09/22/21 12:55	SO	n/a	n/a	VI2314
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	630	250	ug/l	
71-43-2	Benzene	ND	25	7.8	ug/l	
74-97-5	Bromochloromethane	ND	25	11	ug/l	
75-27-4	Bromodichloromethane	ND	25	6.1	ug/l	
75-25-2	Bromoform	ND	25	10	ug/l	
78-93-3	2-Butanone (MEK)	ND	130	50	ug/l	
75-15-0	Carbon Disulfide	ND	50	13	ug/l	
56-23-5	Carbon Tetrachloride	ND	25	8.9	ug/l	
108-90-7	Chlorobenzene	ND	25	5.0	ug/l	
75-00-3	Chloroethane	ND	50	17	ug/l	
67-66-3	Chloroform	ND	25	7.5	ug/l	
110-82-7	Cyclohexane	ND	25	9.8	ug/l	
124-48-1	Dibromochloromethane	ND	25	6.9	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	130	26	ug/l	
106-93-4	1,2-Dibromoethane	ND	50	6.9	ug/l	
75-71-8	Dichlorodifluoromethane	ND	50	13	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	25	8.1	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	25	5.4	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	25	6.4	ug/l	
75-34-3	1,1-Dichloroethane	ND	25	8.5	ug/l	
107-06-2	1,2-Dichloroethane	ND	25	7.8	ug/l	
75-35-4	1,1-Dichloroethylene	ND	25	8.1	ug/l	
156-59-2	cis-1,2-Dichloroethylene	69.0	25	6.9	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	25	5.5	ug/l	
78-87-5	1,2-Dichloropropane	ND	25	11	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	25	7.3	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	25	5.4	ug/l	
100-41-4	Ethylbenzene	ND	25	8.9	ug/l	
76-13-1	Freon 113	ND	25	12	ug/l	
591-78-6	2-Hexanone	ND	250	50	ug/l	
98-82-8	Isopropylbenzene	ND	25	5.5	ug/l	
79-20-9	Methyl Acetate	ND	500	130	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-6		
Lab Sample ID:	FA88901-16	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	130	50	ug/l	
74-87-3	Methyl Chloride	ND	50	13	ug/l	
108-87-2	Methylcyclohexane	ND	25	11	ug/l	
75-09-2	Methylene Chloride	61.9	130	50	ug/l	J
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	130	25	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	25	5.7	ug/l	
100-42-5	Styrene	ND	25	5.6	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	25	7.5	ug/l	
127-18-4	Tetrachloroethylene	ND	25	5.4	ug/l	
108-88-3	Toluene	ND	25	7.5	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	50	15	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	50	13	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	25	6.2	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	25	12	ug/l	
79-01-6	Trichloroethylene	1470	25	8.6	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	50	13	ug/l	
75-01-4	Vinyl Chloride	ND	25	10	ug/l	
	m,p-Xylene	ND	50	12	ug/l	
95-47-6	o-Xylene	ND	25	6.4	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	93%		83-118%
17060-07-0	1,2-Dichloroethane-D4	98%		79-125%
2037-26-5	Toluene-D8	91%		85-112%
460-00-4	4-Bromofluorobenzene	92%		83-118%

(a) Associated CCV outside of control limits low.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-8		
Lab Sample ID:	FA88901-17	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I71019.D	2	09/22/21 13:19	SO	n/a	n/a	VI2314
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	50	20	ug/l	
71-43-2	Benzene	ND	2.0	0.62	ug/l	
74-97-5	Bromochloromethane	ND	2.0	0.90	ug/l	
75-27-4	Bromodichloromethane	ND	2.0	0.48	ug/l	
75-25-2	Bromoform	ND	2.0	0.81	ug/l	
78-93-3	2-Butanone (MEK)	ND	10	4.0	ug/l	
75-15-0	Carbon Disulfide	ND	4.0	1.1	ug/l	
56-23-5	Carbon Tetrachloride	ND	2.0	0.71	ug/l	
108-90-7	Chlorobenzene	ND	2.0	0.40	ug/l	
75-00-3	Chloroethane	ND	4.0	1.3	ug/l	
67-66-3	Chloroform	5.6	2.0	0.60	ug/l	
110-82-7	Cyclohexane	ND	2.0	0.78	ug/l	
124-48-1	Dibromochloromethane	ND	2.0	0.55	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	10	2.1	ug/l	
106-93-4	1,2-Dibromoethane	ND	4.0	0.55	ug/l	
75-71-8	Dichlorodifluoromethane	ND	4.0	1.0	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	2.0	0.65	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	2.0	0.43	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	2.0	0.51	ug/l	
75-34-3	1,1-Dichloroethane	ND	2.0	0.68	ug/l	
107-06-2	1,2-Dichloroethane	ND	2.0	0.62	ug/l	
75-35-4	1,1-Dichloroethylene	ND	2.0	0.64	ug/l	
156-59-2	cis-1,2-Dichloroethylene	9.3	2.0	0.55	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	2.0	0.44	ug/l	
78-87-5	1,2-Dichloropropane	ND	2.0	0.85	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	2.0	0.58	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	2.0	0.43	ug/l	
100-41-4	Ethylbenzene	ND	2.0	0.71	ug/l	
76-13-1	Freon 113	ND	2.0	0.96	ug/l	
591-78-6	2-Hexanone	ND	20	4.0	ug/l	
98-82-8	Isopropylbenzene	ND	2.0	0.44	ug/l	
79-20-9	Methyl Acetate	ND	40	10	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	SMMW-8		
Lab Sample ID:	FA88901-17	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	10	4.0	ug/l	
74-87-3	Methyl Chloride	ND	4.0	1.0	ug/l	
108-87-2	Methylcyclohexane	ND	2.0	0.87	ug/l	
75-09-2	Methylene Chloride	4.8	10	4.0	ug/l	J
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	10	2.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	2.0	0.46	ug/l	
100-42-5	Styrene	ND	2.0	0.44	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	2.0	0.60	ug/l	
127-18-4	Tetrachloroethylene	0.44	2.0	0.43	ug/l	J
108-88-3	Toluene	ND	2.0	0.60	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	4.0	1.2	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	4.0	1.0	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	2.0	0.50	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	2.0	0.93	ug/l	
79-01-6	Trichloroethylene	122	2.0	0.69	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	4.0	1.0	ug/l	
75-01-4	Vinyl Chloride	ND	2.0	0.82	ug/l	
	m,p-Xylene	ND	4.0	0.93	ug/l	
95-47-6	o-Xylene	ND	2.0	0.51	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	93%		83-118%
17060-07-0	1,2-Dichloroethane-D4	98%		79-125%
2037-26-5	Toluene-D8	92%		85-112%
460-00-4	4-Bromofluorobenzene	92%		83-118%

(a) Associated CCV outside of control limits low.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	B2SF		
Lab Sample ID:	FA88901-18	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I71020.D	2.5	09/22/21 13:43	SO	n/a	n/a	VI2314
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	63	25	ug/l	
71-43-2	Benzene	ND	2.5	0.78	ug/l	
74-97-5	Bromochloromethane	ND	2.5	1.1	ug/l	
75-27-4	Bromodichloromethane	ND	2.5	0.61	ug/l	
75-25-2	Bromoform	ND	2.5	1.0	ug/l	
78-93-3	2-Butanone (MEK)	ND	13	5.0	ug/l	
75-15-0	Carbon Disulfide	ND	5.0	1.3	ug/l	
56-23-5	Carbon Tetrachloride	ND	2.5	0.89	ug/l	
108-90-7	Chlorobenzene	ND	2.5	0.50	ug/l	
75-00-3	Chloroethane	ND	5.0	1.7	ug/l	
67-66-3	Chloroform	8.7	2.5	0.75	ug/l	
110-82-7	Cyclohexane	ND	2.5	0.98	ug/l	
124-48-1	Dibromochloromethane	ND	2.5	0.69	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	13	2.6	ug/l	
106-93-4	1,2-Dibromoethane	ND	5.0	0.69	ug/l	
75-71-8	Dichlorodifluoromethane	ND	5.0	1.3	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	2.5	0.81	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	2.5	0.54	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	2.5	0.64	ug/l	
75-34-3	1,1-Dichloroethane	ND	2.5	0.85	ug/l	
107-06-2	1,2-Dichloroethane	ND	2.5	0.78	ug/l	
75-35-4	1,1-Dichloroethylene	1.9	2.5	0.81	ug/l	J
156-59-2	cis-1,2-Dichloroethylene	21.2	2.5	0.69	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	2.5	0.55	ug/l	
78-87-5	1,2-Dichloropropane	ND	2.5	1.1	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	2.5	0.73	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	2.5	0.54	ug/l	
100-41-4	Ethylbenzene	ND	2.5	0.89	ug/l	
76-13-1	Freon 113	ND	2.5	1.2	ug/l	
591-78-6	2-Hexanone	ND	25	5.0	ug/l	
98-82-8	Isopropylbenzene	ND	2.5	0.55	ug/l	
79-20-9	Methyl Acetate	ND	50	13	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	B2SF		
Lab Sample ID:	FA88901-18	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	13	5.0	ug/l	
74-87-3	Methyl Chloride	ND	5.0	1.3	ug/l	
108-87-2	Methylcyclohexane	ND	2.5	1.1	ug/l	
75-09-2	Methylene Chloride	22.4	13	5.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	13	2.5	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	2.5	0.57	ug/l	
100-42-5	Styrene	ND	2.5	0.56	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	2.5	0.75	ug/l	
127-18-4	Tetrachloroethylene	0.80	2.5	0.54	ug/l	J
108-88-3	Toluene	ND	2.5	0.75	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	5.0	1.5	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	5.0	1.3	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	2.5	0.62	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	2.5	1.2	ug/l	
79-01-6	Trichloroethylene	192	2.5	0.86	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	5.0	1.3	ug/l	
75-01-4	Vinyl Chloride	ND	2.5	1.0	ug/l	
	m,p-Xylene	ND	5.0	1.2	ug/l	
95-47-6	o-Xylene	ND	2.5	0.64	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	93%		83-118%
17060-07-0	1,2-Dichloroethane-D4	98%		79-125%
2037-26-5	Toluene-D8	91%		85-112%
460-00-4	4-Bromofluorobenzene	93%		83-118%

(a) Associated CCV outside of control limits low.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	B1SF		
Lab Sample ID:	FA88901-19	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I71021.D	100	09/22/21 14:07	SO	n/a	n/a	VI2314
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	2500	1000	ug/l	
71-43-2	Benzene	ND	100	31	ug/l	
74-97-5	Bromochloromethane	ND	100	45	ug/l	
75-27-4	Bromodichloromethane	ND	100	24	ug/l	
75-25-2	Bromoform	ND	100	41	ug/l	
78-93-3	2-Butanone (MEK)	ND	500	200	ug/l	
75-15-0	Carbon Disulfide	ND	200	53	ug/l	
56-23-5	Carbon Tetrachloride	ND	100	36	ug/l	
108-90-7	Chlorobenzene	ND	100	20	ug/l	
75-00-3	Chloroethane	ND	200	67	ug/l	
67-66-3	Chloroform	ND	100	30	ug/l	
110-82-7	Cyclohexane	ND	100	39	ug/l	
124-48-1	Dibromochloromethane	ND	100	28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	500	100	ug/l	
106-93-4	1,2-Dibromoethane	ND	200	28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	200	50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	100	32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	100	22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	100	26	ug/l	
75-34-3	1,1-Dichloroethane	ND	100	34	ug/l	
107-06-2	1,2-Dichloroethane	ND	100	31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	100	32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	773	100	28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	100	22	ug/l	
78-87-5	1,2-Dichloropropane	ND	100	43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	100	29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	100	21	ug/l	
100-41-4	Ethylbenzene	ND	100	36	ug/l	
76-13-1	Freon 113	ND	100	48	ug/l	
591-78-6	2-Hexanone	ND	1000	200	ug/l	
98-82-8	Isopropylbenzene	ND	100	22	ug/l	
79-20-9	Methyl Acetate	ND	2000	500	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	B1SF		
Lab Sample ID:	FA88901-19	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	500	200	ug/l	
74-87-3	Methyl Chloride	ND	200	50	ug/l	
108-87-2	Methylcyclohexane	ND	100	44	ug/l	
75-09-2	Methylene Chloride	209	500	200	ug/l	J
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	500	100	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	100	23	ug/l	
100-42-5	Styrene	ND	100	22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	100	30	ug/l	
127-18-4	Tetrachloroethylene	ND	100	22	ug/l	
108-88-3	Toluene	ND	100	30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	200	61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	200	50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	100	25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	100	47	ug/l	
79-01-6	Trichloroethylene	5710	100	35	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	200	50	ug/l	
75-01-4	Vinyl Chloride	ND	100	41	ug/l	
	m,p-Xylene	ND	200	47	ug/l	
95-47-6	o-Xylene	ND	100	26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	93%		83-118%
17060-07-0	1,2-Dichloroethane-D4	97%		79-125%
2037-26-5	Toluene-D8	91%		85-112%
460-00-4	4-Bromofluorobenzene	91%		83-118%

(a) Associated CCV outside of control limits low.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	B4SF		
Lab Sample ID:	FA88901-20	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I71022.D	20	09/22/21 14:31	SO	n/a	n/a	VI2314
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	500	200	ug/l	
71-43-2	Benzene	ND	20	6.2	ug/l	
74-97-5	Bromochloromethane	ND	20	9.0	ug/l	
75-27-4	Bromodichloromethane	ND	20	4.8	ug/l	
75-25-2	Bromoform	ND	20	8.1	ug/l	
78-93-3	2-Butanone (MEK)	ND	100	40	ug/l	
75-15-0	Carbon Disulfide	ND	40	11	ug/l	
56-23-5	Carbon Tetrachloride	ND	20	7.1	ug/l	
108-90-7	Chlorobenzene	ND	20	4.0	ug/l	
75-00-3	Chloroethane	ND	40	13	ug/l	
67-66-3	Chloroform	ND	20	6.0	ug/l	
110-82-7	Cyclohexane	ND	20	7.8	ug/l	
124-48-1	Dibromochloromethane	ND	20	5.5	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	100	21	ug/l	
106-93-4	1,2-Dibromoethane	ND	40	5.5	ug/l	
75-71-8	Dichlorodifluoromethane	ND	40	10	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	20	6.5	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	20	4.3	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	20	5.1	ug/l	
75-34-3	1,1-Dichloroethane	ND	20	6.8	ug/l	
107-06-2	1,2-Dichloroethane	ND	20	6.2	ug/l	
75-35-4	1,1-Dichloroethylene	ND	20	6.4	ug/l	
156-59-2	cis-1,2-Dichloroethylene	93.6	20	5.5	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	20	4.4	ug/l	
78-87-5	1,2-Dichloropropane	ND	20	8.5	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	20	5.8	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	20	4.3	ug/l	
100-41-4	Ethylbenzene	ND	20	7.1	ug/l	
76-13-1	Freon 113	ND	20	9.6	ug/l	
591-78-6	2-Hexanone	ND	200	40	ug/l	
98-82-8	Isopropylbenzene	ND	20	4.4	ug/l	
79-20-9	Methyl Acetate	ND	400	100	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	B4SF		
Lab Sample ID:	FA88901-20	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	100	40	ug/l	
74-87-3	Methyl Chloride	ND	40	10	ug/l	
108-87-2	Methylcyclohexane	ND	20	8.7	ug/l	
75-09-2	Methylene Chloride	ND	100	40	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	100	20	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	20	4.6	ug/l	
100-42-5	Styrene	ND	20	4.4	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	20	6.0	ug/l	
127-18-4	Tetrachloroethylene	ND	20	4.3	ug/l	
108-88-3	Toluene	ND	20	6.0	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	40	12	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	40	10	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	20	5.0	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	20	9.3	ug/l	
79-01-6	Trichloroethylene	1580	20	6.9	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	40	10	ug/l	
75-01-4	Vinyl Chloride	ND	20	8.2	ug/l	
	m,p-Xylene	ND	40	9.3	ug/l	
95-47-6	o-Xylene	ND	20	5.1	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	93%		83-118%
17060-07-0	1,2-Dichloroethane-D4	98%		79-125%
2037-26-5	Toluene-D8	91%		85-112%
460-00-4	4-Bromofluorobenzene	94%		83-118%

(a) Associated CCV outside of control limits low.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	B3SF		
Lab Sample ID:	FA88901-21	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I71066.D	10	09/24/21 10:28	SO	n/a	n/a	VI2319
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	250	100	ug/l	
71-43-2	Benzene	ND	10	3.1	ug/l	
74-97-5	Bromochloromethane	ND	10	4.5	ug/l	
75-27-4	Bromodichloromethane	ND	10	2.4	ug/l	
75-25-2	Bromoform	ND	10	4.1	ug/l	
78-93-3	2-Butanone (MEK)	ND	50	20	ug/l	
75-15-0	Carbon Disulfide	ND	20	5.3	ug/l	
56-23-5	Carbon Tetrachloride	ND	10	3.6	ug/l	
108-90-7	Chlorobenzene	ND	10	2.0	ug/l	
75-00-3	Chloroethane	ND	20	6.7	ug/l	
67-66-3	Chloroform	ND	10	3.0	ug/l	
110-82-7	Cyclohexane	ND	10	3.9	ug/l	
124-48-1	Dibromochloromethane	ND	10	2.8	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	50	10	ug/l	
106-93-4	1,2-Dibromoethane	ND	20	2.8	ug/l	
75-71-8	Dichlorodifluoromethane	ND	20	5.0	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	10	3.2	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	10	2.2	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	10	2.6	ug/l	
75-34-3	1,1-Dichloroethane	ND	10	3.4	ug/l	
107-06-2	1,2-Dichloroethane	ND	10	3.1	ug/l	
75-35-4	1,1-Dichloroethylene	ND	10	3.2	ug/l	
156-59-2	cis-1,2-Dichloroethylene	126	10	2.8	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	10	2.2	ug/l	
78-87-5	1,2-Dichloropropane	ND	10	4.3	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	10	2.9	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	10	2.1	ug/l	
100-41-4	Ethylbenzene	ND	10	3.6	ug/l	
76-13-1	Freon 113	ND	10	4.8	ug/l	
591-78-6	2-Hexanone	ND	100	20	ug/l	
98-82-8	Isopropylbenzene	ND	10	2.2	ug/l	
79-20-9	Methyl Acetate	ND	200	50	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	B3SF		
Lab Sample ID:	FA88901-21	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	50	20	ug/l	
74-87-3	Methyl Chloride	ND	20	5.0	ug/l	
108-87-2	Methylcyclohexane	ND	10	4.4	ug/l	
75-09-2	Methylene Chloride	ND	50	20	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	50	10	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	10	2.3	ug/l	
100-42-5	Styrene	ND	10	2.2	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	10	3.0	ug/l	
127-18-4	Tetrachloroethylene	ND	10	2.2	ug/l	
108-88-3	Toluene	ND	10	3.0	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	20	6.1	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	20	5.0	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	10	2.5	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	10	4.7	ug/l	
79-01-6	Trichloroethylene	871	10	3.5	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	20	5.0	ug/l	
75-01-4	Vinyl Chloride	ND	10	4.1	ug/l	
	m,p-Xylene	ND	20	4.7	ug/l	
95-47-6	o-Xylene	ND	10	2.6	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	91%		83-118%
17060-07-0	1,2-Dichloroethane-D4	97%		79-125%
2037-26-5	Toluene-D8	92%		85-112%
460-00-4	4-Bromofluorobenzene	92%		83-118%

(a) Associated CCV outside of control limits high.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	B5SF		
Lab Sample ID:	FA88901-22	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I71049.D	10	09/23/21 14:07	SO	n/a	n/a	VI2316
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	250	100	ug/l	
71-43-2	Benzene	ND	10	3.1	ug/l	
74-97-5	Bromochloromethane	ND	10	4.5	ug/l	
75-27-4	Bromodichloromethane	ND	10	2.4	ug/l	
75-25-2	Bromoform	ND	10	4.1	ug/l	
78-93-3	2-Butanone (MEK)	96.8	50	20	ug/l	
75-15-0	Carbon Disulfide	ND	20	5.3	ug/l	
56-23-5	Carbon Tetrachloride	ND	10	3.6	ug/l	
108-90-7	Chlorobenzene	ND	10	2.0	ug/l	
75-00-3	Chloroethane	ND	20	6.7	ug/l	
67-66-3	Chloroform	ND	10	3.0	ug/l	
110-82-7	Cyclohexane	ND	10	3.9	ug/l	
124-48-1	Dibromochloromethane	ND	10	2.8	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	50	10	ug/l	
106-93-4	1,2-Dibromoethane	ND	20	2.8	ug/l	
75-71-8	Dichlorodifluoromethane [a]	ND	20	5.0	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	10	3.2	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	10	2.2	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	10	2.6	ug/l	
75-34-3	1,1-Dichloroethane	ND	10	3.4	ug/l	
107-06-2	1,2-Dichloroethane	ND	10	3.1	ug/l	
75-35-4	1,1-Dichloroethylene	ND	10	3.2	ug/l	
156-59-2	cis-1,2-Dichloroethylene	66.9	10	2.8	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	10	2.2	ug/l	
78-87-5	1,2-Dichloropropane	ND	10	4.3	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	10	2.9	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	10	2.1	ug/l	
100-41-4	Ethylbenzene	ND	10	3.6	ug/l	
76-13-1	Freon 113	ND	10	4.8	ug/l	
591-78-6	2-Hexanone	ND	100	20	ug/l	
98-82-8	Isopropylbenzene	ND	10	2.2	ug/l	
79-20-9	Methyl Acetate	ND	200	50	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	B5SF		
Lab Sample ID:	FA88901-22	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	50	20	ug/l	
74-87-3	Methyl Chloride	ND	20	5.0	ug/l	
108-87-2	Methylcyclohexane	ND	10	4.4	ug/l	
75-09-2	Methylene Chloride	ND	50	20	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	50	10	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	10	2.3	ug/l	
100-42-5	Styrene	ND	10	2.2	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	10	3.0	ug/l	
127-18-4	Tetrachloroethylene	ND	10	2.2	ug/l	
108-88-3	Toluene	ND	10	3.0	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	20	6.1	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	20	5.0	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	10	2.5	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	10	4.7	ug/l	
79-01-6	Trichloroethylene	838	10	3.5	ug/l	
75-69-4	Trichlorofluoromethane [b]	ND	20	5.0	ug/l	
75-01-4	Vinyl Chloride	ND	10	4.1	ug/l	
	m,p-Xylene	ND	20	4.7	ug/l	
95-47-6	o-Xylene	ND	10	2.6	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	94%		83-118%
17060-07-0	1,2-Dichloroethane-D4	98%		79-125%
2037-26-5	Toluene-D8	91%		85-112%
460-00-4	4-Bromofluorobenzene	92%		83-118%

(a) Associated CCV outside of control limits low.
(b) Associated CCV and ECC outside DOD QSM control limits high.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	TMW-1		
Lab Sample ID:	FA88901-23	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I71050.D	1	09/23/21 14:31	SO	n/a	n/a	VI2316
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	0.26	1.0	0.24	ug/l	J
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	0.57	1.0	0.30	ug/l	J
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane [a]	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	TMW-1		
Lab Sample ID:	FA88901-23	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane [b]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	95%		83-118%
17060-07-0	1,2-Dichloroethane-D4	99%		79-125%
2037-26-5	Toluene-D8	92%		85-112%
460-00-4	4-Bromofluorobenzene	92%		83-118%

(a) Associated CCV outside of control limits low.
(b) Associated CCV and ECC outside DOD QSM control limits high.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	TMW-2		
Lab Sample ID:	FA88901-24	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I71051.D	1	09/23/21 14:56	SO	n/a	n/a	VI2316
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	0.61	1.0	0.30	ug/l	J
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane [a]	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	TMW-2		
Lab Sample ID:	FA88901-24	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane [b]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	95%		83-118%
17060-07-0	1,2-Dichloroethane-D4	100%		79-125%
2037-26-5	Toluene-D8	92%		85-112%
460-00-4	4-Bromofluorobenzene	91%		83-118%

(a) Associated CCV outside of control limits low.
(b) Associated CCV and ECC outside DOD QSM control limits high.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	RTB-3		
Lab Sample ID:	FA88901-25	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I71052.D	25	09/23/21 15:20	SO	n/a	n/a	VI2316
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	630	250	ug/l	
71-43-2	Benzene	ND	25	7.8	ug/l	
74-97-5	Bromochloromethane	ND	25	11	ug/l	
75-27-4	Bromodichloromethane	ND	25	6.1	ug/l	
75-25-2	Bromoform	ND	25	10	ug/l	
78-93-3	2-Butanone (MEK)	ND	130	50	ug/l	
75-15-0	Carbon Disulfide	ND	50	13	ug/l	
56-23-5	Carbon Tetrachloride	ND	25	8.9	ug/l	
108-90-7	Chlorobenzene	ND	25	5.0	ug/l	
75-00-3	Chloroethane	ND	50	17	ug/l	
67-66-3	Chloroform	ND	25	7.5	ug/l	
110-82-7	Cyclohexane	ND	25	9.8	ug/l	
124-48-1	Dibromochloromethane	ND	25	6.9	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	130	26	ug/l	
106-93-4	1,2-Dibromoethane	ND	50	6.9	ug/l	
75-71-8	Dichlorodifluoromethane [a]	ND	50	13	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	25	8.1	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	25	5.4	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	25	6.4	ug/l	
75-34-3	1,1-Dichloroethane	ND	25	8.5	ug/l	
107-06-2	1,2-Dichloroethane	ND	25	7.8	ug/l	
75-35-4	1,1-Dichloroethylene	ND	25	8.1	ug/l	
156-59-2	cis-1,2-Dichloroethylene	469	25	6.9	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	25	5.5	ug/l	
78-87-5	1,2-Dichloropropane	ND	25	11	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	25	7.3	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	25	5.4	ug/l	
100-41-4	Ethylbenzene	ND	25	8.9	ug/l	
76-13-1	Freon 113	ND	25	12	ug/l	
591-78-6	2-Hexanone	ND	250	50	ug/l	
98-82-8	Isopropylbenzene	ND	25	5.5	ug/l	
79-20-9	Methyl Acetate	ND	500	130	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	RTB-3		
Lab Sample ID:	FA88901-25	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	130	50	ug/l	
74-87-3	Methyl Chloride	ND	50	13	ug/l	
108-87-2	Methylcyclohexane	ND	25	11	ug/l	
75-09-2	Methylene Chloride	ND	130	50	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	130	25	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	25	5.7	ug/l	
100-42-5	Styrene	ND	25	5.6	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	25	7.5	ug/l	
127-18-4	Tetrachloroethylene	ND	25	5.4	ug/l	
108-88-3	Toluene	ND	25	7.5	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	50	15	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	50	13	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	25	6.2	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	25	12	ug/l	
79-01-6	Trichloroethylene	2030	25	8.6	ug/l	
75-69-4	Trichlorofluoromethane [b]	ND	50	13	ug/l	
75-01-4	Vinyl Chloride	ND	25	10	ug/l	
	m,p-Xylene	ND	50	12	ug/l	
95-47-6	o-Xylene	ND	25	6.4	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	93%		83-118%
17060-07-0	1,2-Dichloroethane-D4	99%		79-125%
2037-26-5	Toluene-D8	91%		85-112%
460-00-4	4-Bromofluorobenzene	92%		83-118%

(a) Associated CCV outside of control limits low.
(b) Associated CCV and ECC outside DOD QSM control limits high.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	RTB-4		
Lab Sample ID:	FA88901-26	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I71067.D	1	09/24/21 10:52	SO	n/a	n/a	VI2319
Run #2	I71053.D	2	09/23/21 15:43	SO	n/a	n/a	VI2316

	Purge Volume
Run #1	5.0 ml
Run #2	5.0 ml

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	10.6	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	RTB-4		
Lab Sample ID:	FA88901-26	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	0.43	1.0	0.22	ug/l	J
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	88.5 [a]	2.0	0.69	ug/l	
75-69-4	Trichlorofluoromethane [b]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	93%	94%	83-118%
17060-07-0	1,2-Dichloroethane-D4	97%	99%	79-125%
2037-26-5	Toluene-D8	92%	91%	85-112%
460-00-4	4-Bromofluorobenzene	92%	90%	83-118%

(a) Result is from Run# 2
(b) Associated CCV outside of control limits high.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID: TB
Lab Sample ID: FA88901-27
Matrix: AQ - Trip Blank Water
Method: SW846 8260D
Project: FPE; Edgefield, SC

Date Sampled: 09/07/21
Date Received: 09/14/21
Percent Solids: n/a

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	2A37775.D	1	09/20/21 13:18	CV	n/a	n/a	V2A1591
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane [a]	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	TB		
Lab Sample ID:	FA88901-27	**Date Sampled:**	09/07/21
Matrix:	AQ - Trip Blank Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	0.36	1.0	0.30	ug/l	J
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	97%		83-118%
17060-07-0	1,2-Dichloroethane-D4	99%		79-125%
2037-26-5	Toluene-D8	100%		85-112%
460-00-4	4-Bromofluorobenzene	99%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Misc. Forms

Custody Documents and Other Forms

Includes the following where applicable:

- Chain of Custody

ARCADIS | ID#: | **CHAIN OF CUSTODY & LABORATORY ANALYSIS REQUEST FORM** | Page ___ of ___ | Lab Work Order # FA88901

Send Results to:
Contact & Company Name: Jeff Beckner
Telephone: 706-828-4421
Address: 1450 Greene St, Suite 220
Fax:
City: Augusta State: GA Zip: 30901
E-mail Address:
Project Name/Location (City, State): PPE Edgefield, SC
Project #:
Sampler's Printed Name: J. O'Brien
Sampler's Signature:

	Preservative	Filtered (✓)	# of Containers	Container Information
	B		3	1

PARAMETER ANALYSIS & METHOD

V8260TC 2,8

Keys

Preservation Key: A. H_2SO_4; B. HCL; C. HNO_3; D. NaOH; E. None; F. Other: _____; G. Other: _____; H. Other: _____

Container Information Key: 1. 40 ml Vial; 2. 1 L Amber; 3. 250 ml Plastic; 4. 500 ml Plastic; 5. Encore; 6. 2 oz. Glass; 7. 4 oz. Glass; 8. 8 oz. Glass; 9. Other: _____; 10. Other: _____

Matrix Key: SO - Soil; W - Water; T - Tissue; SE - Sediment; SL - Sludge; A - Air; NL - NAPL/Oil; SW - Sample Wipe; Other: _____

	Sample ID	Collection Date	Collection Time	Type (✓) Comp	Type (✓) Grab	Matrix		REMARKS
1	SMMW-1	9-7	0939		✓	W	3	
2	RWMW-2	9-7	1043		✓	W	3	
3	RWMW-1	9-7	1230		✓	W	3	
4	SMMW-13	9-7	1324		✓	W	3	
5	SMMW-11	9-7	1421		✓	W	3	
6	SMMW-10	9-7	1454		✓	W	3	
7	SMMW-3	9-8	0822		✓	W	3	
8	SMMW-9	9-8	0900		✓	W	3	
9	SMMW-7	9-8	0958		✓	W	3	
10	SMMW-12	9-8	1049		✓	W	3	
11	SMMW-2	9-8	1159		✓	W	3	
12	SFMW-1A	9-8	1250		✓	W	3	
13	SMMW-5	9-8	1345		✓	W	3	
14	SMMW-4	9-9	0850		✓	W	3	

INITIAL ASSESSMENT JN

Special Instructions/Comments:

☐ Special QA/QC Instructions(✓):

LABEL VERIFICATION

Laboratory Information and Receipt		Relinquished By	Received By	Relinquished By	Laboratory Received By
Lab Name: SGS	Cooler Custody Seal (✓) ☐ Intact ☐ Not Intact	Printed Name: J. O'Brien	Printed Name: FX	Printed Name: FX	Printed Name: Peter H.
# Cooler packed with ice (✓)		Signature:	Signature:	Signature:	Signature:
Specify Turnaround Requirements:	Sample Receipt:	Firm: ARCADIS	Firm/Courier:	Firm/Courier:	Firm: SGS
Shipping Tracking #:	Condition/Cooler Temp: _____	Date/Time: 9-13-21 1400	Date/Time:	Date/Time:	Date/Time: 9/14/21 0906

20730826 CofC AR Form 08.27.2015

Distribution: WHITE – Laboratory returns with results; YELLOW – Lab copy; PINK – Retained by Arcadis

FA88901: Chain of Custody
Page 1 of 3

ARCADIS

ID#:

CHAIN OF CUSTODY & LABORATORY ANALYSIS REQUEST FORM

Page ___ of ___

Lab Work Order #: FA88901

Send Results to:

Contact & Company Name: Jeff BECKNER

Telephone: 706-828-4421

Address: 1450 greene ST STE 220

Fax:

City: AUGUSTA State: GA Zip: 30901

E-mail Address:

Project Name/Location (City, State): FPE Edgefield SC

Project #:

Sampler's Printed Name: J. OBRIEN

Sampler's Signature:

Preservative	B							
Filtered (✓)								
# of Containers	3							
Container Information	1							

PARAMETER ANALYSIS & METHOD

TB260TOTL 20

Keys

Preservation Key:
A. H_2SO_4
B. HCL
C. HNO_3
D. NaOH
E. None
F. Other: _____
G. Other: _____
H. Other: _____

Container Information Key:
1. 40 ml Vial
2. 1 L Amber
3. 250 ml Plastic
4. 500 ml Plastic
5. Encore
6. 2 oz. Glass
7. 4 oz. Glass
8. 8 oz. Glass
9. Other: _____
10. Other: _____

Matrix Key:
SO - Soil
W - Water
T - Tissue
SE - Sediment
SL - Sludge
A - Air
NL - NAPL/Oil
SW - Sample Wipe
Other: _____

	Sample ID	Collection Date	Collection Time	Type (✓) Comp	Type (✓) Grab	Matrix		REMARKS
15	DUP-2	9.9	—		✓	W	3	
16	SMMW-6	9-9	0948		✓	W	3	
17	SMMW-8	9-9	1036		✓	W	3	
18	B25F	9-9	1230		✓	W	3	
19	B1SF	9-9	1320		✓	W	3	
20	B4SF	9-9	1410		✓	W	3	
21	B3SF	9-10	0820		✓	W	3	
22	B5SF	9-10	0905		✓	W	3	
23	IMW-1	9-10	1046		✓	W	3	
24	IMW-2	9-10	1203		✓	W	3	
25	RTB-3	9-10	1257		✓	W	3	
26	RTB-4	9-10	1333		✓	W	3	
27	TB						3	

Special Instructions/Comments:

☐ Special QA/QC Instructions(✓):

Laboratory Information and Receipt		Relinquished By	Received By	Relinquished By	Laboratory Received By
Lab Name: SGS	Cooler Custody Seal (✓)	Printed Name: J. OBRIEN	Printed Name: FX	Printed Name: FX	Printed Name: Peter H
☒ Cooler packed with ice (✓)	☐ Intact ☐ Not Intact	Signature:	Signature:	Signature:	Signature:
Specify Turnaround Requirements:	Sample Receipt:	Firm: ARCADIS	Firm/Courier:	Firm/Courier:	Firm: SGS
Shipping Tracking #:	Condition/Cooler Temp: _____	Date/Time: 9.13.21/1400	Date/Time:	Date/Time:	Date/Time: 9/14/21 1000

20730826 CofC AR Form 08.27.2015

Distribution: WHITE – Laboratory returns with results; YELLOW – Lab copy; PINK – Retained by Arcadis

FA88901: Chain of Custody
Page 2 of 3

SGS Sample Receipt Summary

Job Number: FA88901 **Client:** ARCADIS **Project:** FPE.EDGEFIELD

Date / Time Received: 9/14/2021 10:00:00 AM **Delivery Method:** FX **Airbill #'s:** 5061 4510 5406

Therm ID: IR 1; **Therm CF:** 0.2; **# of Coolers:** 1

Cooler Temps (Raw Measured) °C: Cooler 1: (2.6);

Cooler Temps (Corrected) °C: Cooler 1: (2.8);

Cooler Information	Y	or	N
1. Custody Seals Present	☑		☐
2. Custody Seals Intact	☑		☐
3. Temp criteria achieved	☑		☐
4. Cooler temp verification	IR Gun		
5. Cooler media	Ice (Bag)		

Trip Blank Information	Y	or	N	N/A
1. Trip Blank present / cooler	☑		☐	☐
2. Trip Blank listed on COC	☑		☐	☐

	W	or	S	N/A
3. Type Of TB Received	☑		☐	☐

Sample Information	Y	or	N	N/A
1. Sample labels present on bottles	☑		☐	
2. Samples preserved properly	☑		☐	
3. Sufficient volume/containers recvd for analysis:	☑		☐	
4. Condition of sample	Intact			
5. Sample recvd within HT	☑		☐	
6. Dates/Times/IDs on COC match Sample Label	☑		☐	
7. VOCs have headspace	☐		☑	☐
8. Bottles received for unspecified tests	☐		☑	
9. Compositing instructions clear	☐		☐	☑
10. Voa Soil Kits/Jars received past 48hrs?	☐		☐	☑
11. % Solids Jar received?	☐		☐	☑
12. Residual Chlorine Present?	☐		☐	☑

Misc. Information

Number of Encores: 25-Gram _____ 5-Gram _____ Number of 5035 Field Kits: _____ Number of Lab Filtered Metals: _____

Test Strip Lot #s: pH 0-3 230315 pH 10-12 219813A Other: (Specify) _____ _____

Residual Chlorine Test Strip Lot #: _____

Comments

SM001
Rev. Date 05/24/17

Technician: PETERH Date: 9/14/2021 10:00:00 A Reviewer: _____ Date: _____

FA88901: Chain of Custody
Page 3 of 3

The results set forth herein are provided by SGS North America Inc.

e-Hardcopy 2.0
Automated Report

Technical Report for

ARCADIS Geraghty & Miller

FPE; Edgefield, SC

30067293.2.2

SGS Job Number: FA88902

Sampling Dates: 09/07/21 - 09/10/21

Report to:

ARCADIS Geraghty & Miller

jbeckner@arcadis-us.com

ATTN: Jeff Beckner

Total number of pages in report: 50

Test results contained within this data package meet the requirements of the National Environmental Laboratory Accreditation Program and/or state specific certification programs as applicable.

Norm Farmer
Technical Director

Client Service contact: Evita Martinez 407-425-6700

Certifications: FL(E83510), LA(03051), KS(E-10327), NC(573), NJ(FL002), NY(12022), SC(96038001) DoD ELAP(ANAB L2229), AZ(AZ0806), CA(2937), TX(T104704404), PA(68-03573), VA(460177), AL, AK, AR, CT, IA, KY, MA, MI. MS, ND, NH, NV, OK, OR, UT, VT, WA, WV

Table of Contents

Sample Summary

ARCADIS Geraghty & Miller

Job No: FA88902

FPE; Edgefield, SC
Project No: 30067293.2.2

Sample Number	Collected Date	Time	By	Received	Matrix Code	Type	Client Sample ID
This report contains results reported as ND = Not detected. The following applies: Organics ND = Not detected above the MDL							
FA88902-1	09/07/21	11:45	AB	09/14/21	AQ	Ground Water	LBMW-101
FA88902-2	09/07/21	13:30	AB	09/14/21	AQ	Ground Water	LBMW-102
FA88902-3	09/08/21	09:55	AB	09/14/21	AQ	Ground Water	LBMW-103
FA88902-4	09/07/21	15:30	AB	09/14/21	AQ	Ground Water	LBMW-104
FA88902-5	09/09/21	09:04	AB	09/14/21	AQ	Ground Water	MW-8
FA88902-6	09/10/21	09:45	AB	09/14/21	AQ	Ground Water	MW-17
FA88902-7	09/09/21	13:40	AB	09/14/21	AQ	Ground Water	MW-20
FA88902-8	09/08/21	14:30	AB	09/14/21	AQ	Ground Water	MW-25
FA88902-9	09/09/21	12:30	AB	09/14/21	AQ	Ground Water	MW-26
FA88902-10	09/09/21	11:38	AB	09/14/21	AQ	Ground Water	MW-27
FA88902-11	09/10/21	08:50	AB	09/14/21	AQ	Ground Water	MW-28
FA88902-12	09/09/21	10:23	AB	09/14/21	AQ	Ground Water	MW-32

Sample Summary
(continued)

ARCADIS Geraghty & Miller

Job No: FA88902

FPE; Edgefield, SC
Project No: 30067293.2.2

Sample Number	Collected Date	Time	By	Received	Matrix Code	Type	Client Sample ID
FA88902-13	09/08/21	13:32	AB	09/14/21	AQ	Ground Water	MW-33
FA88902-14	09/08/21	12:18	AB	09/14/21	AQ	Ground Water	MW-42
FA88902-15	09/08/21	11:04	AB	09/14/21	AQ	Ground Water	MW-45
FA88902-16	09/10/21	11:32	AB	09/14/21	AQ	Ground Water	MW-52
FA88902-17	09/10/21	14:05	AB	09/14/21	AQ	Ground Water	MW-53
FA88902-18	09/10/21	10:36	AB	09/14/21	AQ	Ground Water	MW-54
FA88902-19	09/10/21	00:00	AB	09/14/21	AQ	Ground Water	DUP-03

Summary of Hits

Job Number: FA88902
Account: ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC
Collected: 09/07/21 thru 09/10/21

Lab Sample ID / Analyte	Client Sample ID	Result/ Qual	RL	MDL	Units	Method
FA88902-1	**LBMW-101**					
2-Butanone (MEK)		2.9 J	5.0	2.0	ug/l	SW846 8260D
FA88902-2	**LBMW-102**					
Acetone		45.2	25	10	ug/l	SW846 8260D
2-Butanone (MEK)		66.2	5.0	2.0	ug/l	SW846 8260D
cis-1,2-Dichloroethylene		1.7	1.0	0.28	ug/l	SW846 8260D
2-Hexanone		5.7 J	10	2.0	ug/l	SW846 8260D
Vinyl Chloride		1.2	1.0	0.41	ug/l	SW846 8260D
FA88902-3	**LBMW-103**					
2-Butanone (MEK)		8.6	5.0	2.0	ug/l	SW846 8260D
Carbon Disulfide		1.1 J	2.0	0.53	ug/l	SW846 8260D
FA88902-4	**LBMW-104**					
2-Butanone (MEK)		2.4 J	5.0	2.0	ug/l	SW846 8260D
FA88902-5	**MW-8**					
Chloroform		3.3	1.0	0.30	ug/l	SW846 8260D
1,1-Dichloroethylene		0.72 J	1.0	0.32	ug/l	SW846 8260D
Tetrachloroethylene		0.45 J	1.0	0.22	ug/l	SW846 8260D
Trichloroethylene		2.6	1.0	0.35	ug/l	SW846 8260D
FA88902-6	**MW-17**					
1,1-Dichloroethylene		14.8	10	3.2	ug/l	SW846 8260D
cis-1,2-Dichloroethylene		9.3 J	10	2.8	ug/l	SW846 8260D
Tetrachloroethylene		31.2	10	2.2	ug/l	SW846 8260D
Trichloroethylene		788	10	3.5	ug/l	SW846 8260D
FA88902-7	**MW-20**					
Chloroform		3.4	1.0	0.30	ug/l	SW846 8260D
cis-1,2-Dichloroethylene		11.8	1.0	0.28	ug/l	SW846 8260D
trans-1,2-Dichloroethylene		0.38 J	1.0	0.22	ug/l	SW846 8260D
Trichloroethylene		70.9	1.0	0.35	ug/l	SW846 8260D
FA88902-8	**MW-25**					
cis-1,2-Dichloroethylene		2030	50	14	ug/l	SW846 8260D

Summary of Hits

Job Number: FA88902
Account: ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC
Collected: 09/07/21 thru 09/10/21

Lab Sample ID / Client Sample ID / Analyte	Result/ Qual	RL	MDL	Units	Method
Trichloroethylene	5590	100	35	ug/l	SW846 8260D
FA88902-9 MW-26					
cis-1,2-Dichloroethylene	0.31 J	1.0	0.28	ug/l	SW846 8260D
Trichloroethylene	3.7	1.0	0.35	ug/l	SW846 8260D
FA88902-10 MW-27					
cis-1,2-Dichloroethylene	1.7	1.0	0.28	ug/l	SW846 8260D
Trichloroethylene	5.9	1.0	0.35	ug/l	SW846 8260D
FA88902-11 MW-28					
1,1-Dichloroethylene	10.6	5.0	1.6	ug/l	SW846 8260D
cis-1,2-Dichloroethylene	4.1 J	5.0	1.4	ug/l	SW846 8260D
Methylene Chloride	41.8 J	50	20	ug/l	SW846 8260D
Tetrachloroethylene	26.0	5.0	1.1	ug/l	SW846 8260D
Trichloroethylene	525	10	3.5	ug/l	SW846 8260D
FA88902-12 MW-32					
1,1-Dichloroethylene	0.67 J	2.0	0.64	ug/l	SW846 8260D
cis-1,2-Dichloroethylene	108	2.0	0.55	ug/l	SW846 8260D
Trichloroethylene	123	2.0	0.69	ug/l	SW846 8260D
Vinyl Chloride	2.8	2.0	0.82	ug/l	SW846 8260D
FA88902-13 MW-33					
cis-1,2-Dichloroethylene	1.2	1.0	0.28	ug/l	SW846 8260D
FA88902-14 MW-42					
Trichloroethylene	4.1	1.0	0.35	ug/l	SW846 8260D
FA88902-15 MW-45					
1,1-Dichloroethylene	1.3	1.0	0.32	ug/l	SW846 8260D
FA88902-16 MW-52					
cis-1,2-Dichloroethylene	52.7	5.0	1.4	ug/l	SW846 8260D
Tetrachloroethylene	7.1	5.0	1.1	ug/l	SW846 8260D
Trichloroethylene	268	5.0	1.7	ug/l	SW846 8260D

Summary of Hits

Job Number: FA88902
Account: ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC
Collected: 09/07/21 thru 09/10/21

Lab Sample ID / Analyte	Client Sample ID	Result/ Qual	RL	MDL	Units	Method
FA88902-17	**MW-53**					
1,1-Dichloroethylene		9.4	1.0	0.32	ug/l	SW846 8260D
Trichloroethylene		3.7	1.0	0.35	ug/l	SW846 8260D
FA88902-18	**MW-54**					
1,1-Dichloroethylene		22.7 J	25	8.1	ug/l	SW846 8260D
cis-1,2-Dichloroethylene		162	25	6.9	ug/l	SW846 8260D
Tetrachloroethylene		66.9	25	5.4	ug/l	SW846 8260D
Trichloroethylene		1610	25	8.6	ug/l	SW846 8260D
FA88902-19	**DUP-03**					
1,1-Dichloroethylene		22.3	20	6.4	ug/l	SW846 8260D
cis-1,2-Dichloroethylene		158	20	5.5	ug/l	SW846 8260D
Tetrachloroethylene		70.0	20	4.3	ug/l	SW846 8260D
Trichloroethylene		1590	20	6.9	ug/l	SW846 8260D

Sample Results

Report of Analysis

Report of Analysis

Client Sample ID:	LBMW-101		
Lab Sample ID:	FA88902-1	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	2A37789.D	1	09/20/21 16:48	CV	n/a	n/a	V2A1591
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	2.9	5.0	2.0	ug/l	J
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane [a]	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	LBMW-101		
Lab Sample ID:	FA88902-1	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	99%		83-118%
17060-07-0	1,2-Dichloroethane-D4	102%		79-125%
2037-26-5	Toluene-D8	100%		85-112%
460-00-4	4-Bromofluorobenzene	98%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	LBMW-102		
Lab Sample ID:	FA88902-2	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	2A37791.D	1	09/20/21 17:18	CV	n/a	n/a	V2A1591
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	45.2	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	66.2	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane [a]	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	1.7	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	5.7	10	2.0	ug/l	J
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	LBMW-102		
Lab Sample ID:	FA88902-2	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	1.2	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	98%		83-118%
17060-07-0	1,2-Dichloroethane-D4	100%		79-125%
2037-26-5	Toluene-D8	100%		85-112%
460-00-4	4-Bromofluorobenzene	98%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	LBMW-103		
Lab Sample ID:	FA88902-3	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I71011.D	1	09/22/21 10:07	SO	n/a	n/a	VI2314
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	8.6	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	1.1	2.0	0.53	ug/l	J
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	LBMW-103		
Lab Sample ID:	FA88902-3	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	93%		83-118%
17060-07-0	1,2-Dichloroethane-D4	97%		79-125%
2037-26-5	Toluene-D8	92%		85-112%
460-00-4	4-Bromofluorobenzene	93%		83-118%

(a) Associated CCV outside of control limits low.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	LBMW-104		
Lab Sample ID:	FA88902-4	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	2A37793.D	1	09/20/21 17:48	CV	n/a	n/a	V2A1591
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	2.4	5.0	2.0	ug/l	J
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane [a]	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	LBMW-104		
Lab Sample ID:	FA88902-4	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	98%		83-118%
17060-07-0	1,2-Dichloroethane-D4	102%		79-125%
2037-26-5	Toluene-D8	99%		85-112%
460-00-4	4-Bromofluorobenzene	98%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-8		
Lab Sample ID:	FA88902-5	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I71023.D	1	09/22/21 14:56	SO	n/a	n/a	VI2314
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	3.3	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	0.72	1.0	0.32	ug/l	J
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-8		
Lab Sample ID:	FA88902-5	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	0.45	1.0	0.22	ug/l	J
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	2.6	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	94%		83-118%
17060-07-0	1,2-Dichloroethane-D4	100%		79-125%
2037-26-5	Toluene-D8	90%		85-112%
460-00-4	4-Bromofluorobenzene	93%		83-118%

(a) Associated CCV outside of control limits low.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-17		
Lab Sample ID:	FA88902-6	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	1A37944.D	10	09/23/21 14:03	CV	n/a	n/a	V1A1594
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	250	100	ug/l	
71-43-2	Benzene	ND	10	3.1	ug/l	
74-97-5	Bromochloromethane	ND	10	4.5	ug/l	
75-27-4	Bromodichloromethane	ND	10	2.4	ug/l	
75-25-2	Bromoform	ND	10	4.1	ug/l	
78-93-3	2-Butanone (MEK)	ND	50	20	ug/l	
75-15-0	Carbon Disulfide	ND	20	5.3	ug/l	
56-23-5	Carbon Tetrachloride	ND	10	3.6	ug/l	
108-90-7	Chlorobenzene	ND	10	2.0	ug/l	
75-00-3	Chloroethane [a]	ND	20	6.7	ug/l	
67-66-3	Chloroform	ND	10	3.0	ug/l	
110-82-7	Cyclohexane	ND	10	3.9	ug/l	
124-48-1	Dibromochloromethane	ND	10	2.8	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	50	10	ug/l	
106-93-4	1,2-Dibromoethane	ND	20	2.8	ug/l	
75-71-8	Dichlorodifluoromethane	ND	20	5.0	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	10	3.2	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	10	2.2	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	10	2.6	ug/l	
75-34-3	1,1-Dichloroethane	ND	10	3.4	ug/l	
107-06-2	1,2-Dichloroethane	ND	10	3.1	ug/l	
75-35-4	1,1-Dichloroethylene	14.8	10	3.2	ug/l	
156-59-2	cis-1,2-Dichloroethylene	9.3	10	2.8	ug/l	J
156-60-5	trans-1,2-Dichloroethylene	ND	10	2.2	ug/l	
78-87-5	1,2-Dichloropropane	ND	10	4.3	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	10	2.9	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	10	2.1	ug/l	
100-41-4	Ethylbenzene	ND	10	3.6	ug/l	
76-13-1	Freon 113	ND	10	4.8	ug/l	
591-78-6	2-Hexanone	ND	100	20	ug/l	
98-82-8	Isopropylbenzene	ND	10	2.2	ug/l	
79-20-9	Methyl Acetate	ND	200	50	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-17		
Lab Sample ID:	FA88902-6	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	50	20	ug/l	
74-87-3	Methyl Chloride	ND	20	5.0	ug/l	
108-87-2	Methylcyclohexane	ND	10	4.4	ug/l	
75-09-2	Methylene Chloride	ND	50	20	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	50	10	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	10	2.3	ug/l	
100-42-5	Styrene	ND	10	2.2	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	10	3.0	ug/l	
127-18-4	Tetrachloroethylene	31.2	10	2.2	ug/l	
108-88-3	Toluene	ND	10	3.0	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	20	6.1	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	20	5.0	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	10	2.5	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	10	4.7	ug/l	
79-01-6	Trichloroethylene	788	10	3.5	ug/l	
75-69-4	Trichlorofluoromethane	ND	20	5.0	ug/l	
75-01-4	Vinyl Chloride	ND	10	4.1	ug/l	
	m,p-Xylene	ND	20	4.7	ug/l	
95-47-6	o-Xylene	ND	10	2.6	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	97%		83-118%
17060-07-0	1,2-Dichloroethane-D4	101%		79-125%
2037-26-5	Toluene-D8	97%		85-112%
460-00-4	4-Bromofluorobenzene	99%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID: MW-20
Lab Sample ID: FA88902-7
Matrix: AQ - Ground Water
Method: SW846 8260D
Project: FPE; Edgefield, SC

Date Sampled: 09/09/21
Date Received: 09/14/21
Percent Solids: n/a

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I71024.D	1	09/22/21 15:20	SO	n/a	n/a	VI2314
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	3.4	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	11.8	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	0.38	1.0	0.22	ug/l	J
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-20		
Lab Sample ID:	FA88902-7	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	70.9	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	94%		83-118%
17060-07-0	1,2-Dichloroethane-D4	99%		79-125%
2037-26-5	Toluene-D8	92%		85-112%
460-00-4	4-Bromofluorobenzene	92%		83-118%

(a) Associated CCV outside of control limits low.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-25		
Lab Sample ID:	FA88902-8	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I70997.D	50	09/21/21 23:41	SO	n/a	n/a	VI2313
Run #2	I71015.D	100	09/22/21 11:43	SO	n/a	n/a	VI2314

	Purge Volume
Run #1	5.0 ml
Run #2	5.0 ml

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	1300	500	ug/l	
71-43-2	Benzene	ND	50	16	ug/l	
74-97-5	Bromochloromethane	ND	50	23	ug/l	
75-27-4	Bromodichloromethane	ND	50	12	ug/l	
75-25-2	Bromoform	ND	50	20	ug/l	
78-93-3	2-Butanone (MEK)	ND	250	100	ug/l	
75-15-0	Carbon Disulfide [a]	ND	100	27	ug/l	
56-23-5	Carbon Tetrachloride	ND	50	18	ug/l	
108-90-7	Chlorobenzene	ND	50	10	ug/l	
75-00-3	Chloroethane	ND	100	33	ug/l	
67-66-3	Chloroform	ND	50	15	ug/l	
110-82-7	Cyclohexane	ND	50	20	ug/l	
124-48-1	Dibromochloromethane	ND	50	14	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	250	52	ug/l	
106-93-4	1,2-Dibromoethane	ND	100	14	ug/l	
75-71-8	Dichlorodifluoromethane	ND	100	25	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	50	16	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	50	11	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	50	13	ug/l	
75-34-3	1,1-Dichloroethane	ND	50	17	ug/l	
107-06-2	1,2-Dichloroethane	ND	50	16	ug/l	
75-35-4	1,1-Dichloroethylene	ND	50	16	ug/l	
156-59-2	cis-1,2-Dichloroethylene	2030	50	14	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	50	11	ug/l	
78-87-5	1,2-Dichloropropane	ND	50	21	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	50	15	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	50	11	ug/l	
100-41-4	Ethylbenzene	ND	50	18	ug/l	
76-13-1	Freon 113	ND	50	24	ug/l	
591-78-6	2-Hexanone	ND	500	100	ug/l	
98-82-8	Isopropylbenzene	ND	50	11	ug/l	
79-20-9	Methyl Acetate	ND	1000	250	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-25		
Lab Sample ID:	FA88902-8	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	250	100	ug/l	
74-87-3	Methyl Chloride	ND	100	25	ug/l	
108-87-2	Methylcyclohexane	ND	50	22	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	250	50	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	50	11	ug/l	
100-42-5	Styrene	ND	50	11	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	50	15	ug/l	
127-18-4	Tetrachloroethylene [b]	ND	50	11	ug/l	
108-88-3	Toluene	ND	50	15	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	100	31	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	100	25	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	50	12	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	50	23	ug/l	
79-01-6	Trichloroethylene	5590 [c]	100	35	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	100	25	ug/l	
75-01-4	Vinyl Chloride	ND	50	20	ug/l	
	m,p-Xylene	ND	100	23	ug/l	
95-47-6	o-Xylene	ND	50	13	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	93%	93%	83-118%
17060-07-0	1,2-Dichloroethane-D4	97%	97%	79-125%
2037-26-5	Toluene-D8	92%	91%	85-112%
460-00-4	4-Bromofluorobenzene	92%	91%	83-118%

(a) Associated CCV outside of control limits low.
(b) Associated CCV outside of control limits high, sample was ND.
(c) Result is from Run# 2

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-26		
Lab Sample ID:	FA88902-9	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I71025.D	1	09/22/21 15:44	SO	n/a	n/a	VI2314
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	0.31	1.0	0.28	ug/l	J
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-26		
Lab Sample ID:	FA88902-9	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	3.7	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	94%		83-118%
17060-07-0	1,2-Dichloroethane-D4	100%		79-125%
2037-26-5	Toluene-D8	91%		85-112%
460-00-4	4-Bromofluorobenzene	91%		83-118%

(a) Associated CCV outside of control limits low.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID: MW-27
Lab Sample ID: FA88902-10
Matrix: AQ - Ground Water
Method: SW846 8260D
Project: FPE; Edgefield, SC

Date Sampled: 09/09/21
Date Received: 09/14/21
Percent Solids: n/a

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I71026.D	1	09/22/21 16:08	SO	n/a	n/a	VI2314
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	1.7	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-27		
Lab Sample ID:	FA88902-10	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide [a]	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	5.9	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	94%		83-118%
17060-07-0	1,2-Dichloroethane-D4	100%		79-125%
2037-26-5	Toluene-D8	91%		85-112%
460-00-4	4-Bromofluorobenzene	92%		83-118%

(a) Associated CCV outside of control limits low.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-28		
Lab Sample ID:	FA88902-11	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	1A37946.D	5	09/23/21 14:33	CV	n/a	n/a	V1A1594
Run #2	1P81482.D	10	09/24/21 12:25	CV	n/a	n/a	V1P3302

	Purge Volume
Run #1	5.0 ml
Run #2	5.0 ml

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	130	50	ug/l	
71-43-2	Benzene	ND	5.0	1.6	ug/l	
74-97-5	Bromochloromethane	ND	5.0	2.3	ug/l	
75-27-4	Bromodichloromethane	ND	5.0	1.2	ug/l	
75-25-2	Bromoform	ND	5.0	2.0	ug/l	
78-93-3	2-Butanone (MEK)	ND	25	10	ug/l	
75-15-0	Carbon Disulfide	ND	10	2.7	ug/l	
56-23-5	Carbon Tetrachloride	ND	5.0	1.8	ug/l	
108-90-7	Chlorobenzene	ND	5.0	1.0	ug/l	
75-00-3	Chloroethane [a]	ND	10	3.3	ug/l	
67-66-3	Chloroform	ND	5.0	1.5	ug/l	
110-82-7	Cyclohexane	ND	5.0	2.0	ug/l	
124-48-1	Dibromochloromethane	ND	5.0	1.4	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	25	5.2	ug/l	
106-93-4	1,2-Dibromoethane	ND	10	1.4	ug/l	
75-71-8	Dichlorodifluoromethane	ND	10	2.5	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	5.0	1.6	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	5.0	1.1	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	5.0	1.3	ug/l	
75-34-3	1,1-Dichloroethane	ND	5.0	1.7	ug/l	
107-06-2	1,2-Dichloroethane	ND	5.0	1.6	ug/l	
75-35-4	1,1-Dichloroethylene	10.6	5.0	1.6	ug/l	
156-59-2	cis-1,2-Dichloroethylene	4.1	5.0	1.4	ug/l	J
156-60-5	trans-1,2-Dichloroethylene	ND	5.0	1.1	ug/l	
78-87-5	1,2-Dichloropropane	ND	5.0	2.1	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	5.0	1.5	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	5.0	1.1	ug/l	
100-41-4	Ethylbenzene	ND	5.0	1.8	ug/l	
76-13-1	Freon 113	ND	5.0	2.4	ug/l	
591-78-6	2-Hexanone	ND	50	10	ug/l	
98-82-8	Isopropylbenzene	ND	5.0	1.1	ug/l	
79-20-9	Methyl Acetate	ND	100	25	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-28		
Lab Sample ID:	FA88902-11	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	25	10	ug/l	
74-87-3	Methyl Chloride	ND	10	2.5	ug/l	
108-87-2	Methylcyclohexane	ND	5.0	2.2	ug/l	
75-09-2	Methylene Chloride	41.8 [b]	50	20	ug/l	J
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	25	5.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	5.0	1.1	ug/l	
100-42-5	Styrene	ND	5.0	1.1	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	5.0	1.5	ug/l	
127-18-4	Tetrachloroethylene	26.0	5.0	1.1	ug/l	
108-88-3	Toluene	ND	5.0	1.5	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	10	3.1	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	10	2.5	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	5.0	1.2	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	5.0	2.3	ug/l	
79-01-6	Trichloroethylene	525 [b]	10	3.5	ug/l	
75-69-4	Trichlorofluoromethane	ND	10	2.5	ug/l	
75-01-4	Vinyl Chloride	ND	5.0	2.0	ug/l	
	m,p-Xylene	ND	10	2.3	ug/l	
95-47-6	o-Xylene	ND	5.0	1.3	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	96%	102%	83-118%
17060-07-0	1,2-Dichloroethane-D4	100%	109%	79-125%
2037-26-5	Toluene-D8	97%	96%	85-112%
460-00-4	4-Bromofluorobenzene	97%	104%	83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.
(b) Result is from Run# 2

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-32		
Lab Sample ID:	FA88902-12	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	Y58497.D	2	09/23/21 17:28	LV	n/a	n/a	VY2429
Run #2 [a]	Y58469.D	2	09/22/21 20:05	LV	n/a	n/a	VY2428

	Purge Volume
Run #1	5.0 ml
Run #2	5.0 ml

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	50	20	ug/l	
71-43-2	Benzene	ND	2.0	0.62	ug/l	
74-97-5	Bromochloromethane [b]	ND	2.0	0.90	ug/l	
75-27-4	Bromodichloromethane	ND	2.0	0.48	ug/l	
75-25-2	Bromoform	ND	2.0	0.81	ug/l	
78-93-3	2-Butanone (MEK)	ND	10	4.0	ug/l	
75-15-0	Carbon Disulfide	ND	4.0	1.1	ug/l	
56-23-5	Carbon Tetrachloride	ND	2.0	0.71	ug/l	
108-90-7	Chlorobenzene	ND	2.0	0.40	ug/l	
75-00-3	Chloroethane	ND	4.0	1.3	ug/l	
67-66-3	Chloroform	ND	2.0	0.60	ug/l	
110-82-7	Cyclohexane	ND	2.0	0.78	ug/l	
124-48-1	Dibromochloromethane	ND	2.0	0.55	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	10	2.1	ug/l	
106-93-4	1,2-Dibromoethane	ND	4.0	0.55	ug/l	
75-71-8	Dichlorodifluoromethane	ND	4.0	1.0	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	2.0	0.65	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	2.0	0.43	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	2.0	0.51	ug/l	
75-34-3	1,1-Dichloroethane	ND	2.0	0.68	ug/l	
107-06-2	1,2-Dichloroethane	ND	2.0	0.62	ug/l	
75-35-4	1,1-Dichloroethylene	0.67	2.0	0.64	ug/l	J
156-59-2	cis-1,2-Dichloroethylene	108	2.0	0.55	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	2.0	0.44	ug/l	
78-87-5	1,2-Dichloropropane	ND	2.0	0.85	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	2.0	0.58	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	2.0	0.43	ug/l	
100-41-4	Ethylbenzene	ND	2.0	0.71	ug/l	
76-13-1	Freon 113	ND	2.0	0.96	ug/l	
591-78-6	2-Hexanone	ND	20	4.0	ug/l	
98-82-8	Isopropylbenzene	ND	2.0	0.44	ug/l	
79-20-9	Methyl Acetate	ND	40	10	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-32		
Lab Sample ID:	FA88902-12	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	10	4.0	ug/l	
74-87-3	Methyl Chloride	ND	4.0	1.0	ug/l	
108-87-2	Methylcyclohexane	ND	2.0	0.87	ug/l	
75-09-2	Methylene Chloride	ND	10	4.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	10	2.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	2.0	0.46	ug/l	
100-42-5	Styrene	ND	2.0	0.44	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	2.0	0.60	ug/l	
127-18-4	Tetrachloroethylene	ND	2.0	0.43	ug/l	
108-88-3	Toluene	ND	2.0	0.60	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	4.0	1.2	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	4.0	1.0	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	2.0	0.50	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	2.0	0.93	ug/l	
79-01-6	Trichloroethylene	123	2.0	0.69	ug/l	
75-69-4	Trichlorofluoromethane	ND	4.0	1.0	ug/l	
75-01-4	Vinyl Chloride	2.8	2.0	0.82	ug/l	
	m,p-Xylene	ND	4.0	0.93	ug/l	
95-47-6	o-Xylene	ND	2.0	0.51	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	112%	110%	83-118%
17060-07-0	1,2-Dichloroethane-D4	130% [c]	132% [c]	79-125%
2037-26-5	Toluene-D8	99%	103%	85-112%
460-00-4	4-Bromofluorobenzene	102%	101%	83-118%

(a) Confirmation run for surrogate recoveries.
(b) Associated BS recovery outside control limits low.
(c) Outside control limits. Confirmed by reanalysis.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-33		
Lab Sample ID:	FA88902-13	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I70998.D	1	09/22/21 00:05	SO	n/a	n/a	VI2313
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide [a]	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	1.2	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-33		
Lab Sample ID:	FA88902-13	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene [b]	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	93%		83-118%
17060-07-0	1,2-Dichloroethane-D4	98%		79-125%
2037-26-5	Toluene-D8	93%		85-112%
460-00-4	4-Bromofluorobenzene	92%		83-118%

(a) Associated CCV outside of control limits low.
(b) Associated CCV outside of control limits high, sample was ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-42		
Lab Sample ID:	FA88902-14	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I70999.D	1	09/22/21 00:29	SO	n/a	n/a	VI2313
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide [a]	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-42		
Lab Sample ID:	FA88902-14	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene [b]	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	4.1	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	94%		83-118%
17060-07-0	1,2-Dichloroethane-D4	98%		79-125%
2037-26-5	Toluene-D8	92%		85-112%
460-00-4	4-Bromofluorobenzene	92%		83-118%

(a) Associated CCV outside of control limits low.
(b) Associated CCV outside of control limits high, sample was ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-45		
Lab Sample ID:	FA88902-15	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I71000.D	1	09/22/21 00:52	SO	n/a	n/a	VI2313
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide [a]	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	1.3	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-45		
Lab Sample ID:	FA88902-15	**Date Sampled:**	09/08/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene [b]	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	94%		83-118%
17060-07-0	1,2-Dichloroethane-D4	99%		79-125%
2037-26-5	Toluene-D8	92%		85-112%
460-00-4	4-Bromofluorobenzene	92%		83-118%

(a) Associated CCV outside of control limits low.
(b) Associated CCV outside of control limits high, sample was ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-52		
Lab Sample ID:	FA88902-16	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	1A37948.D	5	09/23/21 15:03	CV	n/a	n/a	V1A1594
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	130	50	ug/l	
71-43-2	Benzene	ND	5.0	1.6	ug/l	
74-97-5	Bromochloromethane	ND	5.0	2.3	ug/l	
75-27-4	Bromodichloromethane	ND	5.0	1.2	ug/l	
75-25-2	Bromoform	ND	5.0	2.0	ug/l	
78-93-3	2-Butanone (MEK)	ND	25	10	ug/l	
75-15-0	Carbon Disulfide	ND	10	2.7	ug/l	
56-23-5	Carbon Tetrachloride	ND	5.0	1.8	ug/l	
108-90-7	Chlorobenzene	ND	5.0	1.0	ug/l	
75-00-3	Chloroethane [a]	ND	10	3.3	ug/l	
67-66-3	Chloroform	ND	5.0	1.5	ug/l	
110-82-7	Cyclohexane	ND	5.0	2.0	ug/l	
124-48-1	Dibromochloromethane	ND	5.0	1.4	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	25	5.2	ug/l	
106-93-4	1,2-Dibromoethane	ND	10	1.4	ug/l	
75-71-8	Dichlorodifluoromethane	ND	10	2.5	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	5.0	1.6	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	5.0	1.1	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	5.0	1.3	ug/l	
75-34-3	1,1-Dichloroethane	ND	5.0	1.7	ug/l	
107-06-2	1,2-Dichloroethane	ND	5.0	1.6	ug/l	
75-35-4	1,1-Dichloroethylene	ND	5.0	1.6	ug/l	
156-59-2	cis-1,2-Dichloroethylene	52.7	5.0	1.4	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	5.0	1.1	ug/l	
78-87-5	1,2-Dichloropropane	ND	5.0	2.1	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	5.0	1.5	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	5.0	1.1	ug/l	
100-41-4	Ethylbenzene	ND	5.0	1.8	ug/l	
76-13-1	Freon 113	ND	5.0	2.4	ug/l	
591-78-6	2-Hexanone	ND	50	10	ug/l	
98-82-8	Isopropylbenzene	ND	5.0	1.1	ug/l	
79-20-9	Methyl Acetate	ND	100	25	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-52		
Lab Sample ID:	FA88902-16	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	25	10	ug/l	
74-87-3	Methyl Chloride	ND	10	2.5	ug/l	
108-87-2	Methylcyclohexane	ND	5.0	2.2	ug/l	
75-09-2	Methylene Chloride	ND	25	10	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	25	5.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	5.0	1.1	ug/l	
100-42-5	Styrene	ND	5.0	1.1	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	5.0	1.5	ug/l	
127-18-4	Tetrachloroethylene	7.1	5.0	1.1	ug/l	
108-88-3	Toluene	ND	5.0	1.5	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	10	3.1	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	10	2.5	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	5.0	1.2	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	5.0	2.3	ug/l	
79-01-6	Trichloroethylene	268	5.0	1.7	ug/l	
75-69-4	Trichlorofluoromethane	ND	10	2.5	ug/l	
75-01-4	Vinyl Chloride	ND	5.0	2.0	ug/l	
	m,p-Xylene	ND	10	2.3	ug/l	
95-47-6	o-Xylene	ND	5.0	1.3	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	97%		83-118%
17060-07-0	1,2-Dichloroethane-D4	99%		79-125%
2037-26-5	Toluene-D8	97%		85-112%
460-00-4	4-Bromofluorobenzene	99%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-53		
Lab Sample ID:	FA88902-17	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	1A37950.D	1	09/23/21 15:33	CV	n/a	n/a	V1A1594
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane [a]	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	9.4	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-53		
Lab Sample ID:	FA88902-17	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	3.7	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	97%		83-118%
17060-07-0	1,2-Dichloroethane-D4	98%		79-125%
2037-26-5	Toluene-D8	96%		85-112%
460-00-4	4-Bromofluorobenzene	98%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-54		
Lab Sample ID:	FA88902-18	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	1A37952.D	25	09/23/21 16:03	CV	n/a	n/a	V1A1594
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	630	250	ug/l	
71-43-2	Benzene	ND	25	7.8	ug/l	
74-97-5	Bromochloromethane	ND	25	11	ug/l	
75-27-4	Bromodichloromethane	ND	25	6.1	ug/l	
75-25-2	Bromoform	ND	25	10	ug/l	
78-93-3	2-Butanone (MEK)	ND	130	50	ug/l	
75-15-0	Carbon Disulfide	ND	50	13	ug/l	
56-23-5	Carbon Tetrachloride	ND	25	8.9	ug/l	
108-90-7	Chlorobenzene	ND	25	5.0	ug/l	
75-00-3	Chloroethane [a]	ND	50	17	ug/l	
67-66-3	Chloroform	ND	25	7.5	ug/l	
110-82-7	Cyclohexane	ND	25	9.8	ug/l	
124-48-1	Dibromochloromethane	ND	25	6.9	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	130	26	ug/l	
106-93-4	1,2-Dibromoethane	ND	50	6.9	ug/l	
75-71-8	Dichlorodifluoromethane	ND	50	13	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	25	8.1	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	25	5.4	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	25	6.4	ug/l	
75-34-3	1,1-Dichloroethane	ND	25	8.5	ug/l	
107-06-2	1,2-Dichloroethane	ND	25	7.8	ug/l	
75-35-4	1,1-Dichloroethylene	22.7	25	8.1	ug/l	J
156-59-2	cis-1,2-Dichloroethylene	162	25	6.9	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	25	5.5	ug/l	
78-87-5	1,2-Dichloropropane	ND	25	11	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	25	7.3	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	25	5.4	ug/l	
100-41-4	Ethylbenzene	ND	25	8.9	ug/l	
76-13-1	Freon 113	ND	25	12	ug/l	
591-78-6	2-Hexanone	ND	250	50	ug/l	
98-82-8	Isopropylbenzene	ND	25	5.5	ug/l	
79-20-9	Methyl Acetate	ND	500	130	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	MW-54		
Lab Sample ID:	FA88902-18	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	130	50	ug/l	
74-87-3	Methyl Chloride	ND	50	13	ug/l	
108-87-2	Methylcyclohexane	ND	25	11	ug/l	
75-09-2	Methylene Chloride	ND	130	50	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	130	25	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	25	5.7	ug/l	
100-42-5	Styrene	ND	25	5.6	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	25	7.5	ug/l	
127-18-4	Tetrachloroethylene	66.9	25	5.4	ug/l	
108-88-3	Toluene	ND	25	7.5	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	50	15	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	50	13	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	25	6.2	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	25	12	ug/l	
79-01-6	Trichloroethylene	1610	25	8.6	ug/l	
75-69-4	Trichlorofluoromethane	ND	50	13	ug/l	
75-01-4	Vinyl Chloride	ND	25	10	ug/l	
	m,p-Xylene	ND	50	12	ug/l	
95-47-6	o-Xylene	ND	25	6.4	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	98%		83-118%
17060-07-0	1,2-Dichloroethane-D4	102%		79-125%
2037-26-5	Toluene-D8	97%		85-112%
460-00-4	4-Bromofluorobenzene	100%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	DUP-03		
Lab Sample ID:	FA88902-19	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	1A37954.D	20	09/23/21 16:33	CV	n/a	n/a	V1A1594
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	500	200	ug/l	
71-43-2	Benzene	ND	20	6.2	ug/l	
74-97-5	Bromochloromethane	ND	20	9.0	ug/l	
75-27-4	Bromodichloromethane	ND	20	4.8	ug/l	
75-25-2	Bromoform	ND	20	8.1	ug/l	
78-93-3	2-Butanone (MEK)	ND	100	40	ug/l	
75-15-0	Carbon Disulfide	ND	40	11	ug/l	
56-23-5	Carbon Tetrachloride	ND	20	7.1	ug/l	
108-90-7	Chlorobenzene	ND	20	4.0	ug/l	
75-00-3	Chloroethane [a]	ND	40	13	ug/l	
67-66-3	Chloroform	ND	20	6.0	ug/l	
110-82-7	Cyclohexane	ND	20	7.8	ug/l	
124-48-1	Dibromochloromethane	ND	20	5.5	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	100	21	ug/l	
106-93-4	1,2-Dibromoethane	ND	40	5.5	ug/l	
75-71-8	Dichlorodifluoromethane	ND	40	10	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	20	6.5	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	20	4.3	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	20	5.1	ug/l	
75-34-3	1,1-Dichloroethane	ND	20	6.8	ug/l	
107-06-2	1,2-Dichloroethane	ND	20	6.2	ug/l	
75-35-4	1,1-Dichloroethylene	22.3	20	6.4	ug/l	
156-59-2	cis-1,2-Dichloroethylene	158	20	5.5	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	20	4.4	ug/l	
78-87-5	1,2-Dichloropropane	ND	20	8.5	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	20	5.8	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	20	4.3	ug/l	
100-41-4	Ethylbenzene	ND	20	7.1	ug/l	
76-13-1	Freon 113	ND	20	9.6	ug/l	
591-78-6	2-Hexanone	ND	200	40	ug/l	
98-82-8	Isopropylbenzene	ND	20	4.4	ug/l	
79-20-9	Methyl Acetate	ND	400	100	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	DUP-03		
Lab Sample ID:	FA88902-19	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	100	40	ug/l	
74-87-3	Methyl Chloride	ND	40	10	ug/l	
108-87-2	Methylcyclohexane	ND	20	8.7	ug/l	
75-09-2	Methylene Chloride	ND	100	40	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	100	20	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	20	4.6	ug/l	
100-42-5	Styrene	ND	20	4.4	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	20	6.0	ug/l	
127-18-4	Tetrachloroethylene	70.0	20	4.3	ug/l	
108-88-3	Toluene	ND	20	6.0	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	40	12	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	40	10	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	20	5.0	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	20	9.3	ug/l	
79-01-6	Trichloroethylene	1590	20	6.9	ug/l	
75-69-4	Trichlorofluoromethane	ND	40	10	ug/l	
75-01-4	Vinyl Chloride	ND	20	8.2	ug/l	
	m,p-Xylene	ND	40	9.3	ug/l	
95-47-6	o-Xylene	ND	20	5.1	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	97%		83-118%
17060-07-0	1,2-Dichloroethane-D4	98%		79-125%
2037-26-5	Toluene-D8	98%		85-112%
460-00-4	4-Bromofluorobenzene	99%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Misc. Forms

Custody Documents and Other Forms

Includes the following where applicable:

- Chain of Custody

SGS North America Inc - Orlando
Chain of Custody

FA88902

SGS - ORLANDO JOB # : PAGE 1 OF 2

4405 Vineland Road, Suite C-15 Orlando, Fl 32811
TEL: 407-425-6700 FAX: 407-425-0707
www.sgs.com

SGS - ORLANDO Quote # | SKIFF #

Client / Reporting Information

Company Name: Accadis
Address: 1450 Greene St, Ste 220
City: Augusta State: GA Zip: 30904
Project Contact: Jeff Beckner Email:
Phone #:
Sampler(s) Name(s) (Printed)
Sampler 1: A. Burgess Sampler 2:

Project Information

Project Name: FPE - Edgefield, SC
Street
City Edgefield State SC
Project #
Fax #
Client Purchase Order #

Analytical Information

VOC - 8260B TCL 20

Matrix Codes

DW - Drinking Water
GW - Ground Water
WW - Water
SW - Surface Water
SO - Soil
SL - Sludge
OI - Oil
LIQ - Other Liquid
AIR - Air
SOL - Other Solid

SGS Orlando Sample #	Field ID / Point of Collection	COLLECTION DATE	TIME	SAMPLED BY:	MATRIX	CONTAINER INFORMATION TOTAL # OF BOTTLES	OTHER	NONE	HCl	NaOH	HNO3	H2SO4	NaOH+ZnAc	DI WATER	MEOH	LAB USE ONLY
1	LBMW-101	9-7-21	11:45	AB	GW	3			X							3
2	LBMW-102	9-7-21	13:30			3			X							3
3	LBMW-103	9-8-21	09:55			3			X							3
4	LBMW-104	9-7-21	15:30			3			X							3
5	MW-8	9-9-21	09:04			3			X							3
6	MW-17	9-10-21	09:45			3			X							3
7	MW-20 9-9-21	9-8-21	13:40			3			X							3
8	MW-25	9-8-21	14:30			3			X							3
9	MW-26	9-9-21	12:30			3			X							3
10	MW-27	9-9-21	11:30			3			X							3
11	MW-28	9-10-21	08:50			3			X							3
12	MW-32	9-9-21	10:23	↓	↓	3			X							3

Turnaround Time (Business days)

10 Day (Business) Approved By: / Date:
7 Day
5 Day
3 Day *RUSH*
2 Day *RUSH*
1 Day *RUSH*
Other
Rush T/A Data Available VIA Email or Lablink

Data Deliverable Information

- [ ] COMMERCIAL "A" (RESULTS ONLY)
- [ ] COMMERCIAL "B" (RESULTS PLUS QC)
- [ ] REDT1 (EPA LEVEL 3)
- [ ] FULLT1 (EPA LEVEL 4)
- [ ] EDD'S

Comments / Remarks

INITIAL ASSESSMENT
LABEL VC...

Sample Custody must be documented below each time samples change possession, including courier delivery.

	Relinquished by Sampler/Affiliation	Date Time:	Received By/Affiliation	Relinquished By/Affiliation	Date Time:	Received By/Affiliation
1		9-13-21	2	3	9/14/21	4
	Relinquished by/Affiliation	Date Time:	Received By/Affiliation	Relinquished By/Affiliation	Date Time:	Received By/Affiliation
5			6	7	1000	8

Lab Use Only : Cooler Temperature (s) Celsius (corrected): 0.8 IR1

http://www.sgs.com/en/terms-and-conditions

ORLD-SMT-0001-03-FORM-COC (4).xls Rev 031318

SGS

CHAIN OF CUSTODY

FA88902 Page __ of __

SGS North America Inc. - Dayton
2235 Route 130, Dayton, NJ 08810
TEL. 732-329-0200 FAX: 732-329-3499/3480
www.sgs.com/ehsusa

FED-EX Tracking # | Bottle Order Control #
SGS Quote # | SGS Job #

Client / Reporting Information

Company Name: Arcadis
Street Address:
City / State / Zip:
Project Contact / E-mail: Jeff Beckner
Phone #:
Sampler(s) Name(s): A. Burgess Phone #:

Project Information

Project Name: FPE - Edgefield, SC
Street:
City / State:
Project #:
Client Purchase Order #:
Project Manager:

Billing Information (if different from Report to)

Company Name:
Street Address:
City / State / Zip:
Attention:

Requested Analysis

8260B - VOCs - WW WW WW WW WW

Matrix Codes

DW - Drinking Water
GW - Ground Water
WW - Water
SW - Surface Water
SO - Soil
SL - Sludge
SED-Sediment
OI - Oil
LIQ - Other Liquid
AIR - Air
SOL - Other Solid
WP - Wipe
FB - Field Blank
EB-Equipment Blank
RB - Rinse Blank
TB - Trip Blank

SGS Sample #	Field ID / Point of Collection	MEOH/DI Vial #	Collection Date	Collection Time	Sampled by	Grab (G) Comp (C)	Matrix	# of bottles	Number of preserved Bottles: HCl	NaOH	HNO3	H2SO4	NONE	DI Water	MEOH	ENCORE	LAB USE ONLY
13	MW-33		9-8-21	13:32	AB	G	GW	3	X								
14	MW-42		9-8-21	12:18				3	X								
15	MW-45		9-8-21	11:04				3	X								
16	MW-52		9-10-21	11:32				3	X								
17	MW-53		9-10-21	14:05				3	X								
18	MW-54		9-10-21	10:36				3	X								
19	DUP-03		9-10-21	—				3	X								

Turn Around Time (Business Days)

Approved By (SGS PM): / Date:

- [ ] 10 Business Days
- [ ] 5 Business Days
- [ ] 3 Business Days*
- [ ] 2 Business Days*
- [ ] 1 Business Day*
- [ ] Other

All data available via Lablink
*Approval needed for 1-3 Business Day TAT

Deliverable

- [ ] Commercial "A" (Level 1)
- [ ] Commercial "B" (Level 2)
- [ ] NJ Reduced (Level 3)
- [ ] Full Tier I (Level 4)
- [ ] Commercial "C"
- [ ] NJ DKQP
- [ ] NYASP Category A
- [ ] NYASP Category B
- [ ] MA MCP Criteria_____
- [ ] CT RCP Criteria_____
- [ ] State Forms
- [ ] EDD Format _____
- [ ] DOD-QSM5

Commercial "A" = Results only; Commercial "B" = Results + QC Summary
Commercial "C" = Results + QC Summary + Partial Raw data

Comments / Special Instructions

http://www.sgs.com/en/terms-and-conditions

Sample Custody must be documented below each time samples change possession, including courier delivery.

	Relinquished by:	Date / Time:	Received By:	Relinquished By:	Date / Time:	Received By:
1		9-13-21	1 FX	2 FX	9/14/21 1000	2
3			3	4		4
5			5	Custody Seal #	Intact / Not Intact	Preserved where applicable / Absent	On Ice	Cooler Temp. °C

Therm. ID:

EHSA-QAC-0023-02-FORM-Dayton - Standard COC.xlsx

FA88902: Chain of Custody
Page 2 of 3

SGS Sample Receipt Summary

Job Number: FA88902 **Client:** ARCADIS **Project:** FPE-EDGEFIELD

Date / Time Received: 9/14/2021 10:00:00 AM **Delivery Method:** FX **Airbill #'s:** 5061 4510 5417

Therm ID: IR 1; **Therm CF:** 0.2; **# of Coolers:** 1

Cooler Temps (Raw Measured) °C: Cooler 1: (0.6);

Cooler Temps (Corrected) °C: Cooler 1: (0.8);

Cooler Information	Y	or	N
1. Custody Seals Present	☑		☐
2. Custody Seals Intact	☑		☐
3. Temp criteria achieved	☑		☐
4. Cooler temp verification	IR Gun		
5. Cooler media	Ice (Bag)		

Trip Blank Information	Y	or	N	N/A
1. Trip Blank present / cooler	☑		☐	☐
2. Trip Blank listed on COC	☑		☐	☐

	W	or	S	N/A
3. Type Of TB Received	☑		☐	☐

Sample Information	Y	or	N	N/A
1. Sample labels present on bottles	☑		☐	
2. Samples preserved properly	☑		☐	
3. Sufficient volume/containers recvd for analysis:	☑		☐	
4. Condition of sample	Intact			
5. Sample recvd within HT	☑		☐	
6. Dates/Times/IDs on COC match Sample Label	☑		☐	
7. VOCs have headspace	☐		☑	☐
8. Bottles received for unspecified tests	☐		☑	
9. Compositing instructions clear	☐		☐	☑
10. Voa Soil Kits/Jars received past 48hrs?	☐		☐	☑
11. % Solids Jar received?	☐		☐	☑
12. Residual Chlorine Present?	☐		☐	☑

Misc. Information

Number of Encores: 25-Gram _____ 5-Gram _____ Number of 5035 Field Kits: _____ Number of Lab Filtered Metals: _____

Test Strip Lot #s: pH 0-3 230315 pH 10-12 219813A Other: (Specify) _____ _____

Residual Chlorine Test Strip Lot #: _____

Comments

SM001
Rev. Date 05/24/17

Technician: PETERH Date: 9/14/2021 10:00:00 A Reviewer: _____ Date: _____

FA88902: Chain of Custody
Page 3 of 3

The results set forth herein are provided by SGS North America Inc.

e-Hardcopy 2.0
Automated Report

Technical Report for

ARCADIS Geraghty & Miller

FPE; Edgefield, SC

30067293.2.2

SGS Job Number: FA88903

Sampling Dates: 09/07/21 - 09/10/21

Report to:

ARCADIS Geraghty & Miller

jbeckner@arcadis-us.com

ATTN: Jeff Beckner

Total number of pages in report: 44

Test results contained within this data package meet the requirements of the National Environmental Laboratory Accreditation Program and/or state specific certification programs as applicable.

Norm Farmer
Technical Director

Client Service contact: Evita Martinez 407-425-6700

Certifications: FL(E83510), LA(03051), KS(E-10327), NC(573), NJ(FL002), NY(12022), SC(96038001) DoD ELAP(ANAB L2229), AZ(AZ0806), CA(2937), TX(T104704404), PA(68-03573), VA(460177), AL, AK, AR, CT, IA, KY, MA, MI. MS, ND, NH, NV, OK, OR, UT, VT, WA, WV

Sections: 1 2 3 4

Table of Contents

Sample Summary

ARCADIS Geraghty & Miller

Job No: FA88903

FPE; Edgefield, SC
Project No: 30067293.2.2

Sample Number	Collected Date	Time	By	Received	Matrix Code	Type	Client Sample ID
This report contains results reported as ND = Not detected. The following applies: Organics ND = Not detected above the MDL							
FA88903-1	09/07/21	11:15	RR	09/14/21	AQ	Ground Water	PSMW-6
FA88903-2	09/07/21	14:10	RR	09/14/21	AQ	Ground Water	PSMW-7
FA88903-3	09/07/21	14:50	RR	09/14/21	AQ	Ground Water	PSMW-2
FA88903-4	09/09/21	08:25	RR	09/14/21	AQ	Ground Water	PMW-2
FA88903-5	09/09/21	09:10	RR	09/14/21	AQ	Ground Water	PSMW-3
FA88903-6	09/09/21	00:00	RR	09/14/21	AQ	Ground Water	DUP-1
FA88903-7	09/09/21	10:55	RR	09/14/21	AQ	Ground Water	PSMW-4
FA88903-8	09/09/21	12:35	RR	09/14/21	AQ	Ground Water	PMW-4
FA88903-9	09/09/21	14:50	RR	09/14/21	AQ	Ground Water	PMW-5
FA88903-10	09/09/21	16:25	RR	09/14/21	AQ	Ground Water	PMW-3
FA88903-11	09/10/21	08:10	RR	09/14/21	AQ	Ground Water	AMW-5
FA88903-12	09/10/21	10:05	RR	09/14/21	AQ	Ground Water	RTB-6

Sample Summary
(continued)

ARCADIS Geraghty & Miller

Job No: FA88903

FPE; Edgefield, SC
Project No: 30067293.2.2

Sample Number	Collected Date	Time	By	Received	Matrix Code	Type	Client Sample ID
FA88903-13	09/10/21	10:35	RR	09/14/21	AQ	Ground Water	PSMW-5
FA88903-14	09/10/21	12:25	RR	09/14/21	AQ	Ground Water	AMW-1
FA88903-15	09/10/21	13:05	RR	09/14/21	AQ	Ground Water	AMW-2
FA88903-16	09/10/21	14:00	RR	09/14/21	AQ	Ground Water	AMW-3
FA88903-17	09/10/21	00:00	RR	09/14/21	AQ	Trip Blank Water	TRIP BLANK

Summary of Hits

Job Number: FA88903
Account: ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC
Collected: 09/07/21 thru 09/10/21

Lab Sample ID / Analyte	Client Sample ID	Result/ Qual	RL	MDL	Units	Method
FA88903-1	**PSMW-6**					
No hits reported in this sample.						
FA88903-2	**PSMW-7**					
No hits reported in this sample.						
FA88903-3	**PSMW-2**					
No hits reported in this sample.						
FA88903-4	**PMW-2**					
No hits reported in this sample.						
FA88903-5	**PSMW-3**					
cis-1,2-Dichloroethylene		0.64 J	1.0	0.28	ug/l	SW846 8260D
Trichloroethylene		4.6	1.0	0.35	ug/l	SW846 8260D
FA88903-6	**DUP-1**					
cis-1,2-Dichloroethylene		0.95 J	1.0	0.28	ug/l	SW846 8260D
Trichloroethylene		5.3	1.0	0.35	ug/l	SW846 8260D
FA88903-7	**PSMW-4**					
Chloroform		0.41 J	1.0	0.30	ug/l	SW846 8260D
cis-1,2-Dichloroethylene		0.45 J	1.0	0.28	ug/l	SW846 8260D
Trichloroethylene		7.8	1.0	0.35	ug/l	SW846 8260D
FA88903-8	**PMW-4**					
cis-1,2-Dichloroethylene		23.3	1.0	0.28	ug/l	SW846 8260D
Trichloroethylene		78.1	1.0	0.35	ug/l	SW846 8260D
FA88903-9	**PMW-5**					
cis-1,2-Dichloroethylene		0.50 J	1.0	0.28	ug/l	SW846 8260D
Trichloroethylene		2.5	1.0	0.35	ug/l	SW846 8260D
FA88903-10	**PMW-3**					
cis-1,2-Dichloroethylene		0.53 J	1.0	0.28	ug/l	SW846 8260D

Summary of Hits

Job Number: FA88903
Account: ARCADIS Geraghty & Miller
Project: FPE; Edgefield, SC
Collected: 09/07/21 thru 09/10/21

Lab Sample ID / Analyte	Client Sample ID	Result/ Qual	RL	MDL	Units	Method
Trichloroethylene		24.3	1.0	0.35	ug/l	SW846 8260D
FA88903-11	**AMW-5**					
1,1-Dichloroethane		4.1	1.0	0.34	ug/l	SW846 8260D
1,1-Dichloroethylene		7.2	1.0	0.32	ug/l	SW846 8260D
cis-1,2-Dichloroethylene		7.1	1.0	0.28	ug/l	SW846 8260D
Trichloroethylene		63.0	1.0	0.35	ug/l	SW846 8260D
Vinyl Chloride		0.56 J	1.0	0.41	ug/l	SW846 8260D
FA88903-12	**RTB-6**					
1,1-Dichloroethylene		11.4 J	25	8.1	ug/l	SW846 8260D
cis-1,2-Dichloroethylene		219	25	6.9	ug/l	SW846 8260D
Trichloroethylene		1730	25	8.6	ug/l	SW846 8260D
Vinyl Chloride		29.6	25	10	ug/l	SW846 8260D
FA88903-13	**PSMW-5**					
cis-1,2-Dichloroethylene		122	10	2.8	ug/l	SW846 8260D
Trichloroethylene		729	10	3.5	ug/l	SW846 8260D
FA88903-14	**AMW-1**					
cis-1,2-Dichloroethylene		7.3	1.0	0.28	ug/l	SW846 8260D
Trichloroethylene		23.4	1.0	0.35	ug/l	SW846 8260D
FA88903-15	**AMW-2**					
cis-1,2-Dichloroethylene		6.5	1.0	0.28	ug/l	SW846 8260D
Trichloroethylene		18.0	1.0	0.35	ug/l	SW846 8260D
FA88903-16	**AMW-3**					
1,1-Dichloroethylene		1.2 J	2.5	0.81	ug/l	SW846 8260D
cis-1,2-Dichloroethylene		35.5	2.5	0.69	ug/l	SW846 8260D
Trichloroethylene		196	2.5	0.86	ug/l	SW846 8260D
FA88903-17	**TRIP BLANK**					

No hits reported in this sample.

Sample Results

Report of Analysis

Report of Analysis

Client Sample ID:	PSMW-6		
Lab Sample ID:	FA88903-1	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	2A37795.D	1	09/20/21 18:18	CV	n/a	n/a	V2A1591
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane [a]	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	PSMW-6		
Lab Sample ID:	FA88903-1	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	97%		83-118%
17060-07-0	1,2-Dichloroethane-D4	98%		79-125%
2037-26-5	Toluene-D8	101%		85-112%
460-00-4	4-Bromofluorobenzene	98%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	PSMW-7		
Lab Sample ID:	FA88903-2	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	2A37797.D	1	09/20/21 18:48	CV	n/a	n/a	V2A1591
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane [a]	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	PSMW-7		
Lab Sample ID:	FA88903-2	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	97%		83-118%
17060-07-0	1,2-Dichloroethane-D4	100%		79-125%
2037-26-5	Toluene-D8	100%		85-112%
460-00-4	4-Bromofluorobenzene	98%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	PSMW-2		
Lab Sample ID:	FA88903-3	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	2A37799.D	1	09/20/21 19:18	CV	n/a	n/a	V2A1591
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane [a]	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	PSMW-2		
Lab Sample ID:	FA88903-3	**Date Sampled:**	09/07/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	97%		83-118%
17060-07-0	1,2-Dichloroethane-D4	98%		79-125%
2037-26-5	Toluene-D8	101%		85-112%
460-00-4	4-Bromofluorobenzene	99%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	PMW-2		
Lab Sample ID:	FA88903-4	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1 [a]	Y58462.D	1	09/22/21 17:10	LV	n/a	n/a	VY2428
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	Units	Q

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	108%		83-118%
17060-07-0	1,2-Dichloroethane-D4	127% [b]		79-125%
2037-26-5	Toluene-D8	102%		85-112%
460-00-4	4-Bromofluorobenzene	101%		83-118%

(a) Confirmation run.
(b) Outside control limits.

ND = Not detected
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	PSMW-3		
Lab Sample ID:	FA88903-5	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	Y58491.D	1	09/23/21 14:59	LV	n/a	n/a	VY2429
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane [a]	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	0.64	1.0	0.28	ug/l	J
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	PSMW-3		
Lab Sample ID:	FA88903-5	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	4.6	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	101%		83-118%
17060-07-0	1,2-Dichloroethane-D4	107%		79-125%
2037-26-5	Toluene-D8	102%		85-112%
460-00-4	4-Bromofluorobenzene	103%		83-118%

(a) Associated BS recovery outside control limits low.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	DUP-1		
Lab Sample ID:	FA88903-6	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	Y58492.D	1	09/23/21 15:24	LV	n/a	n/a	VY2429
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane [a]	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	0.95	1.0	0.28	ug/l	J
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	DUP-1		
Lab Sample ID:	FA88903-6	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	5.3	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	103%		83-118%
17060-07-0	1,2-Dichloroethane-D4	111%		79-125%
2037-26-5	Toluene-D8	102%		85-112%
460-00-4	4-Bromofluorobenzene	104%		83-118%

(a) Associated BS recovery outside control limits low.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	PSMW-4		
Lab Sample ID:	FA88903-7	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	Y58493.D	1	09/23/21 15:49	LV	n/a	n/a	VY2429
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane [a]	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	0.41	1.0	0.30	ug/l	J
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	0.45	1.0	0.28	ug/l	J
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	PSMW-4		
Lab Sample ID:	FA88903-7	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	7.8	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	103%		83-118%
17060-07-0	1,2-Dichloroethane-D4	116%		79-125%
2037-26-5	Toluene-D8	102%		85-112%
460-00-4	4-Bromofluorobenzene	104%		83-118%

(a) Associated BS recovery outside control limits low.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	PMW-4		
Lab Sample ID:	FA88903-8	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	Y58494.D	1	09/23/21 16:14	LV	n/a	n/a	VY2429
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane [a]	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	23.3	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	PMW-4		
Lab Sample ID:	FA88903-8	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	78.1	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	105%		83-118%
17060-07-0	1,2-Dichloroethane-D4	121%		79-125%
2037-26-5	Toluene-D8	101%		85-112%
460-00-4	4-Bromofluorobenzene	103%		83-118%

(a) Associated BS recovery outside control limits low.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	PMW-5		
Lab Sample ID:	FA88903-9	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	Y58495.D	1	09/23/21 16:38	LV	n/a	n/a	VY2429
Run #2 [a]	Y58467.D	1	09/22/21 19:15	LV	n/a	n/a	VY2428

	Purge Volume
Run #1	5.0 ml
Run #2	5.0 ml

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane [b]	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	0.50	1.0	0.28	ug/l	J
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	PMW-5		
Lab Sample ID:	FA88903-9	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	2.5	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	109%	113%	83-118%
17060-07-0	1,2-Dichloroethane-D4	127% [c]	132% [c]	79-125%
2037-26-5	Toluene-D8	102%	101%	85-112%
460-00-4	4-Bromofluorobenzene	101%	103%	83-118%

(a) Confirmation run for surrogate recoveries.
(b) Associated BS recovery outside control limits low.
(c) Outside control limits. Confirmed by reanalysis.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	PMW-3		
Lab Sample ID:	FA88903-10	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	Y58496.D	1	09/23/21 17:03	LV	n/a	n/a	VY2429
Run #2 [a]	Y58468.D	1	09/22/21 19:40	LV	n/a	n/a	VY2428

	Purge Volume
Run #1	5.0 ml
Run #2	5.0 ml

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane [b]	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	0.53	1.0	0.28	ug/l	J
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	PMW-3		
Lab Sample ID:	FA88903-10	**Date Sampled:**	09/09/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	24.3	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	108%	109%	83-118%
17060-07-0	1,2-Dichloroethane-D4	130% [c]	132% [c]	79-125%
2037-26-5	Toluene-D8	100%	102%	85-112%
460-00-4	4-Bromofluorobenzene	105%	102%	83-118%

(a) Confirmation run for surrogate recoveries.
(b) Associated BS recovery outside control limits low.
(c) Outside control limits. Confirmed by reanalysis.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	AMW-5		
Lab Sample ID:	FA88903-11	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	1A37956.D	1	09/23/21 17:03	CV	n/a	n/a	V1A1594
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane [a]	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	4.1	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	7.2	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	7.1	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	AMW-5		
Lab Sample ID:	FA88903-11	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	63.0	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	0.56	1.0	0.41	ug/l	J
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	98%		83-118%
17060-07-0	1,2-Dichloroethane-D4	100%		79-125%
2037-26-5	Toluene-D8	97%		85-112%
460-00-4	4-Bromofluorobenzene	99%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	RTB-6		
Lab Sample ID:	FA88903-12	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	1A37958.D	25	09/23/21 17:33	CV	n/a	n/a	V1A1594
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	630	250	ug/l	
71-43-2	Benzene	ND	25	7.8	ug/l	
74-97-5	Bromochloromethane	ND	25	11	ug/l	
75-27-4	Bromodichloromethane	ND	25	6.1	ug/l	
75-25-2	Bromoform	ND	25	10	ug/l	
78-93-3	2-Butanone (MEK)	ND	130	50	ug/l	
75-15-0	Carbon Disulfide	ND	50	13	ug/l	
56-23-5	Carbon Tetrachloride	ND	25	8.9	ug/l	
108-90-7	Chlorobenzene	ND	25	5.0	ug/l	
75-00-3	Chloroethane [a]	ND	50	17	ug/l	
67-66-3	Chloroform	ND	25	7.5	ug/l	
110-82-7	Cyclohexane	ND	25	9.8	ug/l	
124-48-1	Dibromochloromethane	ND	25	6.9	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	130	26	ug/l	
106-93-4	1,2-Dibromoethane	ND	50	6.9	ug/l	
75-71-8	Dichlorodifluoromethane	ND	50	13	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	25	8.1	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	25	5.4	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	25	6.4	ug/l	
75-34-3	1,1-Dichloroethane	ND	25	8.5	ug/l	
107-06-2	1,2-Dichloroethane	ND	25	7.8	ug/l	
75-35-4	1,1-Dichloroethylene	11.4	25	8.1	ug/l	J
156-59-2	cis-1,2-Dichloroethylene	219	25	6.9	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	25	5.5	ug/l	
78-87-5	1,2-Dichloropropane	ND	25	11	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	25	7.3	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	25	5.4	ug/l	
100-41-4	Ethylbenzene	ND	25	8.9	ug/l	
76-13-1	Freon 113	ND	25	12	ug/l	
591-78-6	2-Hexanone	ND	250	50	ug/l	
98-82-8	Isopropylbenzene	ND	25	5.5	ug/l	
79-20-9	Methyl Acetate	ND	500	130	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	RTB-6		
Lab Sample ID:	FA88903-12	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	130	50	ug/l	
74-87-3	Methyl Chloride	ND	50	13	ug/l	
108-87-2	Methylcyclohexane	ND	25	11	ug/l	
75-09-2	Methylene Chloride	ND	130	50	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	130	25	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	25	5.7	ug/l	
100-42-5	Styrene	ND	25	5.6	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	25	7.5	ug/l	
127-18-4	Tetrachloroethylene	ND	25	5.4	ug/l	
108-88-3	Toluene	ND	25	7.5	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	50	15	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	50	13	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	25	6.2	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	25	12	ug/l	
79-01-6	Trichloroethylene	1730	25	8.6	ug/l	
75-69-4	Trichlorofluoromethane	ND	50	13	ug/l	
75-01-4	Vinyl Chloride	29.6	25	10	ug/l	
	m,p-Xylene	ND	50	12	ug/l	
95-47-6	o-Xylene	ND	25	6.4	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	97%		83-118%
17060-07-0	1,2-Dichloroethane-D4	99%		79-125%
2037-26-5	Toluene-D8	97%		85-112%
460-00-4	4-Bromofluorobenzene	98%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	PSMW-5		
Lab Sample ID:	FA88903-13	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	1A37960.D	10	09/23/21 18:02	CV	n/a	n/a	V1A1594
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	250	100	ug/l	
71-43-2	Benzene	ND	10	3.1	ug/l	
74-97-5	Bromochloromethane	ND	10	4.5	ug/l	
75-27-4	Bromodichloromethane	ND	10	2.4	ug/l	
75-25-2	Bromoform	ND	10	4.1	ug/l	
78-93-3	2-Butanone (MEK)	ND	50	20	ug/l	
75-15-0	Carbon Disulfide	ND	20	5.3	ug/l	
56-23-5	Carbon Tetrachloride	ND	10	3.6	ug/l	
108-90-7	Chlorobenzene	ND	10	2.0	ug/l	
75-00-3	Chloroethane [a]	ND	20	6.7	ug/l	
67-66-3	Chloroform	ND	10	3.0	ug/l	
110-82-7	Cyclohexane	ND	10	3.9	ug/l	
124-48-1	Dibromochloromethane	ND	10	2.8	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	50	10	ug/l	
106-93-4	1,2-Dibromoethane	ND	20	2.8	ug/l	
75-71-8	Dichlorodifluoromethane	ND	20	5.0	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	10	3.2	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	10	2.2	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	10	2.6	ug/l	
75-34-3	1,1-Dichloroethane	ND	10	3.4	ug/l	
107-06-2	1,2-Dichloroethane	ND	10	3.1	ug/l	
75-35-4	1,1-Dichloroethylene	ND	10	3.2	ug/l	
156-59-2	cis-1,2-Dichloroethylene	122	10	2.8	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	10	2.2	ug/l	
78-87-5	1,2-Dichloropropane	ND	10	4.3	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	10	2.9	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	10	2.1	ug/l	
100-41-4	Ethylbenzene	ND	10	3.6	ug/l	
76-13-1	Freon 113	ND	10	4.8	ug/l	
591-78-6	2-Hexanone	ND	100	20	ug/l	
98-82-8	Isopropylbenzene	ND	10	2.2	ug/l	
79-20-9	Methyl Acetate	ND	200	50	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	PSMW-5		
Lab Sample ID:	FA88903-13	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	50	20	ug/l	
74-87-3	Methyl Chloride	ND	20	5.0	ug/l	
108-87-2	Methylcyclohexane	ND	10	4.4	ug/l	
75-09-2	Methylene Chloride	ND	50	20	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	50	10	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	10	2.3	ug/l	
100-42-5	Styrene	ND	10	2.2	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	10	3.0	ug/l	
127-18-4	Tetrachloroethylene	ND	10	2.2	ug/l	
108-88-3	Toluene	ND	10	3.0	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	20	6.1	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	20	5.0	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	10	2.5	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	10	4.7	ug/l	
79-01-6	Trichloroethylene	729	10	3.5	ug/l	
75-69-4	Trichlorofluoromethane	ND	20	5.0	ug/l	
75-01-4	Vinyl Chloride	ND	10	4.1	ug/l	
	m,p-Xylene	ND	20	4.7	ug/l	
95-47-6	o-Xylene	ND	10	2.6	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	97%		83-118%
17060-07-0	1,2-Dichloroethane-D4	100%		79-125%
2037-26-5	Toluene-D8	96%		85-112%
460-00-4	4-Bromofluorobenzene	98%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	AMW-1		
Lab Sample ID:	FA88903-14	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	1A37962.D	1	09/23/21 18:32	CV	n/a	n/a	V1A1594
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane [a]	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	7.3	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	AMW-1		
Lab Sample ID:	FA88903-14	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	23.4	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	97%		83-118%
17060-07-0	1,2-Dichloroethane-D4	100%		79-125%
2037-26-5	Toluene-D8	97%		85-112%
460-00-4	4-Bromofluorobenzene	99%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	AMW-2		
Lab Sample ID:	FA88903-15	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	1A37964.D	1	09/23/21 19:02	CV	n/a	n/a	V1A1594
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane [a]	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	6.5	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	AMW-2		
Lab Sample ID:	FA88903-15	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	18.0	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	96%		83-118%
17060-07-0	1,2-Dichloroethane-D4	97%		79-125%
2037-26-5	Toluene-D8	98%		85-112%
460-00-4	4-Bromofluorobenzene	101%		83-118%

(a) Associated Initial Calibration outside control limits (%RSD > 15%); however sample is ND.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	AMW-3		
Lab Sample ID:	FA88903-16	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I71068.D	2.5	09/24/21 11:16	SO	n/a	n/a	VI2319
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	63	25	ug/l	
71-43-2	Benzene	ND	2.5	0.78	ug/l	
74-97-5	Bromochloromethane	ND	2.5	1.1	ug/l	
75-27-4	Bromodichloromethane	ND	2.5	0.61	ug/l	
75-25-2	Bromoform	ND	2.5	1.0	ug/l	
78-93-3	2-Butanone (MEK)	ND	13	5.0	ug/l	
75-15-0	Carbon Disulfide	ND	5.0	1.3	ug/l	
56-23-5	Carbon Tetrachloride	ND	2.5	0.89	ug/l	
108-90-7	Chlorobenzene	ND	2.5	0.50	ug/l	
75-00-3	Chloroethane	ND	5.0	1.7	ug/l	
67-66-3	Chloroform	ND	2.5	0.75	ug/l	
110-82-7	Cyclohexane	ND	2.5	0.98	ug/l	
124-48-1	Dibromochloromethane	ND	2.5	0.69	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	13	2.6	ug/l	
106-93-4	1,2-Dibromoethane	ND	5.0	0.69	ug/l	
75-71-8	Dichlorodifluoromethane	ND	5.0	1.3	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	2.5	0.81	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	2.5	0.54	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	2.5	0.64	ug/l	
75-34-3	1,1-Dichloroethane	ND	2.5	0.85	ug/l	
107-06-2	1,2-Dichloroethane	ND	2.5	0.78	ug/l	
75-35-4	1,1-Dichloroethylene	1.2	2.5	0.81	ug/l	J
156-59-2	cis-1,2-Dichloroethylene	35.5	2.5	0.69	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	2.5	0.55	ug/l	
78-87-5	1,2-Dichloropropane	ND	2.5	1.1	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	2.5	0.73	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	2.5	0.54	ug/l	
100-41-4	Ethylbenzene	ND	2.5	0.89	ug/l	
76-13-1	Freon 113	ND	2.5	1.2	ug/l	
591-78-6	2-Hexanone	ND	25	5.0	ug/l	
98-82-8	Isopropylbenzene	ND	2.5	0.55	ug/l	
79-20-9	Methyl Acetate	ND	50	13	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range

J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	AMW-3		
Lab Sample ID:	FA88903-16	**Date Sampled:**	09/10/21
Matrix:	AQ - Ground Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	13	5.0	ug/l	
74-87-3	Methyl Chloride	ND	5.0	1.3	ug/l	
108-87-2	Methylcyclohexane	ND	2.5	1.1	ug/l	
75-09-2	Methylene Chloride	ND	13	5.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	13	2.5	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	2.5	0.57	ug/l	
100-42-5	Styrene	ND	2.5	0.56	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	2.5	0.75	ug/l	
127-18-4	Tetrachloroethylene	ND	2.5	0.54	ug/l	
108-88-3	Toluene	ND	2.5	0.75	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	5.0	1.5	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	5.0	1.3	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	2.5	0.62	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	2.5	1.2	ug/l	
79-01-6	Trichloroethylene	196	2.5	0.86	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	5.0	1.3	ug/l	
75-01-4	Vinyl Chloride	ND	2.5	1.0	ug/l	
	m,p-Xylene	ND	5.0	1.2	ug/l	
95-47-6	o-Xylene	ND	2.5	0.64	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	94%		83-118%
17060-07-0	1,2-Dichloroethane-D4	98%		79-125%
2037-26-5	Toluene-D8	92%		85-112%
460-00-4	4-Bromofluorobenzene	92%		83-118%

(a) Associated CCV outside of control limits high.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	TRIP BLANK		
Lab Sample ID:	FA88903-17	**Date Sampled:**	09/10/21
Matrix:	AQ - Trip Blank Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

	File ID	DF	Analyzed	By	Prep Date	Prep Batch	Analytical Batch
Run #1	I71064.D	1	09/24/21 09:40	SO	n/a	n/a	VI2319
Run #2							

	Purge Volume
Run #1	5.0 ml
Run #2	

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
67-64-1	Acetone	ND	25	10	ug/l	
71-43-2	Benzene	ND	1.0	0.31	ug/l	
74-97-5	Bromochloromethane	ND	1.0	0.45	ug/l	
75-27-4	Bromodichloromethane	ND	1.0	0.24	ug/l	
75-25-2	Bromoform	ND	1.0	0.41	ug/l	
78-93-3	2-Butanone (MEK)	ND	5.0	2.0	ug/l	
75-15-0	Carbon Disulfide	ND	2.0	0.53	ug/l	
56-23-5	Carbon Tetrachloride	ND	1.0	0.36	ug/l	
108-90-7	Chlorobenzene	ND	1.0	0.20	ug/l	
75-00-3	Chloroethane	ND	2.0	0.67	ug/l	
67-66-3	Chloroform	ND	1.0	0.30	ug/l	
110-82-7	Cyclohexane	ND	1.0	0.39	ug/l	
124-48-1	Dibromochloromethane	ND	1.0	0.28	ug/l	
96-12-8	1,2-Dibromo-3-chloropropane	ND	5.0	1.0	ug/l	
106-93-4	1,2-Dibromoethane	ND	2.0	0.28	ug/l	
75-71-8	Dichlorodifluoromethane	ND	2.0	0.50	ug/l	
95-50-1	1,2-Dichlorobenzene	ND	1.0	0.32	ug/l	
541-73-1	1,3-Dichlorobenzene	ND	1.0	0.22	ug/l	
106-46-7	1,4-Dichlorobenzene	ND	1.0	0.26	ug/l	
75-34-3	1,1-Dichloroethane	ND	1.0	0.34	ug/l	
107-06-2	1,2-Dichloroethane	ND	1.0	0.31	ug/l	
75-35-4	1,1-Dichloroethylene	ND	1.0	0.32	ug/l	
156-59-2	cis-1,2-Dichloroethylene	ND	1.0	0.28	ug/l	
156-60-5	trans-1,2-Dichloroethylene	ND	1.0	0.22	ug/l	
78-87-5	1,2-Dichloropropane	ND	1.0	0.43	ug/l	
10061-01-5	cis-1,3-Dichloropropene	ND	1.0	0.29	ug/l	
10061-02-6	trans-1,3-Dichloropropene	ND	1.0	0.21	ug/l	
100-41-4	Ethylbenzene	ND	1.0	0.36	ug/l	
76-13-1	Freon 113	ND	1.0	0.48	ug/l	
591-78-6	2-Hexanone	ND	10	2.0	ug/l	
98-82-8	Isopropylbenzene	ND	1.0	0.22	ug/l	
79-20-9	Methyl Acetate	ND	20	5.0	ug/l	

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Report of Analysis

Client Sample ID:	TRIP BLANK		
Lab Sample ID:	FA88903-17	**Date Sampled:**	09/10/21
Matrix:	AQ - Trip Blank Water	**Date Received:**	09/14/21
Method:	SW846 8260D	**Percent Solids:**	n/a
Project:	FPE; Edgefield, SC		

VOA TCL List (SOM02.0)

CAS No.	Compound	Result	RL	MDL	Units	Q
74-83-9	Methyl Bromide	ND	5.0	2.0	ug/l	
74-87-3	Methyl Chloride	ND	2.0	0.50	ug/l	
108-87-2	Methylcyclohexane	ND	1.0	0.44	ug/l	
75-09-2	Methylene Chloride	ND	5.0	2.0	ug/l	
108-10-1	4-Methyl-2-pentanone (MIBK)	ND	5.0	1.0	ug/l	
1634-04-4	Methyl Tert Butyl Ether	ND	1.0	0.23	ug/l	
100-42-5	Styrene	ND	1.0	0.22	ug/l	
79-34-5	1,1,2,2-Tetrachloroethane	ND	1.0	0.30	ug/l	
127-18-4	Tetrachloroethylene	ND	1.0	0.22	ug/l	
108-88-3	Toluene	ND	1.0	0.30	ug/l	
87-61-6	1,2,3-Trichlorobenzene	ND	2.0	0.61	ug/l	
120-82-1	1,2,4-Trichlorobenzene	ND	2.0	0.50	ug/l	
71-55-6	1,1,1-Trichloroethane	ND	1.0	0.25	ug/l	
79-00-5	1,1,2-Trichloroethane	ND	1.0	0.47	ug/l	
79-01-6	Trichloroethylene	ND	1.0	0.35	ug/l	
75-69-4	Trichlorofluoromethane [a]	ND	2.0	0.50	ug/l	
75-01-4	Vinyl Chloride	ND	1.0	0.41	ug/l	
	m,p-Xylene	ND	2.0	0.47	ug/l	
95-47-6	o-Xylene	ND	1.0	0.26	ug/l	

CAS No.	Surrogate Recoveries	Run# 1	Run# 2	Limits
1868-53-7	Dibromofluoromethane	93%		83-118%
17060-07-0	1,2-Dichloroethane-D4	97%		79-125%
2037-26-5	Toluene-D8	91%		85-112%
460-00-4	4-Bromofluorobenzene	93%		83-118%

(a) Associated CCV outside of control limits high.

ND = Not detected MDL = Method Detection Limit
RL = Reporting Limit
E = Indicates value exceeds calibration range
J = Indicates an estimated value
B = Indicates analyte found in associated method blank
N = Indicates presumptive evidence of a compound

Misc. Forms

Custody Documents and Other Forms

Includes the following where applicable:

- Chain of Custody

ARCADIS | ID#: | **CHAIN OF CUSTODY & LABORATORY ANALYSIS REQUEST FORM** | Page ___ of ___ | Lab Work Order #: FA88903

Send Results to:
Contact & Company Name: Jeff Beckner / ArcAdis
Telephone: 706-828-4421
Address: 1450 Greene St. Ste. 220
Fax:
City: Augusta State: GA Zip: 30901
E-mail Address:
Project Name/Location (City, State): EPE / Edgefield, SC
Project #:
Sampler's Printed Name: Reggie Rivard
Sampler's Signature: Reggie Rivard

Preservative	B							
Filtered (✓)								
# of Containers	3							
Container Information	1							

PARAMETER ANALYSIS & METHOD

Keys

Preservation Key:
A. H_2SO_4
B. HCL
C. HNO_3
D. NaOH
E. None
F. Other: _____
G. Other: _____
H. Other: _____

Container Information Key:
1. 40 ml Vial
2. 1 L Amber
3. 250 ml Plastic
4. 500 ml Plastic
5. Encore
6. 2 oz. Glass
7. 4 oz. Glass
8. 8 oz. Glass
9. Other: _____
10. Other: _____

Matrix Key:
SO - Soil | SE - Sediment | NL - NAPL/Oil
W - Water | SL - Sludge | SW - Sample Wipe
T - Tissue | A - Air | Other: _____

	Sample ID	Collection Date	Collection Time	Type (✓) Comp	Type (✓) Grab	Matrix	V8260 TCL-20	REMARKS
1	PSMW-6	9-7-21	1115		X	W	X	
2	PSMW-7	9-7-21	1410		X	W	X	
3	PSMW-2	9-7-21	1450		X	W	X	
4	PMW-2	9-8-21	0825		X	W	X	
5	PSMW-3	9-8-21	0910		X	W	X	
6	Dup-1	9-8-21	—		X	W	X	
7	PSMW-4	9-8-21	1055		X	W	X	
8	PMW-4	9-8-21	1235		X	W	X	
9	PMW-5	9-8-21	1450		X	W	X	
10	PMW-3	9-8-21	1625		X	W	X	
11	AMW-5	9-10-21	0810		X	W	X	
12	RTB-6	9-10-21	1005		X	W	X	
13	PSMW-5	9-10-21	1035		X	W	X	
14	AMW-1	9-10-21	1225		X	W	X	

INITIAL ASSESSMENT
LABEL VERIFICATION

Special Instructions/Comments:
0.8 ZN1

☐ Special QA/QC Instructions(✓):

Laboratory Information and Receipt		Relinquished By	Received By	Relinquished By	Laboratory Received By
Lab Name:	Cooler Custody Seal (✓)	Printed Name: Reggie Rivard	Printed Name: FX	Printed Name: FX	Printed Name: Peter Hess
Cooler packed with ice (✓)	☐ Intact ☐ Not Intact	Signature: Reggie Rivard	Signature:	Signature:	Signature:
Specify Turnaround Requirements:	Sample Receipt:	Firm: ARCADIS	Firm/Courier:	Firm/Courier:	Firm: SGS
Shipping Tracking #:	Condition/Cooler Temp: _____	Date/Time: 9-13-21 1400	Date/Time:	Date/Time:	Date/Time: 9/14/21 1000

20730826 CofC AR Form 08.27.2015 | **Distribution:** WHITE – Laboratory returns with results | YELLOW – Lab copy | PINK – Retained by Arcadis

FA88903: Chain of Custody
Page 1 of 3

ARCADIS

ID#:

CHAIN OF CUSTODY & LABORATORY ANALYSIS REQUEST FORM

Page ___ of ___

Lab Work Order #: FA88903

Send Results to:

Contact & Company Name: Jeff Beckner/ARCADIS | Telephone: 706-828-4421

Address: 1450 Greene St. Ste 220 | Fax:

City: Augusta | State: GA | Zip: 30901 | E-mail Address:

Project Name/Location (City, State): FPE/Edgefield, SC | Project #:

Sampler's Printed Name: Reggie Ricard | Sampler's Signature: Reggie Ricard

	Sample ID	Collection Date	Collection Time	Type (✓) Comp	Type (✓) Grab	Matrix	Preservative	Filtered (✓)	# of Containers	Container Information	PARAMETER ANALYSIS & METHOD: 8260 TCL 20
15	AMW-2	9-10-21	1305		X	W	B		3	1	X
16	AMW-3	9-10-21	1400		X	W					X
17	Trip Blank	9-10-21	—		1	W					X

Keys

Preservation Key:
A. H_2SO_4
B. HCL
C. HNO_3
D. NaOH
E. None
F. Other: _____
G. Other: _____
H. Other: _____

Container Information Key:
1. 40 ml Vial
2. 1 L Amber
3. 250 ml Plastic
4. 500 ml Plastic
5. Encore
6. 2 oz. Glass
7. 4 oz. Glass
8. 8 oz. Glass
9. Other: _____
10. Other: _____

Matrix Key:
SO - Soil | SE - Sediment | NL - NAPL/Oil
W - Water | SL - Sludge | SW - Sample Wipe
T - Tissue | A - Air | Other: _____

REMARKS

INITIAL ASSESSMENT

LABEL VERIFICATION

Special Instructions/Comments:

☐ Special QA/QC Instructions(✓):

Laboratory Information and Receipt		Relinquished By	Received By	Relinquished By	Laboratory Received By
Lab Name:	Cooler Custody Seal (✓)	Printed Name: Reggie Ricard	Printed Name: FX	Printed Name: FX	Printed Name: Peter H
☒ Cooler packed with ice (✓)	☐ Intact ☐ Not Intact	Signature: Reggie Ricard	Signature:	Signature:	Signature:
Specify Turnaround Requirements:	Sample Receipt:	Firm: ARCADIS	Firm/Courier:	Firm/Courier:	Firm: SGS
Shipping Tracking #:	Condition/Cooler Temp: _____	Date/Time: 9-10-21 / 1400	Date/Time:	Date/Time:	Date/Time: 9/10/21 1060

20730826 CofC AR Form 08.27.2015

Distribution: WHITE – Laboratory returns with results | YELLOW – Lab copy | PINK – Retained by Arcadis

FA88903: Chain of Custody
Page 2 of 3

SGS Sample Receipt Summary

Job Number: FA88903 **Client:** ARCADIS **Project:** FPE/EDGEFIELD

Date / Time Received: 9/14/2021 10:00:00 AM **Delivery Method:** FX **Airbill #'s:** 5061 4510 5417

Therm ID: IR 1; **Therm CF:** 0.2; **# of Coolers:** 1

Cooler Temps (Raw Measured) °C: Cooler 1: (0.6);

Cooler Temps (Corrected) °C: Cooler 1: (0.8);

Cooler Information	Y	or	N
1. Custody Seals Present	☑		☐
2. Custody Seals Intact	☑		☐
3. Temp criteria achieved	☑		☐
4. Cooler temp verification	IR Gun		
5. Cooler media	Ice (Bag)		

Trip Blank Information	Y	or	N	N/A
1. Trip Blank present / cooler	☑		☐	☐
2. Trip Blank listed on COC	☑		☐	☐

	W	or	S	N/A
3. Type Of TB Received	☑		☐	☐

Sample Information	Y	or	N	N/A
1. Sample labels present on bottles	☑		☐	
2. Samples preserved properly	☑		☐	
3. Sufficient volume/containers recvd for analysis:	☑		☐	
4. Condition of sample	Intact			
5. Sample recvd within HT	☑		☐	
6. Dates/Times/IDs on COC match Sample Label	☑		☐	
7. VOCs have headspace	☐		☑	☐
8. Bottles received for unspecified tests	☐		☑	
9. Compositing instructions clear	☐		☐	☑
10. Voa Soil Kits/Jars received past 48hrs?	☐		☐	☑
11. % Solids Jar received?	☐		☐	☑
12. Residual Chlorine Present?	☐		☐	☑

Misc. Information

Number of Encores: 25-Gram _____ 5-Gram _____ Number of 5035 Field Kits: _____ Number of Lab Filtered Metals: _____

Test Strip Lot #s: pH 0-3 230315 pH 10-12 219813A Other: (Specify) _____ _____

Residual Chlorine Test Strip Lot #: _____

Comments

SM001
Rev. Date 05/24/17

Technician: PETERH Date: 9/14/2021 10:00:00 A Reviewer: _____ Date: _____

FA88903: Chain of Custody
Page 3 of 3

Arcadis U.S., Inc.

1450 Greene Street

Suite 220

Augusta, Georgia 30901-5201

Tel 706 828 4421

Fax 706 828 4722

www.arcadis.com
